



Salt River Pima-Maricopa Indian Community

10005 East Osborn Road • Scottsdale, Arizona 85256

Phone (480) 362-7700 • Fax (480) 362-5597

MONTHLY PROJECT PROGRESS UPDATE

Project: ECEC Classroom and Parking Expansion

Issued Date: April 28, 2023 | **May-2023 UPDATE**

Distribution:

	Name	Department/ Company
X	Tami Brungard	ECEC – Edu Leader
X	Lekisha Morris	ECEC
X	Barbara White	ECEC
X	Melody Herne	Act. Superintendent
X	Tate Walker	Public Relations Dir.
X	Deanna Scabby	Edu. Board./ Council
X	Mikah Carlos	Community Council

	Name	Department/ Company
X	Kimberly Manuel	ECEC – Policy Council
X	Carmen Briones	ECEC – Policy Council
X	Jennifer Correa	ECEC – Policy Council
X	Brittany Barranca	ECEC – Policy Council
X	Frank Perez	ECEC – Policy Council
X	Rene Uriarte	ECEC – Policy Council
X	Symone Kann	ECEC – Policy Council
X	Felicia Toya	ECEC – Policy Council

Work Completed:

Items



1. Tie-in to existing 4" sanitary line, and concrete repair.
2. Concrete footing, grade beam, and elevator pit poured.
3. Electrical conduit site rough-In for site lighting.
4. Concrete curbs & gutters and parking final grading.
5. Under slab utility install, (sanitary & electric).
6. Storage CONEX cleared out ready for removal.

Work anticipated in the next month:

1. Final (2) exterior restroom renovations.
2. Site work continuing including concrete walks, drive and parking base material, fencing and light pole concrete base pour.
3. Masonry stem wall to start, delayed start from last month.
4. Elevator stem wall concrete pour.
5. Classroom renovations are pending material delivery, new heat pumps are currently 12 weeks out for delivery.

SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Project Schedule | Three Week Look Ahead

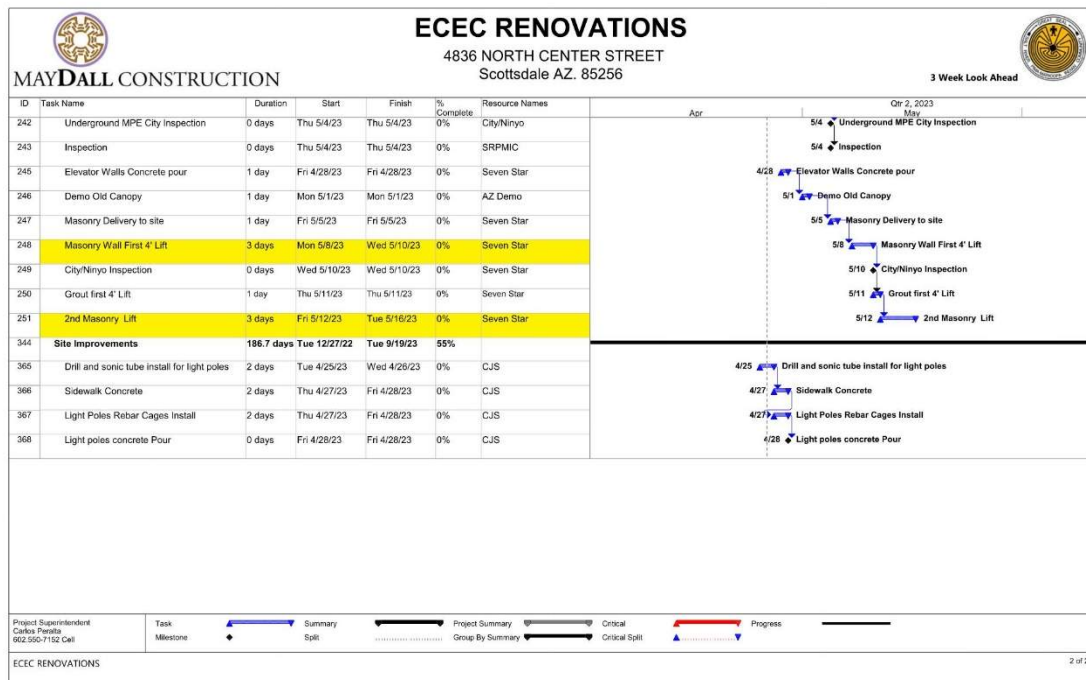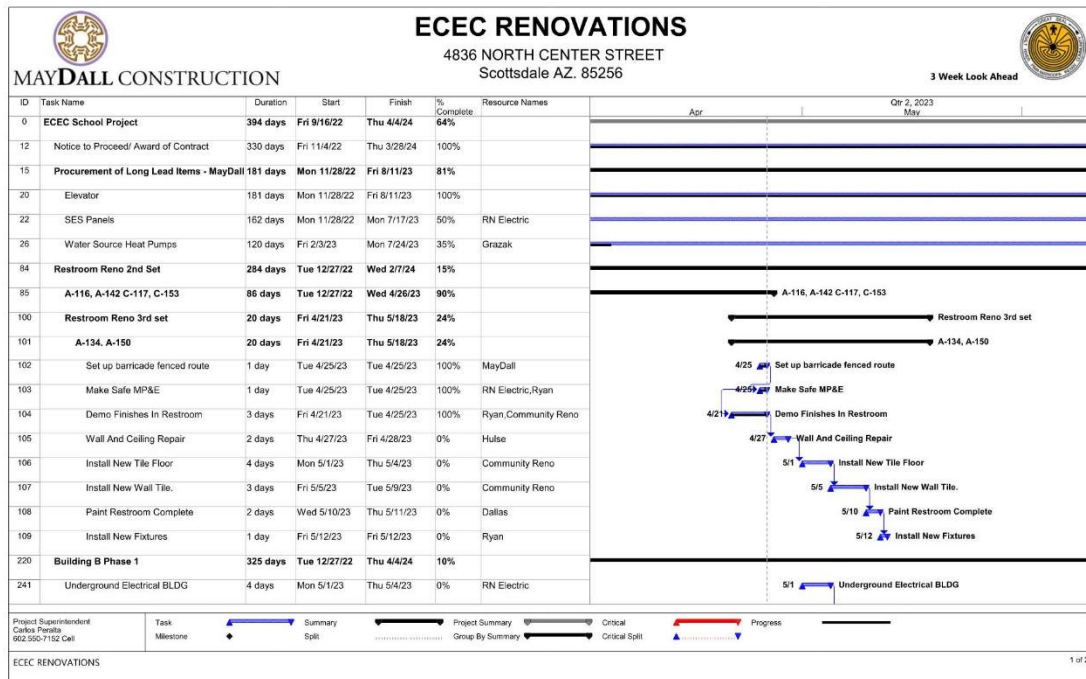

SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Progress Photos:

See attached



Description

4" line repairs complete at west side of bldg B

Taken Date

04/27/2023 at 01:39 pm

Uploaded By

Carlos Peralta

Upload Date

04/27/2023 at 01:39 pm

File Name

[EC4240F2-6160-4112-86CF-3CF9...](#)



Description

Sidewalk form and ready for pour Thursday Morning

Taken Date

04/27/2023 at 07:34 am

Uploaded By


Carlos Peralta

Upload Date

04/27/2023 at 07:59 am

File Name

[D2AC0E4B-F751-4CBB-8BDB-BB6...](#)

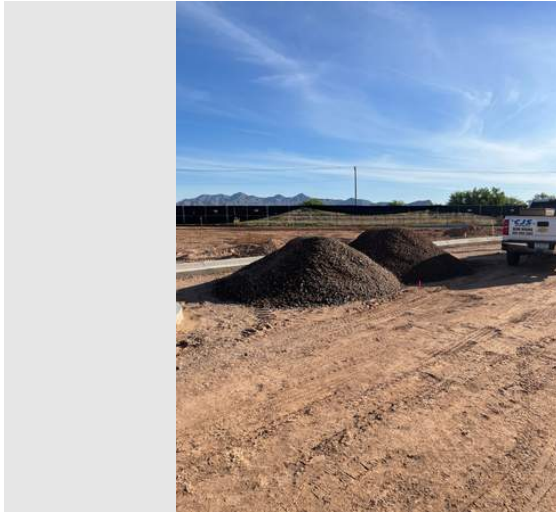

Description

Parking AB on site

Taken Date

04/27/2023 at 07:34 am

Uploaded By

Carlos Peralta

Upload Date

04/27/2023 at 07:59 am

File Name

[AC34F555-E1F3-4BE5-8B2F-086A...](#)



Description

Light pole drilling in progress

Taken Date

04/26/2023 at 12:07 pm

Uploaded By

Carlos Peralta

Upload Date

04/26/2023 at 12:53 pm

File Name

[B2CA67F4-8A23-4890-9A41-EEA...](#)



Description

Light pole cages assemble and light pole anchor bolts on site

Taken Date

04/26/2023 at 12:06 pm

Uploaded By

Carlos Peralta

Upload Date

04/26/2023 at 12:52 pm

File Name

59585AB7-8E86-4AEA-BE72-549E...



Description

Sidewalk from new parking lot to school side on the south east

Taken Date

04/26/2023 at 08:15 am

Uploaded By

Carlos Peralta

Upload Date

04/26/2023 at 11:18 am

File Name

8F23D563-B36E-4650-AED2-07C...



Description

Vapor Barrier on site for Slab.

Taken Date

04/26/2023 at 12:06 pm

Uploaded By

Carlos Peralta

Upload Date

04/26/2023 at 12:52 pm

File Name

F55014E5-6D45-4116-8DE0-E80E...



Description

Taken Date

04/26/2023 at 08:15 am

Uploaded By

Carlos Peralta

Upload Date

04/26/2023 at 08:50 am

File Name

73C6FFE1-AD29-4B82-BABB-E4E...



Description

Taken Date

04/25/2023 at 12:50 pm

Uploaded By

Carlos Peralta

Upload Date

04/25/2023 at 02:44 pm

File Name

[2AB68F89-4F94-4E85-B4F0-64B9...](#)



Description

Taken Date

04/25/2023 at 12:50 pm

Uploaded By

Carlos Peralta

Upload Date

04/25/2023 at 04:17 pm

File Name

[BE68AAC4-90BD-4B2E-B7F5-F60...](#)



Description

Scupper framed out and covers install and inspected on side walk

Taken Date

04/25/2023 at 12:50 pm

Uploaded By

Carlos Peralta

Upload Date

04/26/2023 at 11:09 am

File Name

[F143EEA0-51CE-4AAA-8707-1C0...](#)



Description

Side walk scuppers install in progress

Taken Date

04/25/2023 at 11:09 am

Uploaded By


Carlos Peralta

Upload Date

04/25/2023 at 11:10 am

File Name

[44874708-20BE-4360-8E07-EFB0...](#)

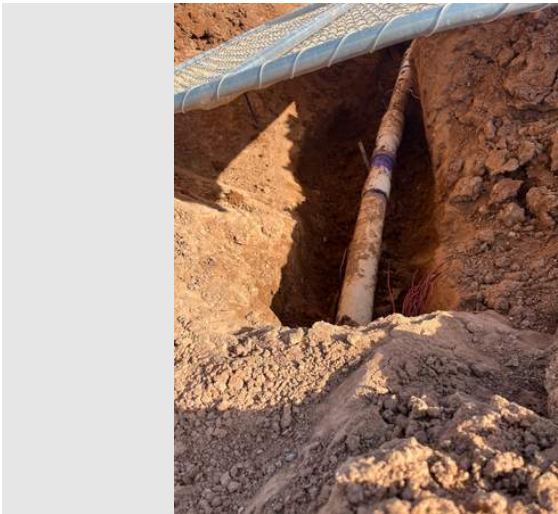

Description

Taken Date

04/25/2023 at 07:55 am

Uploaded By

Carlos Peralta

Upload Date

04/25/2023 at 07:55 am

File Name

88F7E666-B30E-4215-B1F7-D9E6...



Description

Dug down for scuppers area under sidewalk

Taken Date

04/24/2023 at 01:15 pm

Uploaded By

Carlos Peralta

Upload Date

04/24/2023 at 01:23 pm

File Name

E2967BCE-C0D1-4EBB-89C5-422...



Description

Handicap Ramp Ready for compaction testing Weds.

Taken Date

04/24/2023 at 01:15 pm

Uploaded By

Carlos Peralta

Upload Date

04/24/2023 at 01:25 pm

File Name

9CC23B9E-1B59-4EA9-9F2C-EAB...



Description

4" Water line getting fix by Ronning due to the last repair was licking

Taken Date

04/24/2023 at 01:13 pm

Uploaded By

Carlos Peralta

Upload Date

04/24/2023 at 01:14 pm

File Name

AE7DF06A-392B-4BBB-B8F0-028...



Description

Door frames on site bldg. B

Taken Date

04/21/2023 at 12:39 pm

Uploaded By

Carlos Peralta

Upload Date

04/23/2023 at 08:29 pm

File Name

66E9B5A3-B995-483C-9E99-7565...



Description

Concrete ban at handicap parking area Monday they start on side walk

Taken Date

04/21/2023 at 07:32 am

Uploaded By

Carlos Peralta

Upload Date

04/21/2023 at 07:43 am

File Name

2EFA294C-C195-49CD-8931-9C6...



Description

Curb and Gutter at east side form and pour

Taken Date

04/21/2023 at 07:32 am

Uploaded By

Carlos Peralta

Upload Date

04/21/2023 at 07:41 am

File Name

373D4FD4-37C6-4F6B-BB81-7A0...



Description

Elevator pit form and ready for concrete pour

Taken Date

04/20/2023 at 01:11 pm

Uploaded By

Carlos Peralta

Upload Date

04/20/2023 at 06:13 pm

File Name

D7981A77-13DA-4944-9C62-E58...



Description

RN electrical sleeves

Taken Date

04/20/2023 at 01:10 pm

Uploaded By

Carlos Peralta

Upload Date

04/20/2023 at 01:42 pm

File Name

[7AF59024-B906-4935-A014-1784...](#)



Description

underground plumbing backfill completed

Taken Date

04/18/2023 at 11:38 am

Uploaded By

Carlos Peralta

Upload Date

04/18/2023 at 11:38 am

File Name

[B1B720A3-FFA5-47ED-ACD6-C4B...](#)



Description

Stem wall Block on site

Taken Date

04/20/2023 at 01:09 pm

Uploaded By

Carlos Peralta

Upload Date

04/20/2023 at 01:26 pm

File Name

[C21C0209-F808-4A57-928D-36B...](#)



Description

Plumbing backfill in progress should be completed today

Taken Date

04/18/2023 at 11:38 am

Uploaded By


Carlos Peralta

Upload Date

04/18/2023 at 11:38 am

File Name

[13917F74-8440-48A8-B4B4-0044...](#)

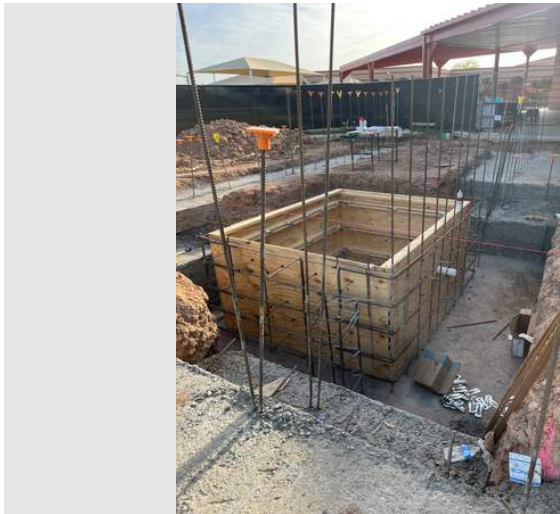

Description

Elevator pit forms complete inspection schedule for weds.

Taken Date

04/18/2023 at 07:39 am

Uploaded By

Carlos Peralta

Upload Date

04/18/2023 at 11:37 am

File Name

018E264B-016E-4831-B24C-F795...



Description

Light poles electrical west side

Taken Date

04/14/2023 at 07:09 am

Uploaded By

Saen Framjee

Upload Date

04/14/2023 at 11:01 am

File Name

184EEADC-A97B-4B95-86FC-997...



Description

CJS Cleaning footings and drilling for vertical bars due to the Halipears on the way of lay out Epoxy is schedule for weds. morning

Taken Date

04/18/2023 at 07:38 am

Uploaded By

Carlos Peralta

Upload Date

04/18/2023 at 11:38 am

File Name

3EE8ED9F-A968-427E-B974-013F...



Description

Site Electrical Lighting Conduit

Taken Date

04/14/2023 at 07:08 am

Uploaded By

Saen Framjee

Upload Date

04/14/2023 at 07:09 am

File Name

41D48A1D-AD99-47A6-AF28-973...



Description

Additional Curb and Gutter poured.

Taken Date

04/14/2023 at 07:07 am

Uploaded By

Saen Framjee

Upload Date

04/14/2023 at 07:07 am

File Name

0240A476-F5A6-47E0-AD35-8CE...



Description

Curb and Gutter recently poured

Taken Date

04/14/2023 at 07:06 am

Uploaded By

Saen Framjee

Upload Date

04/14/2023 at 07:07 am

File Name

BB2E0BA6-D17C-4EF1-A395-9EF...



Description

Curbing being formed for Pour

Taken Date

04/14/2023 at 07:07 am

Uploaded By

Saen Framjee

Upload Date

04/14/2023 at 07:07 am

File Name

0CD7D8F0-D654-429F-ACA2-E4C...



Description

Curb and gutter

Taken Date

04/14/2023 at 07:06 am

Uploaded By

Saen Framjee

Upload Date

04/14/2023 at 07:07 am

File Name

5B00173A-5609-46D4-AE4C-F00...



Description

Curb and Gutter

Taken Date

04/14/2023 at 07:06 am

Uploaded By

Saen Framjee

Upload Date

04/14/2023 at 07:07 am

File Name

[2ADE0A25-EFB5-4239-8C49-EED...](#)



Description

installing rebar for South Footer

Taken Date

04/12/2023 at 11:42 am

Uploaded By


Carlos Peralta

Upload Date

04/12/2023 at 04:42 pm

File Name

[95F7ECDD-D36C-4FEC-A6FE-42C...](#)

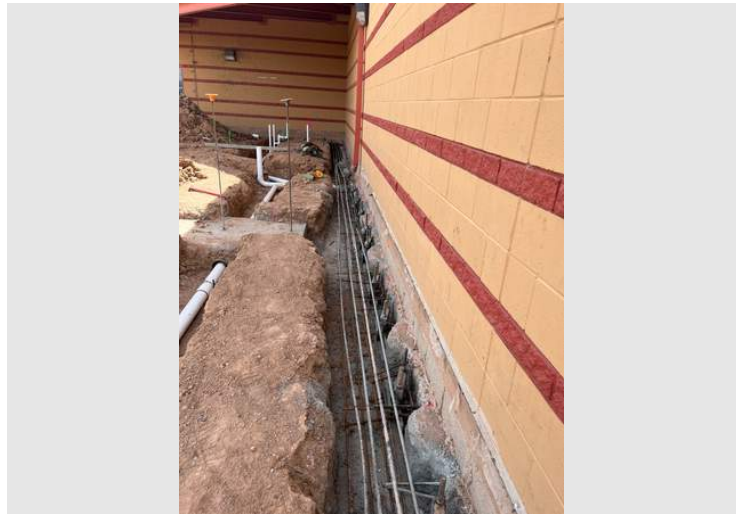

Description

Rebar installed for final footer pour

Taken Date

04/12/2023 at 11:43 am

Uploaded By

Carlos Peralta

Upload Date

04/12/2023 at 11:43 am

File Name

[C705425F-9236-4D80-A4BC-706...](#)



Description

Trenching in progress for underground electric

Taken Date

04/11/2023 at 01:19 pm

Uploaded By

Carlos Peralta

Upload Date

04/11/2023 at 02:06 pm

File Name

[94A6201E-3650-40B3-B2C2-590B...](#)



Description

Site Mascot

Taken Date

04/11/2023 at 11:57 am

Uploaded By

Carlos Peralta

Upload Date

04/11/2023 at 02:05 pm

File Name

072F0990-BE38-473B-BD3B-AF71...



Description

Vertical Curb forming in progress

Taken Date

04/11/2023 at 08:29 am

Uploaded By

Carlos Peralta

Upload Date

04/11/2023 at 08:39 am

File Name

7973F507-6008-4B56-AC5F-87CF...



Description

Trenching for underground electric for light poles

Taken Date

04/11/2023 at 08:29 am

Uploaded By


Carlos Peralta

Upload Date

04/11/2023 at 08:41 am

File Name

F7E7AFB8-31AA-423A-9124-33C...

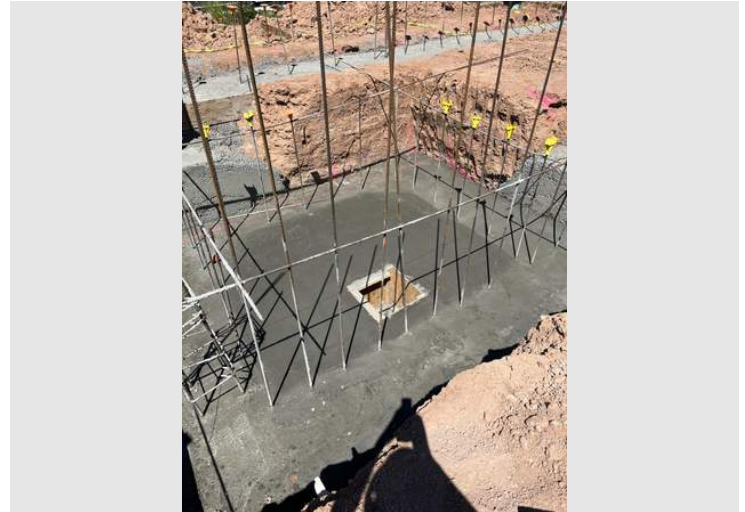

Description

Elevator pit pour complete

Taken Date

04/10/2023 at 01:45 pm

Uploaded By

Carlos Peralta

Upload Date

04/10/2023 at 01:49 pm

File Name

1526B3F7-410C-444F-8E03-5AB8...



Description

Sewer line thru foundation to tie in on storage room side

Taken Date

04/10/2023 at 01:44 pm

Uploaded By

Carlos Peralta

Upload Date

04/10/2023 at 01:45 pm

File Name

F2A107B3-7CD3-49F1-9BDC-62A...



Description

Curb and gutter on the East. side

Taken Date

04/10/2023 at 08:50 am

Uploaded By

Carlos Peralta

Upload Date

04/10/2023 at 08:52 am

File Name

F848614A-78BF-43CD-98AB-AE8...



Description

Underground plumbing install in progress

Taken Date

04/10/2023 at 01:44 pm

Uploaded By

Carlos Peralta

Upload Date

04/10/2023 at 01:47 pm

File Name

7BDE5EB8-169F-4AC1-B12A-0D6...



Description

Sewer line backfill in progress at storage room

Taken Date

04/10/2023 at 07:01 am

Uploaded By

Carlos Peralta

Upload Date

04/10/2023 at 07:28 am

File Name

495913F6-28A3-4A2D-A2AB-936...



Description

Arial above Building B addition of concrete pour for footers

Taken Date

04/07/2023 at 10:47 am

Uploaded By

Saen Framjee

Upload Date

04/07/2023 at 11:03 am

File Name

44DDA57F-D69E-4B2A-94E6-345...



Description

Building B Footing Pour

Taken Date

04/07/2023 at 10:45 am

Uploaded By

Saen Framjee

Upload Date

04/07/2023 at 11:03 am

File Name

BF76D865-8EA4-430C-B129-8D5...



Description

Arial from the North of the project showing the curb and gutter that was poured this week

Taken Date

04/07/2023 at 10:46 am

Uploaded By

Saen Framjee

Upload Date

04/07/2023 at 11:03 am

File Name

0144C025-2683-4C3A-B81E-B268...



Description

South Wall Building B Footer

Taken Date

04/07/2023 at 10:24 am

Uploaded By

Carlos Peralta

Upload Date

04/07/2023 at 10:24 am

File Name

013731A6-AC5F-4D56-95EA-CCE...



Description

Taken Date

04/07/2023 at 10:09 am

Uploaded By

Carlos Peralta

Upload Date

04/07/2023 at 10:09 am

File Name

[2714EEFD-22C9-4AB6-9F4C-66B...](#)



Description

Taken Date

04/07/2023 at 10:00 am

Uploaded By

Carlos Peralta

Upload Date

04/07/2023 at 10:09 am

File Name

[F3AA5493-8AB8-428A-A1B7-B51...](#)



Description

Taken Date

04/07/2023 at 10:01 am

Uploaded By

Carlos Peralta

Upload Date

04/07/2023 at 10:02 am

File Name

[66110ABB-89A0-4C99-B951-155...](#)



Description

Taken Date

04/07/2023 at 09:59 am

Uploaded By

Carlos Peralta

Upload Date

04/07/2023 at 10:01 am

File Name

[4E94566D-F98A-40AB-AC32-41C...](#)



Description

Taken Date

04/07/2023 at 09:59 am

Uploaded By

Carlos Peralta

Upload Date

04/07/2023 at 10:01 am

File Name

0662C0B5-9AEB-4B89-853F-1FD...



Description

Taken Date

04/07/2023 at 07:05 am

Uploaded By


Carlos Peralta

Upload Date

04/07/2023 at 07:06 am

File Name

70D2BD4B-B9F9-49BE-A57A-6F3...

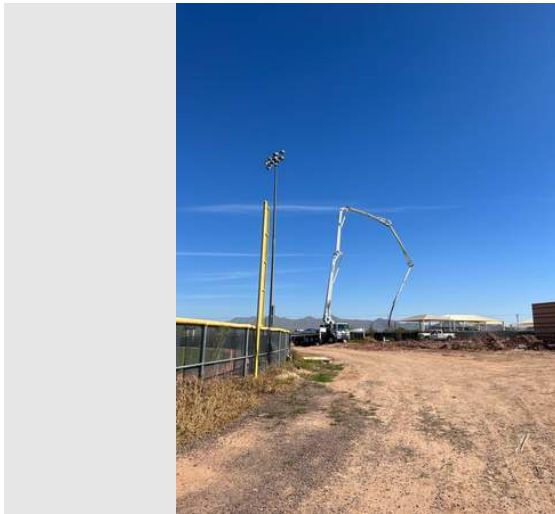

Description

Taken Date

04/07/2023 at 09:28 am

Uploaded By

Carlos Peralta

Upload Date

04/07/2023 at 09:28 am

File Name

D9EFF30A-ABE9-4630-A01C-F394...



Description

Taken Date

04/06/2023 at 12:35 pm

Uploaded By

Carlos Peralta

Upload Date

04/07/2023 at 06:25 am

File Name

7F8A6A7A-13DE-491C-9C01-B83...



Description

Taken Date

04/06/2023 at 12:35 pm

Uploaded By

Carlos Peralta

Upload Date

04/07/2023 at 06:25 am

File Name

[97CABE4F-BB4D-4326-BF0D-953...](#)



Description

Taken Date

04/05/2023 at 12:14 pm

Uploaded By

Carlos Peralta

Upload Date

04/07/2023 at 06:24 am

File Name

[A43DC9A0-404C-4ABA-A5B7-202...](#)



Description

Taken Date

04/06/2023 at 12:34 pm

Uploaded By

Carlos Peralta

Upload Date

04/07/2023 at 06:25 am

File Name

[BE58CCD4-4E85-414E-A5D5-B68...](#)



Description

Taken Date

04/05/2023 at 07:16 am

Uploaded By


Carlos Peralta

Upload Date

04/05/2023 at 07:25 am

File Name

[68EFCA81-EC15-4DF4-9F09-EDD...](#)

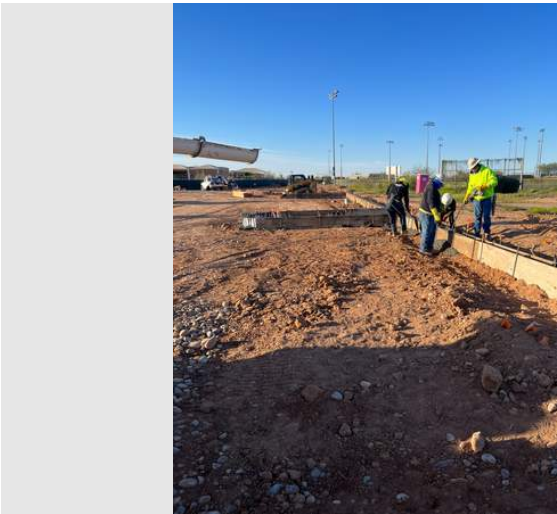

Description

Taken Date

04/05/2023 at 07:15 am

Uploaded By

Carlos Peralta

Upload Date

04/05/2023 at 07:16 am

File Name

[CFC3B2CD-8284-4F4F-ACAD-D37...](#)



Description

Taken Date

04/04/2023 at 02:41 pm

Uploaded By

Carlos Peralta

Upload Date

04/04/2023 at 02:52 pm

File Name

[3B29F3D9-783F-4F58-8C98-AC12...](#)



Description

Taken Date

04/04/2023 at 02:41 pm

Uploaded By

Carlos Peralta

Upload Date

04/04/2023 at 02:43 pm

File Name

[CBDBD044-6982-4D76-A567-430...](#)



Description

Taken Date

04/04/2023 at 02:40 pm

Uploaded By


Carlos Peralta

Upload Date

04/04/2023 at 02:52 pm

File Name

[07D3586E-7258-414F-94B8-3E1...](#)

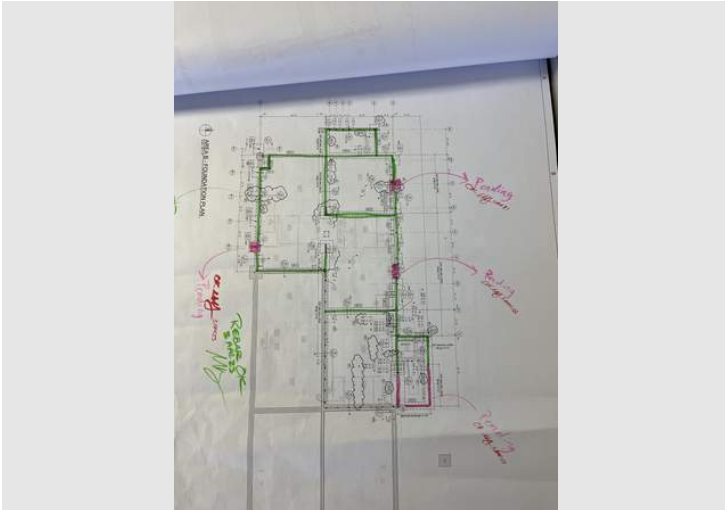

Description

Taken Date

04/03/2023 at 12:18 pm

Uploaded By

Carlos Peralta

Upload Date

04/03/2023 at 12:22 pm

File Name

FC618E32-6637-4D82-94FC-988...



Description

Taken Date

04/03/2023 at 09:11 am

Uploaded By


Carlos Peralta

Upload Date

04/03/2023 at 09:22 am

File Name

615BBFBC-C252-42A3-B38E-EE0...

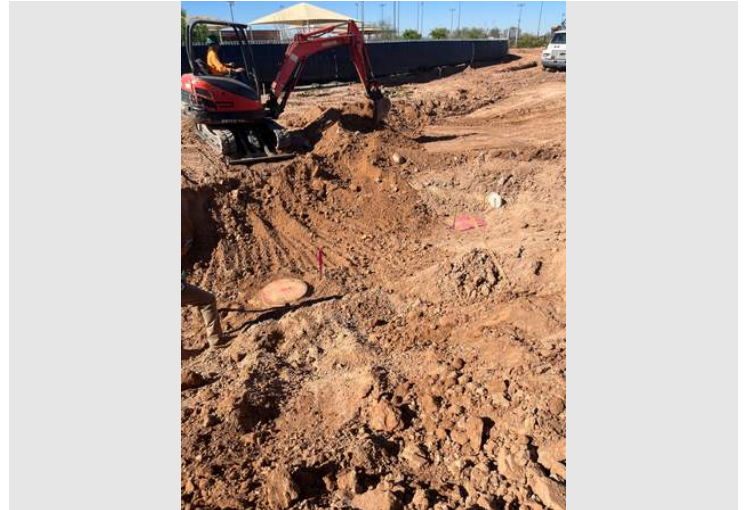

Description

Taken Date

04/03/2023 at 09:12 am

Uploaded By

Carlos Peralta

Upload Date

04/03/2023 at 09:22 am

File Name

CA7899E7-AC61-4F3E-8D1D-B61...



Description

Taken Date

04/03/2023 at 08:14 am

Uploaded By

Carlos Peralta

Upload Date

04/03/2023 at 08:15 am

File Name

21E3CB7C-6CE4-41FD-9D9A-172...



Description

Taken Date
04/01/2023 at 12:03 pm

Uploaded By
Carlos Peralta

Upload Date
04/01/2023 at 12:05 pm

File Name
[9C21816D-C01D-4DE9-B0C0-AC6...](#)



Description

Taken Date
04/01/2023 at 12:02 pm

Uploaded By
Carlos Peralta

Upload Date
04/01/2023 at 12:07 pm

File Name
[9B2807BA-25C2-43B1-B4D5-6B2...](#)



Description

Taken Date
04/01/2023 at 12:02 pm

Uploaded By
Carlos Peralta

Upload Date
04/01/2023 at 12:14 pm

File Name
[435DFD0A-4D53-479D-9E0E-98A...](#)



Description

Closet protection from dust from saw cutting in place

Taken Date
04/01/2023 at 10:22 am

Uploaded By
Carlos Peralta

Upload Date
04/01/2023 at 10:31 am

File Name
[124605FD-AA62-422A-89E7-FD3...](#)



Description

Sewer line expose and slab is 4" thick

Taken Date

04/01/2023 at 10:22 am

Uploaded By

Carlos Peralta

Upload Date

04/01/2023 at 10:31 am

File Name

[6D97D199-629B-48B4-9933-6D7...](#)



Description

Just like the locator said top of pipe at 2' 8"

Taken Date

04/01/2023 at 10:21 am

Uploaded By

Carlos Peralta

Upload Date

04/01/2023 at 10:31 am

File Name

[DA3EA68E-6568-4CEA-8309-F68...](#)

SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Attachments:

Item/s
1. None
