



Salt River Pima-Maricopa Indian Community

10005 East Osborn Road • Scottsdale, Arizona 85256

Phone (480) 362-7700 • Fax (480) 362-5597

MONTHLY PROJECT PROGRESS UPDATE

Project: ECEC Classroom and Parking Expansion

Issued Date: August 4, 2023 | **August-2023 UPDATE**

Distribution:

	Name	Department/ Company
X	Tami Brungard	ECEC – Edu Leader
X	Lekisha Morris	ECEC
X	Barbara White	ECEC
X	Melody Herne	Act. Superintendent
X	Tate Walker	Public Relations Dir.
X	Deanna Scabby	Edu. Board./ Council
X	Mikah Carlos	Community Council
X	Pamela Prasher	ECEC

	Name	Department/ Company
X	Kimberly Manuel	ECEC – Policy Council
X	Carmen Briones	ECEC – Policy Council
X	Jennifer Correa	ECEC – Policy Council
X	Brittany Barranca	ECEC – Policy Council
X	Frank Perez	ECEC – Policy Council
X	Rene Uriarte	ECEC – Policy Council
X	Symone Kann	ECEC – Policy Council
X	Felicia Toya	ECEC – Policy Council

Work Completed:

Items



1. Group #1 Classroom renovation started (A-146, A-147, B-149, B-157), tentative completion 8/31/23.
2. Building B Addition CMU vertical walls above 2nd floor level. 2nd Floor steel beams installed.
3. Central Plant mechanical yard slab and housekeeping pads poured.
4. New parking irrigation lines installed.

Work anticipated in the next month:

1. Group #2 Classroom renovation start (A-154, A-139, B-135, C-102).
2. Building B Addition 1st floor room decking, 2nd floor steel decking and concrete pour.
3. Building B CMU wall completion, 2nd floor roof decking and roofing.
4. Infant playground demolition start and new work continuing.
5. Door Access Control install to start.

SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Project Schedule | Three Week Look Ahead

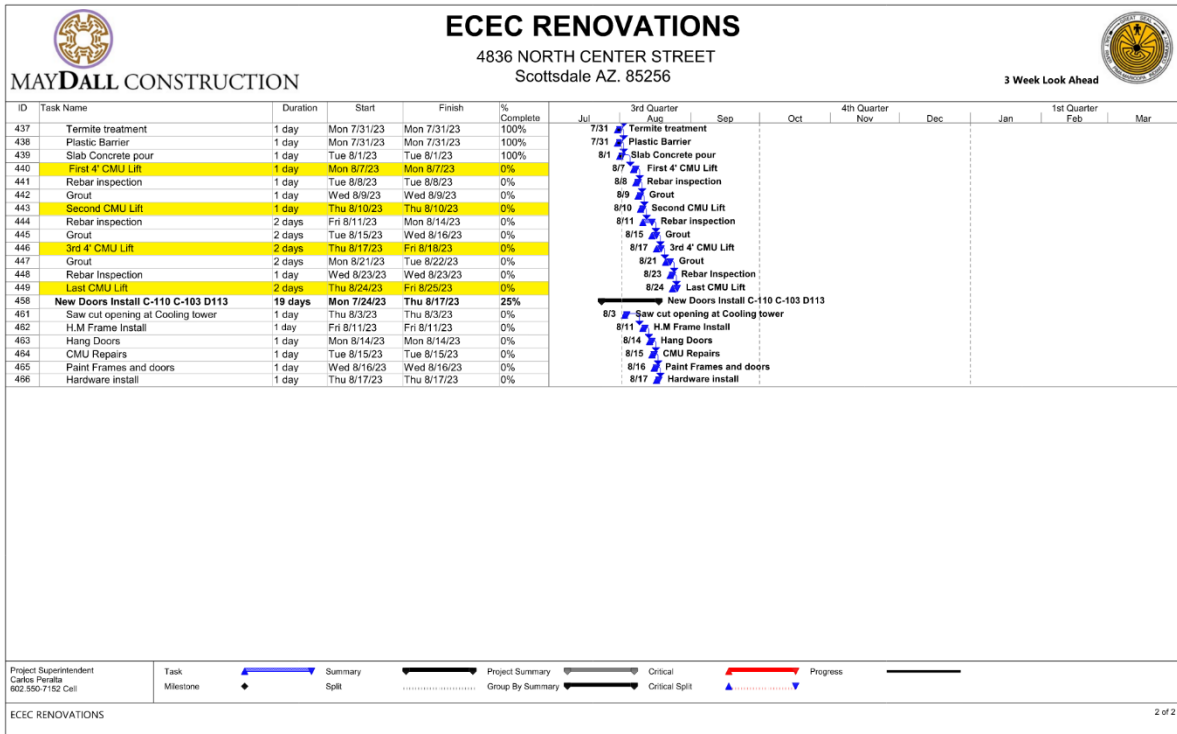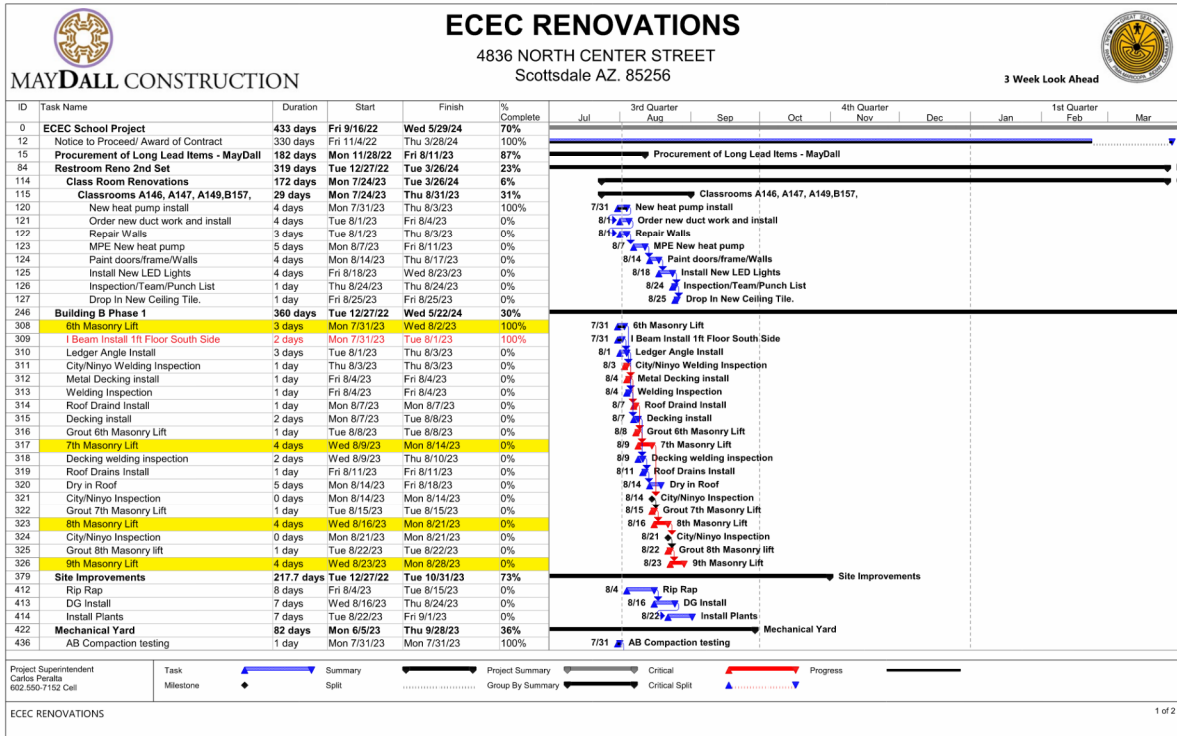

SRP-MIC MONTHLY PROJECT PROGRESS UPDATE


Progress Photos:

See attached.

SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Attachments:

Item/s
1. None

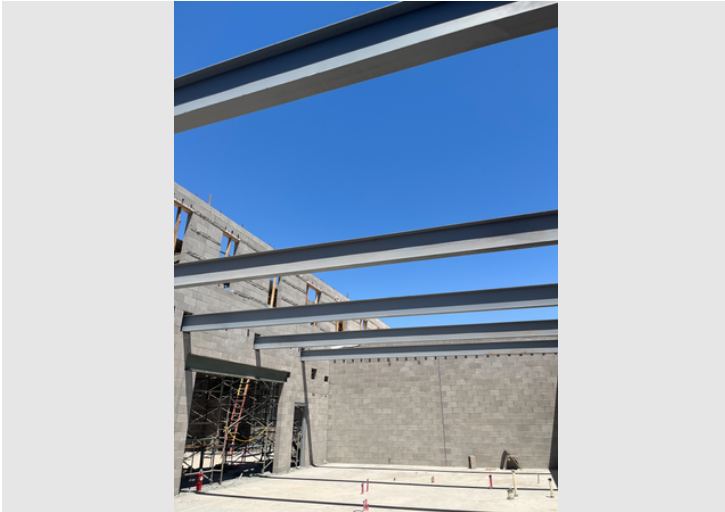

Description

I beams install in progress at first floor level.

Taken Date

07/31/2023 at 01:42 pm

Uploaded By

Carlos Peralta

Upload Date

07/31/2023 at 01:43 pm

File Name

[72C3BFB5-E23C-4C7E-880D-519...](#)



Description

New duct work order for new heat pump.

Taken Date

07/31/2023 at 09:08 am

Uploaded By

Carlos Peralta

Upload Date

07/31/2023 at 10:19 am

File Name

[AF962C1B-AFBD-472E-814A-FEA...](#)



Description

North view of new bldg.

Taken Date

07/31/2023 at 01:42 pm

Uploaded By

Carlos Peralta

Upload Date

07/31/2023 at 01:43 pm

File Name

[1B2CEF20-29CA-479F-A361-1825...](#)



Description

Old hose and valves to be replace with new.

Taken Date

07/31/2023 at 09:08 am

Uploaded By

Carlos Peralta

Upload Date

07/31/2023 at 09:08 am

File Name

[354D935B-2D00-4834-8BE5-055...](#)



Description

New heat pump install in progress at 146 Classroom.

Taken Date

07/31/2023 at 09:08 am

Uploaded By


Carlos Peralta

Upload Date

07/31/2023 at 09:08 am

File Name

98E6DED1-501C-468F-9E87-4CE...

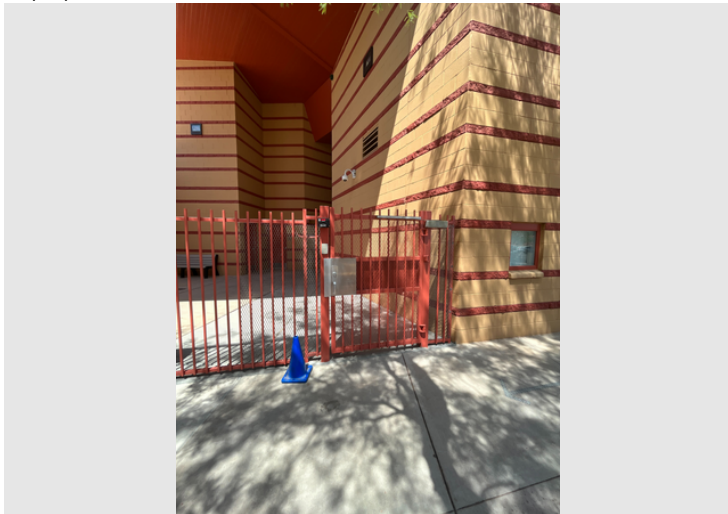

Description

Taken Date

07/28/2023 at 02:04 pm

Uploaded By

Carlos Peralta

Upload Date

07/28/2023 at 02:04 pm

File Name

4BEB3969-267F-4CB5-9037-6E7E...



Description

Compaction in progress Mechanical room.

Taken Date

07/31/2023 at 06:04 am

Uploaded By

Carlos Peralta

Upload Date

07/31/2023 at 06:04 am

File Name

2B6C54DF-17B5-41C6-8B49-173...



Description

Security fence on east gate install complete at mail entrance of ECEC School.

Taken Date

07/28/2023 at 02:04 pm

Uploaded By

Carlos Peralta

Upload Date

07/28/2023 at 02:04 pm

File Name

A38FC869-CC7A-48C7-8DCF-469...



Description

Underground electrical for bldg. B

Taken Date

07/28/2023 at 12:23 pm

Uploaded By

Carlos Peralta

Upload Date

07/28/2023 at 12:26 pm

File Name

[0892574C-EBB3-4218-B3A4-044...](#)



Description

Mechanical house pads.

Taken Date

07/28/2023 at 11:44 am

Uploaded By

Carlos Peralta

Upload Date

07/28/2023 at 11:44 am

File Name

[5C42144E-F718-4B0F-931B-BD1F...](#)



Description

Underground electric for bldg. B

Taken Date

07/28/2023 at 12:23 pm

Uploaded By

Carlos Peralta

Upload Date

07/28/2023 at 12:29 pm

File Name

[EAAAC9E8-683D-4352-A14C-E66...](#)



Description

Mechanical yard house keeping pads

Taken Date

07/28/2023 at 10:38 am

Uploaded By

Carlos Peralta

Upload Date

07/28/2023 at 10:38 am

File Name

[70E53978-DBFB-4C31-8645-8D9...](#)



Description

Mechanical yard house keeping pads

Taken Date

07/28/2023 at 10:38 am

Uploaded By

Carlos Peralta

Upload Date

07/28/2023 at 10:38 am

File Name

BF7E64F6-0639-4946-A44E-BAE9...



Description

Plastic over exciting roof line that we had to cut for new bldg

Taken Date

07/28/2023 at 09:30 am

Uploaded By

Carlos Peralta

Upload Date

07/28/2023 at 09:31 am

File Name

5AEDCCAF-ADDD-462A-971E-B32...



Description

Mechanical yard house keeping pads

Taken Date

07/28/2023 at 10:37 am

Uploaded By

Carlos Peralta

Upload Date

07/28/2023 at 10:37 am

File Name

15D0DF52-050A-4098-B9A8-4A2...



Description

Plastic over exciting roof line that we had to cut for new bldg

Taken Date

07/28/2023 at 09:30 am

Uploaded By


Carlos Peralta

Upload Date


07/28/2023 at 09:30 am

File Name

49B402EB-6704-4381-9137-1D2...

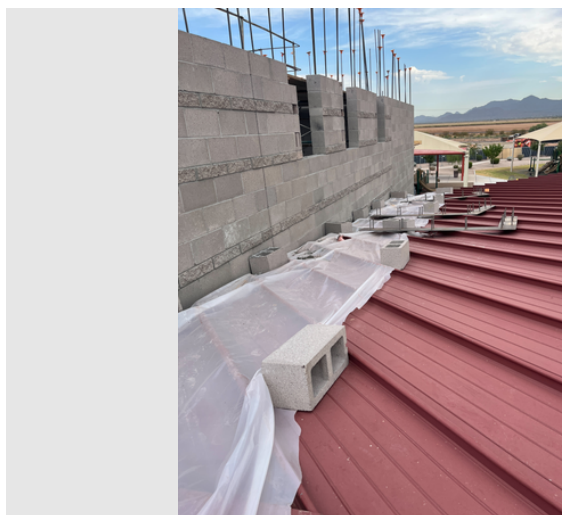

Description

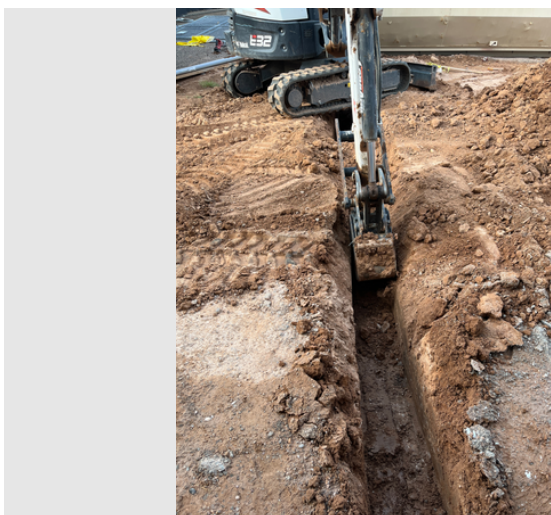

Description

Taken Date

07/28/2023 at 09:29 am

Uploaded By


Carlos Peralta

Upload Date

07/28/2023 at 09:30 am

File Name

[D1EA43E9-14E7-46E0-9060-B921...](#)

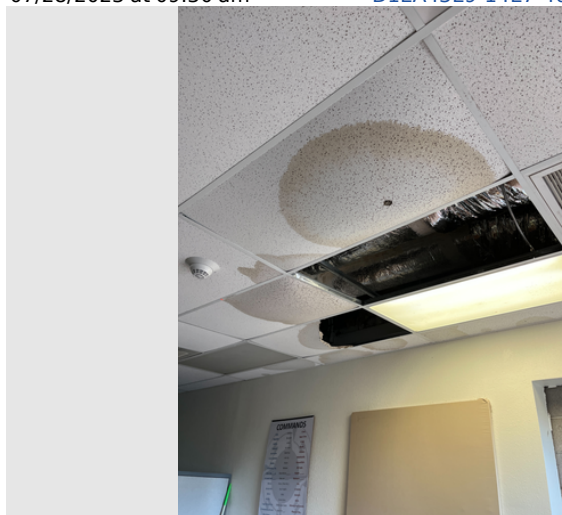

Description

Taken Date

07/28/2023 at 07:14 am

Uploaded By

Carlos Peralta

Upload Date

07/28/2023 at 07:15 am

File Name

[CC70A1A8-D589-41B5-ADCC-0E1...](#)



Description

Asphalt damage by steel delivery 7-26-23 2:30 PM

Taken Date

07/27/2023 at 08:57 am

Uploaded By

Carlos Peralta

Upload Date

07/27/2023 at 08:57 am

File Name

[F360739F-7E44-440F-B049-1326...](#)

Taken Date

07/26/2023 at 01:36 pm

Uploaded By


Carlos Peralta

Upload Date

07/26/2023 at 01:57 pm

File Name

[D16F59C3-BABE-47B9-ABF2-ABC...](#)

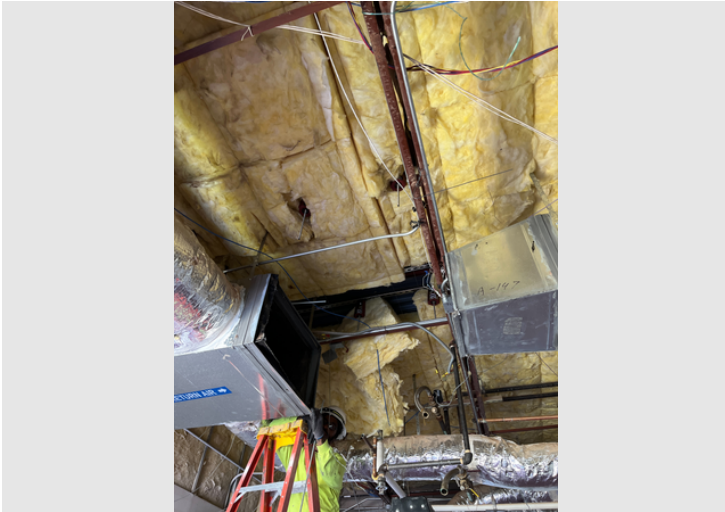

Description

Old heat pump demo complete.

Taken Date

07/26/2023 at 11:04 am

Uploaded By

Carlos Peralta

Upload Date

07/26/2023 at 11:05 am

File Name

[87744099-D176-4C96-9DC0-4C5...](#)



Description

Elevator Shaft from second floor.

Taken Date

07/26/2023 at 08:02 am

Uploaded By

Carlos Peralta

Upload Date

07/26/2023 at 08:03 am

File Name

[FFE9803A-4C40-4B13-BD18-5550...](#)



Description

Ready for core drill tours panels.

Taken Date

07/26/2023 at 08:27 am

Uploaded By


Carlos Peralta

Upload Date

07/26/2023 at 08:49 am

File Name

[20E2A4A1-6BD8-4627-854A-26E...](#)

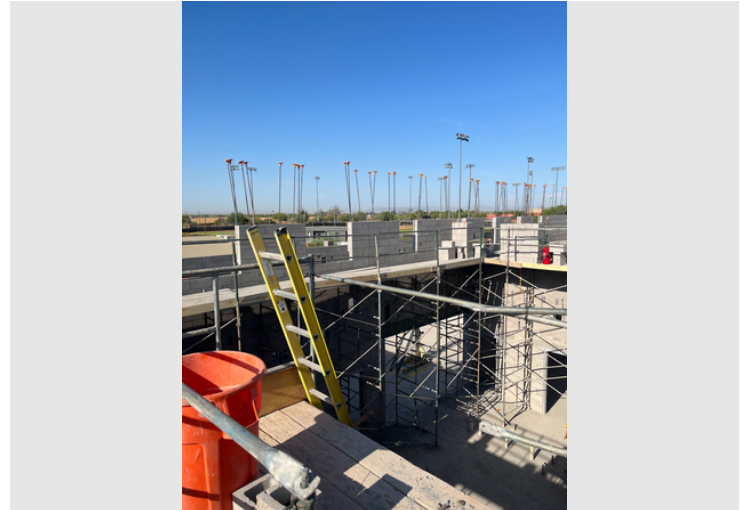

Description

Second floor windows west view

Taken Date

07/26/2023 at 08:02 am

Uploaded By


Carlos Peralta

Upload Date

07/26/2023 at 08:03 am

File Name

[96D69909-CBF2-4BDE-BE46-C2B...](#)

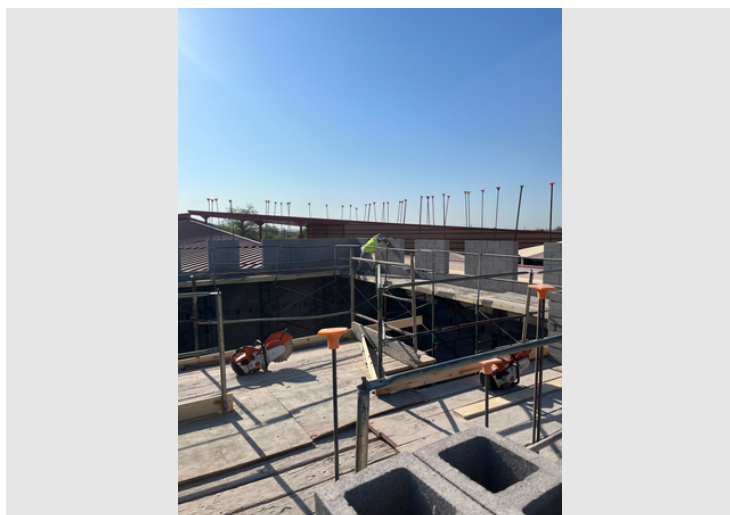

Description

Second floor window openings south view.

Taken Date

07/26/2023 at 08:02 am

Uploaded By

Carlos Peralta

Upload Date

07/26/2023 at 08:03 am

File Name

[3A75E98B-A628-407C-86B6-6AA...](#)



Description

CJS forklifts operator run over door at lay down yard with his rear right tire.

Taken Date

07/25/2023 at 12:27 pm

Uploaded By


Carlos Peralta

Upload Date

07/25/2023 at 12:27 pm

File Name

[856F8535-638B-49D8-BDDD-24C...](#)

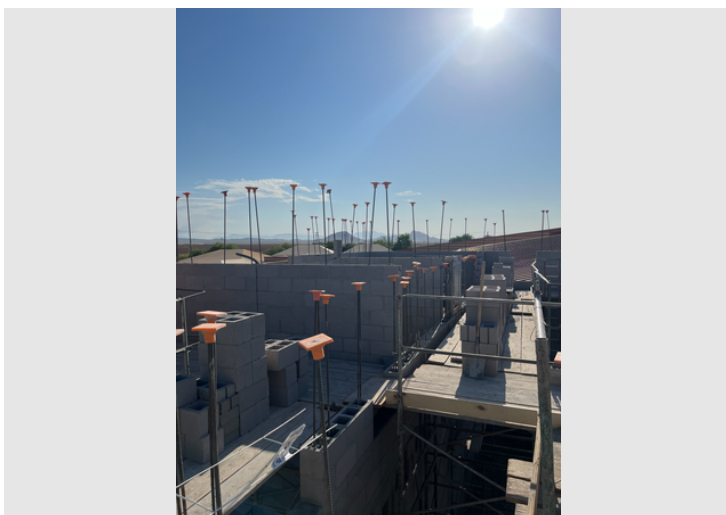

Description

East side view 5 Th CMU lift

Taken Date

07/26/2023 at 08:02 am

Uploaded By

Carlos Peralta

Upload Date

07/26/2023 at 08:03 am

File Name

[4714A4F3-D270-4051-BA20-FDE...](#)



Description

Plumbing removed from lounge area.

Taken Date

07/25/2023 at 07:40 am

Uploaded By


Carlos Peralta

Upload Date

07/25/2023 at 07:41 am

File Name

[CD11E1BD-E989-4EF4-A4A8-43E...](#)

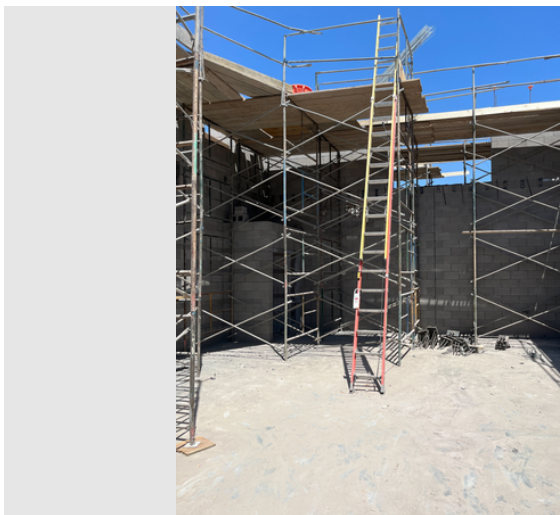

Description

Safety Tag on Ladders at scaffold.

Taken Date

07/24/2023 at 01:43 pm

Uploaded By


Carlos Peralta

Upload Date

07/24/2023 at 01:43 pm

File Name

928E96ED-CCEB-4249-B453-DEE...

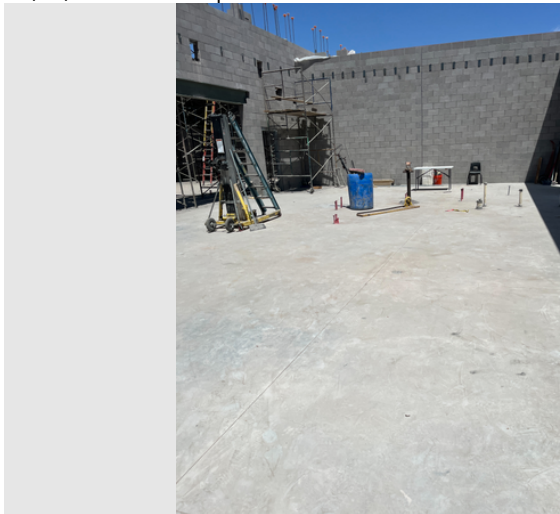

Description

1 Fl.Clean ready for steel crew

Taken Date

07/24/2023 at 01:43 pm

Uploaded By


Carlos Peralta

Upload Date

07/24/2023 at 01:43 pm

File Name

553C458B-218E-4387-B382-AFA0...

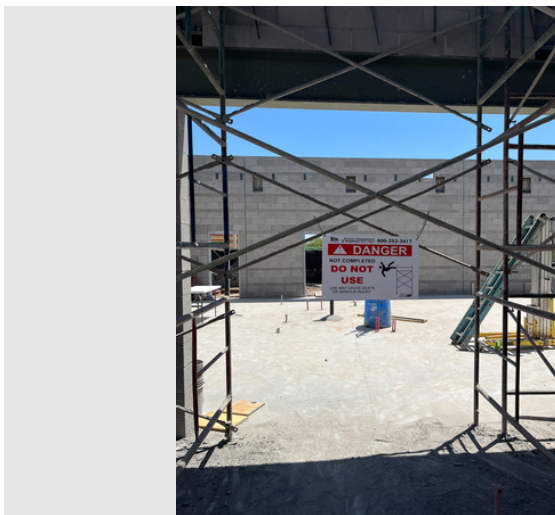

Description

Scaffold tags up to date.

Taken Date

07/24/2023 at 01:43 pm

Uploaded By


Carlos Peralta

Upload Date

07/24/2023 at 01:43 pm

File Name

E7254B42-DD09-46AA-9736-CA1...

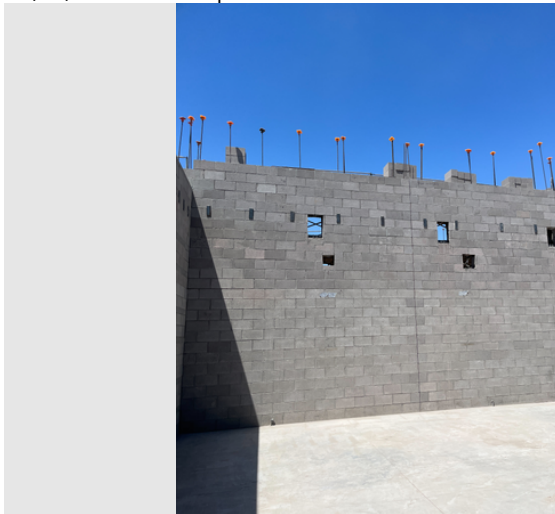

Description

Openings for steel beams complete.

Taken Date

07/24/2023 at 01:43 pm

Uploaded By


Carlos Peralta

Upload Date

07/24/2023 at 01:43 pm

File Name

709E6E0B-BBFC-43F5-86B1-3FDA...

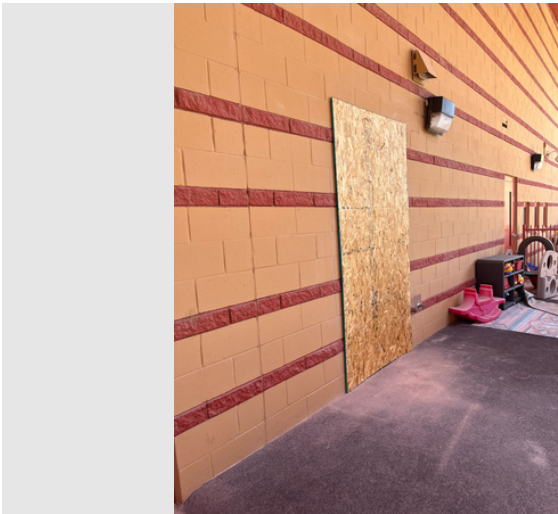

Description

Temp plywood at new doors Teachers lounge.

Taken Date

07/24/2023 at 12:20 pm

Uploaded By


Carlos Peralta

Upload Date

07/24/2023 at 12:25 pm

File Name

[D486EE53-9326-42CD-94BB-6EB...](#)

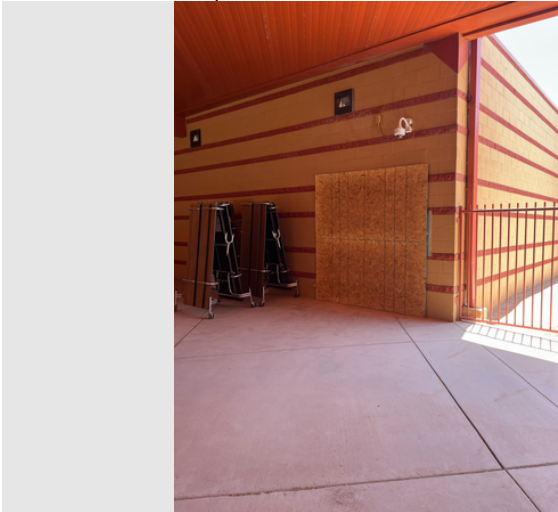

Description

Covering opening until door frame is installed.

Taken Date

07/24/2023 at 12:20 pm

Uploaded By


Carlos Peralta

Upload Date

07/24/2023 at 12:52 pm

File Name

[A2573A4D-F32B-47F0-8190-641F...](#)

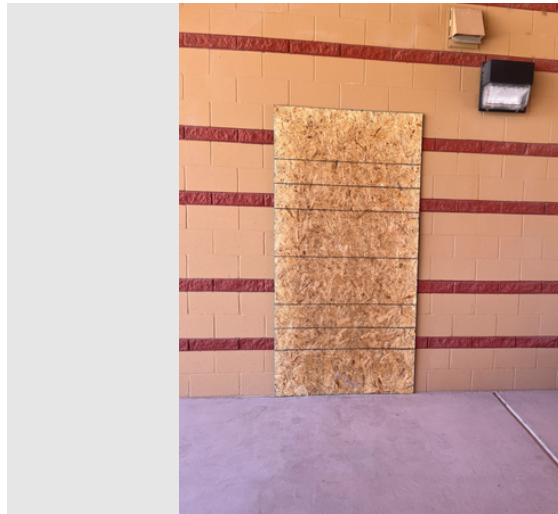

Description

New door at infant area.

Taken Date

07/24/2023 at 12:20 pm

Uploaded By


Carlos Peralta

Upload Date

07/24/2023 at 01:43 pm

File Name

[3B6DE740-933E-44A4-82E7-BAE...](#)

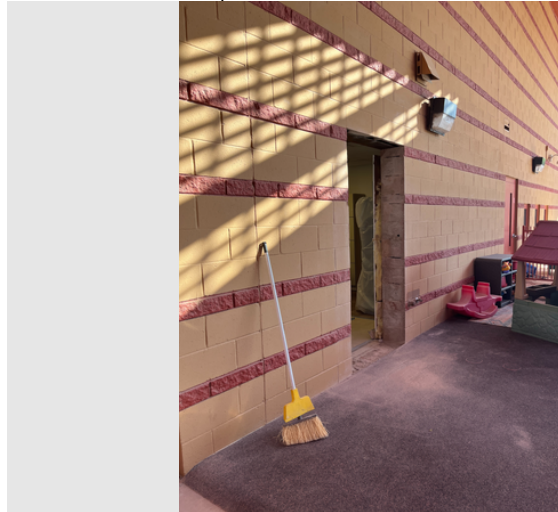

Description

Excysting cells hollow need to work with mason on filling cells for new door install.

Taken Date

07/24/2023 at 08:15 am

Uploaded By


Carlos Peralta

Upload Date

07/24/2023 at 08:18 am

File Name

[2E942FC7-4065-4BD9-B133-FD6...](#)

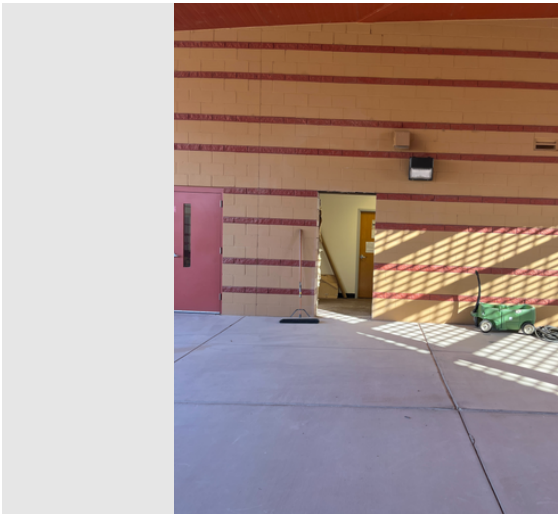

Description

Laundry room new door to follow.

Taken Date

07/24/2023 at 08:14 am

Uploaded By


Carlos Peralta

Upload Date

07/24/2023 at 11:32 am

File Name

6FBFF3D0-2DB6-4EE1-9877-5F73...

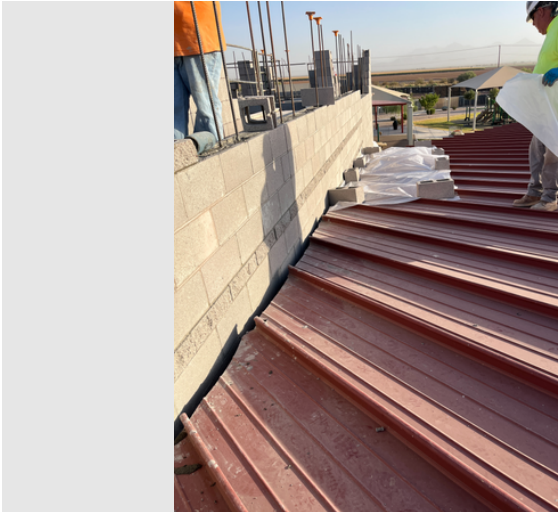

Description

East side existing roof protection in progress.

Taken Date

07/21/2023 at 06:50 am

Uploaded By


Carlos Peralta

Upload Date

07/21/2023 at 06:51 am

File Name

7A0371DB-8BFD-45FE-930B-5FC...

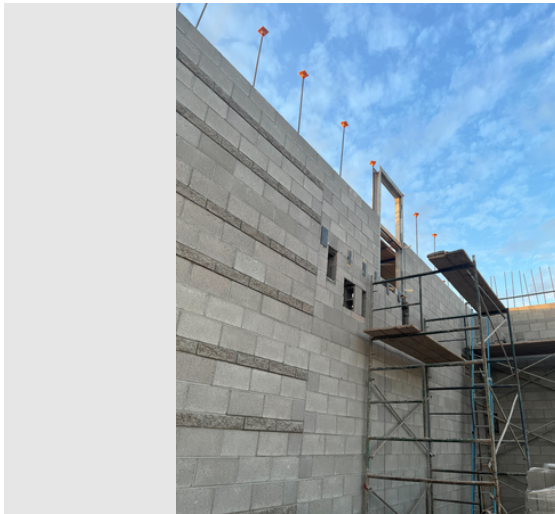

Description

Second floor door framed installed.

Taken Date

07/24/2023 at 05:57 am

Uploaded By


Carlos Peralta

Upload Date

07/24/2023 at 05:57 am

File Name

CA9AA277-D085-4D27-8A67-224...

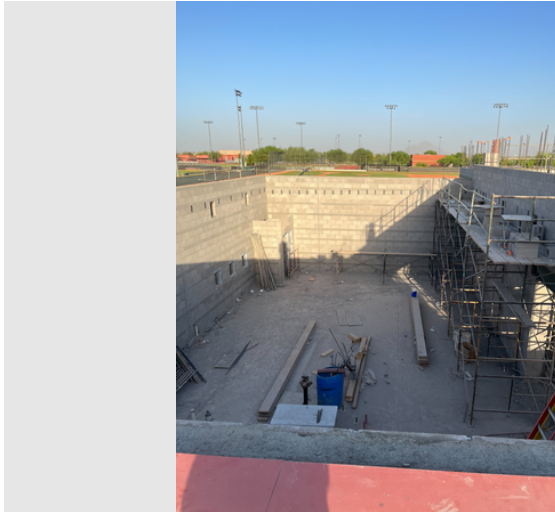

Description

South side first floor cleaning in progress,

Taken Date

07/21/2023 at 06:40 am

Uploaded By


Carlos Peralta

Upload Date

07/21/2023 at 06:40 am

File Name

2721077E-3A24-4A4E-B94F-5A98...

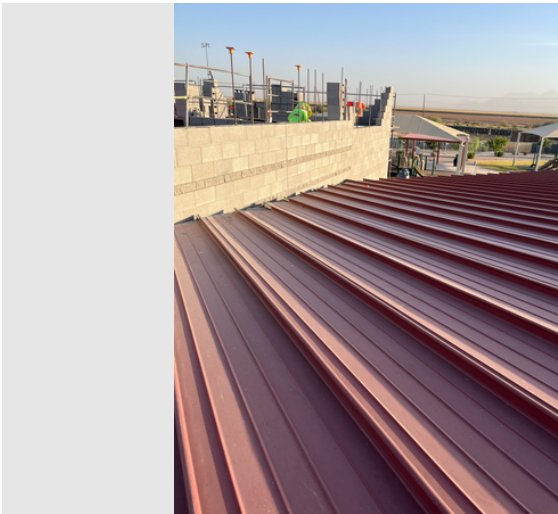

Description

East side all clean roof protection to follow.

Taken Date

07/21/2023 at 06:38 am

Uploaded By

Carlos Peralta

Upload Date

07/21/2023 at 06:39 am

File Name

[3F333EA4-FF80-4A77-8A51-2BEA...](#)



Description

#2 Ties in place.

Taken Date

07/18/2023 at 09:56 am

Uploaded By


Carlos Peralta

Upload Date

07/18/2023 at 11:14 am

File Name

[10B17A00-FA02-42F5-88B4-609D...](#)

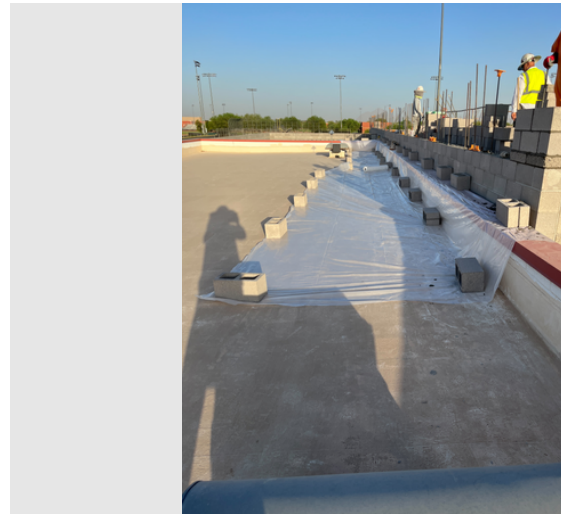

Description

Masons roof protection south side.

Taken Date

07/21/2023 at 06:38 am

Uploaded By

Carlos Peralta

Upload Date

07/21/2023 at 06:39 am

File Name

[61AEC139-18C8-4508-8536-6927...](#)



Description

#2 ties in both columns at mechanical yard.

Taken Date

07/18/2023 at 09:56 am

Uploaded By

Carlos Peralta

Upload Date

07/18/2023 at 11:14 am

File Name

[911DF369-D261-4DD3-9D57-2D9...](#)



Description

Steel lenthil install complete by storage Room.

Taken Date

07/14/2023 at 12:28 pm

Uploaded By


Carlos Peralta

Upload Date

07/14/2023 at 12:30 pm

File Name

91C66BC5-34BA-46B1-B930-5E4...

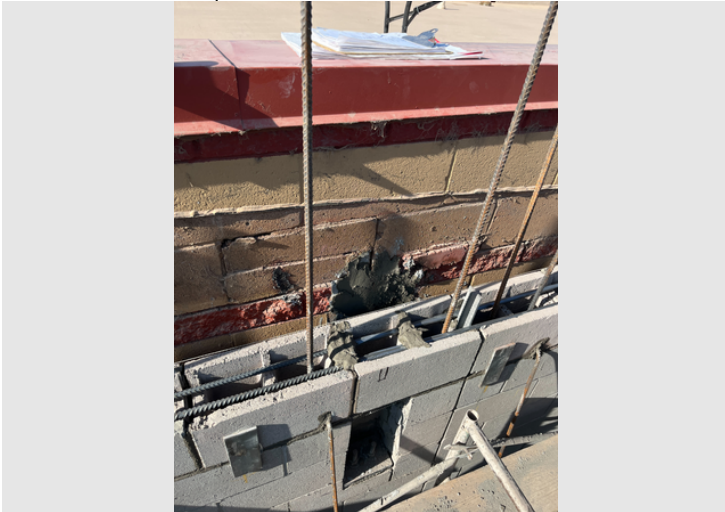

Description

Repairs.

Taken Date

07/14/2023 at 08:00 am

Uploaded By


Carlos Peralta

Upload Date

07/14/2023 at 08:20 am

File Name

FD2B2E30-F548-4FD4-A421-73B1...

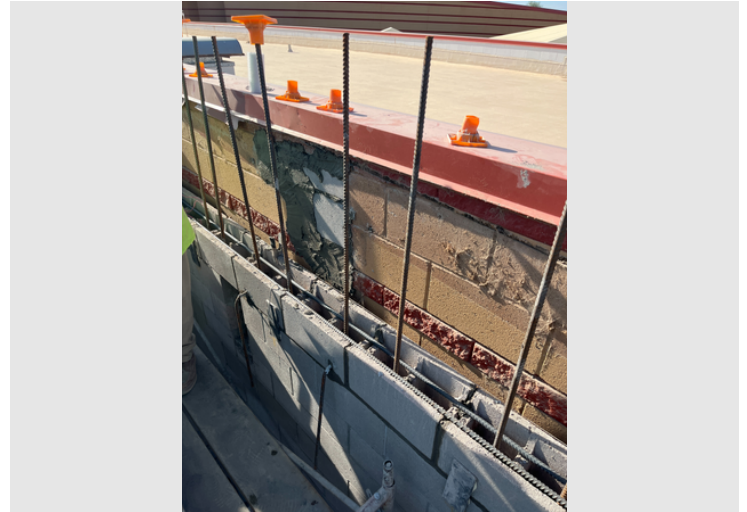

Description

Repairs at excysting bldg.

Taken Date

07/14/2023 at 08:00 am

Uploaded By


Carlos Peralta

Upload Date

07/14/2023 at 08:26 am

File Name

3E661BFD-8CC4-4789-A97E-C73...

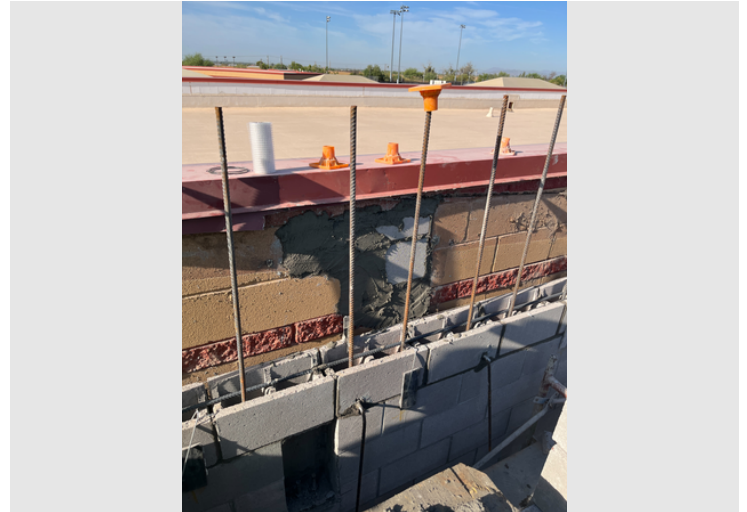

Description

Repairs.

Taken Date

07/14/2023 at 08:00 am

Uploaded By


Carlos Peralta

Upload Date

07/14/2023 at 08:36 am

File Name

2381B949-E8E1-4D6E-84E9-F550...

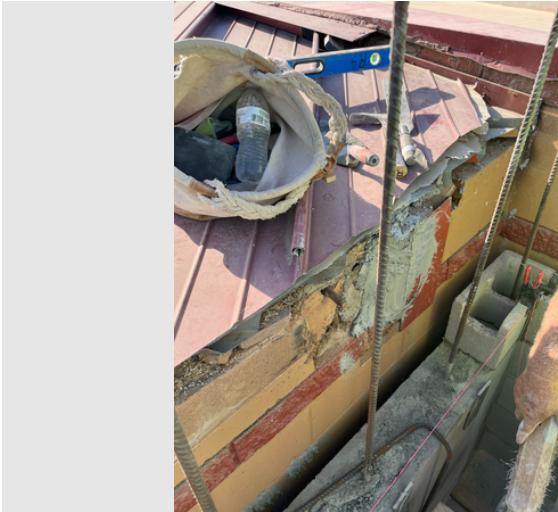

Description

Repairs.

Taken Date

07/14/2023 at 08:00 am

Uploaded By


Carlos Peralta

Upload Date

07/14/2023 at 08:20 am

File Name

7DEE0AC9-36DF-4E0F-8038-E50...

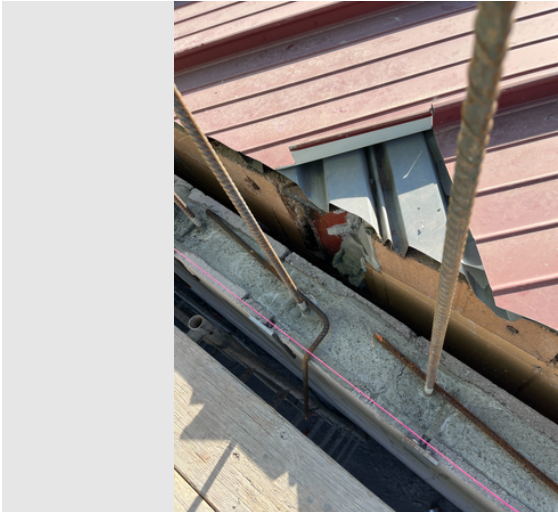

Description

Repairs.

Taken Date

07/14/2023 at 08:00 am

Uploaded By


Carlos Peralta

Upload Date

07/14/2023 at 08:06 am

File Name

CA03D420-E4D8-42F2-A43D-8C5...

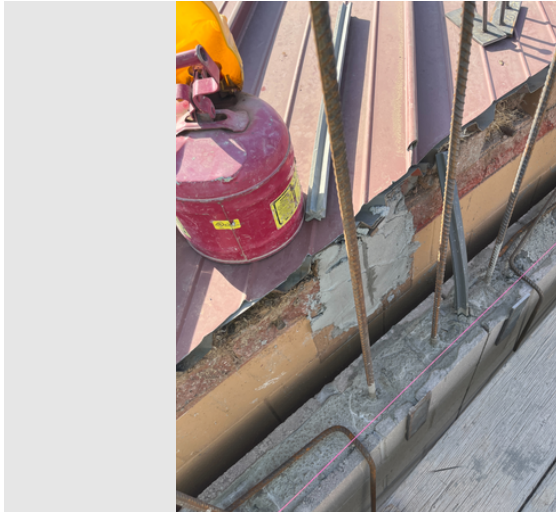

Description

Repairs.

Taken Date

07/14/2023 at 08:00 am

Uploaded By

Carlos Peralta

Upload Date

07/14/2023 at 08:16 am

File Name

04DD1D2B-9199-49FB-8824-D01...



Description

Stem Wall in progress.

Taken Date

07/14/2023 at 07:35 am

Uploaded By

Carlos Peralta

Upload Date

07/14/2023 at 07:49 am

File Name

9A126889-140B-43C3-B2FA-B770...



Description

Mechanical yard stem wall.

Taken Date

07/14/2023 at 07:35 am

Uploaded By

Carlos Peralta

Upload Date

07/14/2023 at 07:49 am

File Name

[BB9FC0AC-54C3-449D-9A8E-88B...](#)



Description

First floor Ledger angle embeds installed.

Taken Date

07/12/2023 at 06:16 am

Uploaded By

Carlos Peralta

Upload Date

07/12/2023 at 06:16 am

File Name

[CF1EA9A6-147C-47A6-963F-6158...](#)



Description

First floor on the south side complete.

Taken Date

07/13/2023 at 08:30 am

Uploaded By

Carlos Peralta

Upload Date

07/13/2023 at 08:31 am

File Name

[5FD149FD-AFA2-47B9-A868-7CF6...](#)



Description

Mechanical yard Rebar inspection today it pass. and electrical sleeve has been removed.

Taken Date

07/05/2023 at 09:56 am

Uploaded By


Carlos Peralta

Upload Date

07/05/2023 at 09:56 am

File Name

[7E42793E-370D-46A5-A5BC-3C0...](#)

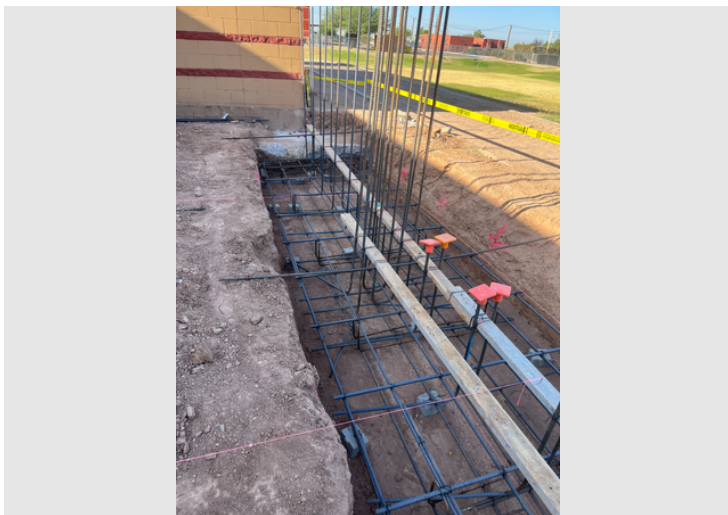

Description

Verticals all good ready for concrete pour.

Taken Date

07/05/2023 at 07:44 am

Uploaded By

Carlos Peralta

Upload Date

07/05/2023 at 07:48 am

File Name

D722C22A-BCB5-4562-AC68-9B3...



Description

Electrical sleeve needs to be removed per city inspector.

Taken Date

07/05/2023 at 07:44 am

Uploaded By

Carlos Peralta

Upload Date

07/05/2023 at 07:49 am

File Name

068B058A-7BED-46CE-94A9-52F...



Description

Pedestals all good and pass inspection ready for concrete.

Taken Date

07/05/2023 at 07:44 am

Uploaded By

Carlos Peralta

Upload Date

07/05/2023 at 07:49 am

File Name

B25AF9C9-FC66-4475-B463-1382...
