



Salt River Pima-Maricopa Indian Community

10005 East Osborn Road • Scottsdale, Arizona 85256
Phone (480) 362-7700 • Fax (480) 362-5597

MONTHLY PROJECT PROGRESS UPDATE

Project: ECEC Classroom and Parking Expansion

Issued Date: December 6, 2023 | **December - 2023 UPDATE**

Distribution:

	Name	Department/ Company
X	Tami Brungard	ECEC – Edu Leader
X	Lekisha Morris	ECEC - EHS
X	Barbara White	ECEC - HS
X	Melody Herne	EDU - Superintendent
X	Michael Fowler	EDU - Support Svc Director
X	Tate Walker	Public Relations Dir.
X	Heaven Sepulveda	Edu. Board./ Policy Council
X	Pamela Prasher	ECEC – CCDF

	Name	Department/ Company
X	Felicia Toya	Policy Council - HSR
X	Jocy Goseyun	Policy Council - HSR
X	Robyn Masten	Policy Council - HSR
X	Lorna Phillips	Policy Council - EHSR
X	Ruben Reyes	Policy Council - EHSR
X	Martha Ludlow-Martinez	Policy Council - HBR
X	Carmen Briones	Policy Council
X	Mikah Carlos	Community Council

Work Completed:


Items

1. Group #3 Classroom renovation completed (A-131, A-120, B-142, C-108).
2. First Floor interior metal stud furring, wall and door frame install completed.
3. 1st Floor and partial 2nd Floor mechanical rough-in completed.
4. Building B Addition CMU painting completed.

Work anticipated in the next month:

1. Group #4 Classroom renovations (A-138, A-121, B-143, C-109).
2. On-going mechanical, plumbing and electrical rough-in work at 2nd Floor.
3. Existing building exterior painting on-going.
4. Building B Addition 2nd Floor metal roof underlayment install and metal roof install to start.
5. Drywall install to start once roof and window openings are dried in.
6. Mechanical yard cooling tower to arrive and be installed.
7. New sand pit and shade structure relocation to start, tentatively complete by end of the month.
8. Staff Lounge at Building D to be completed.

Project Schedule | Three Week Look Ahead

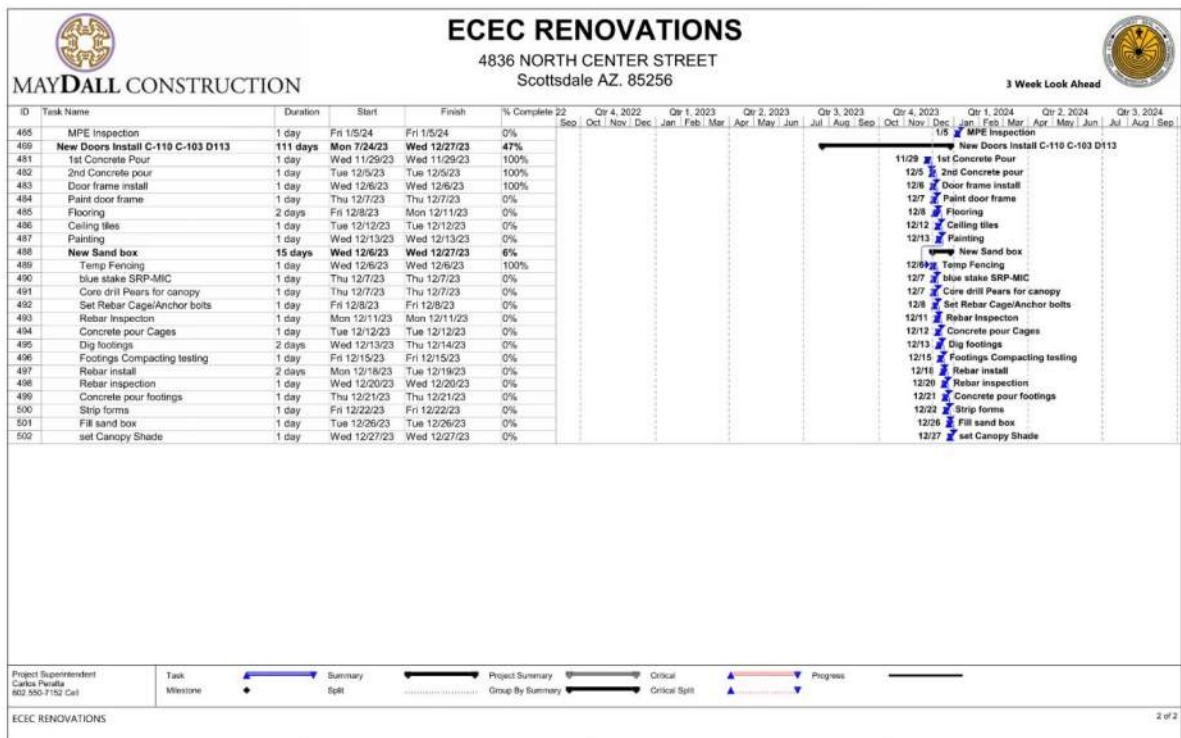

SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Progress Photos:

See attached.



Description

Shark skin underlayment onsite delivery.

Taken Date

12/05/2023 at 02:35 pm

Uploaded By

Carlos Peralta

Upload Date

12/05/2023 at 02:52 pm

File Name

4764CEAA-EEFE-4076-8A23-D99F...



Description

Dens glass board delivery.

Taken Date

12/05/2023 at 02:35 pm

Uploaded By

Carlos Peralta

Upload Date

12/05/2023 at 02:50 pm

File Name

D614350F-C491-40FE-866D-2655...



Description

Roof metal clips.

Taken Date

12/05/2023 at 02:35 pm

Uploaded By

Carlos Peralta

Upload Date

12/05/2023 at 02:50 pm

File Name

4BDE3A34-CE76-49DC-9188-D2A...



Description

Foam delivery. 1st truck

Taken Date

12/05/2023 at 02:35 pm

Uploaded By

Carlos Peralta

Upload Date

12/05/2023 at 02:50 pm

File Name

79A19096-F8E4-4F84-B9F0-08CD...



Description

Teachers lounge broom finish in progress.

Taken Date

12/05/2023 at 10:10 am

Uploaded By

Carlos Peralta

Upload Date

12/05/2023 at 02:35 pm

File Name

[2C6F7E6E-FEB4-4BE5-BFC4-1A72...](#)



Description

Pumping concrete at teachers lounge.

Taken Date

12/05/2023 at 05:43 am

Uploaded By


Frank Bondi

Upload Date

12/05/2023 at 05:43 am

File Name

[8275FF34-6321-4B95-B6B2-5749...](#)

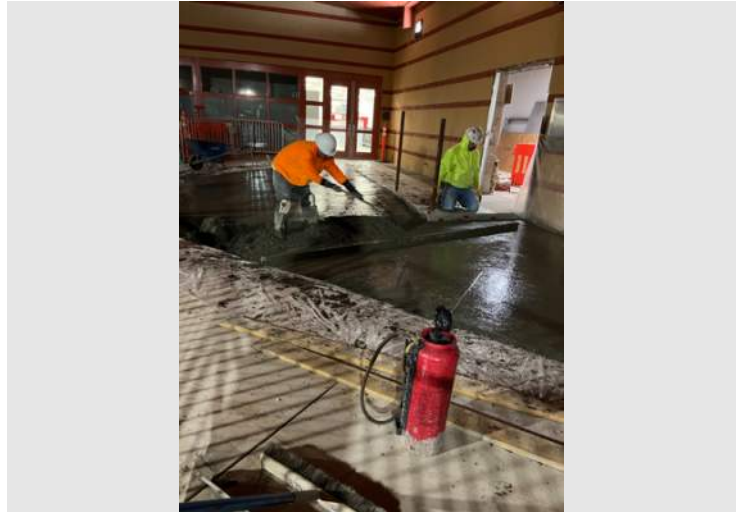

Description

Teachers lounge concrete pour in progress.

Taken Date

12/05/2023 at 06:13 am

Uploaded By

Frank Bondi

Upload Date

12/05/2023 at 06:13 am

File Name

[95CA248A-35FD-46AF-8F6B-2BA...](#)



Description

Concrete crew installing Dowels and Expansion Joint materials.

Taken Date

12/04/2023 at 07:51 am

Uploaded By

Frank Bondi

Upload Date

12/04/2023 at 07:51 am

File Name

[55B6A53B-AC6C-4E83-9277-06C...](#)



Description

Painter masking off window frames.

Taken Date

12/04/2023 at 07:47 am

Uploaded By

Frank Bondi

Upload Date

12/04/2023 at 07:47 am

File Name

[46914EDC-6393-409F-8A11-EDC...](#)



Description

Taken Date

12/01/2023 at 09:35 am

Uploaded By

Carlos Peralta

Upload Date

12/01/2023 at 09:59 am

File Name

[9BA24FD4-A2AF-4D2B-9B01-FFD...](#)



Description

Taken Date

12/01/2023 at 01:44 pm

Uploaded By


Carlos Peralta

Upload Date

12/01/2023 at 02:05 pm

File Name

[214F29C0-81CC-42EB-9254-397E...](#)

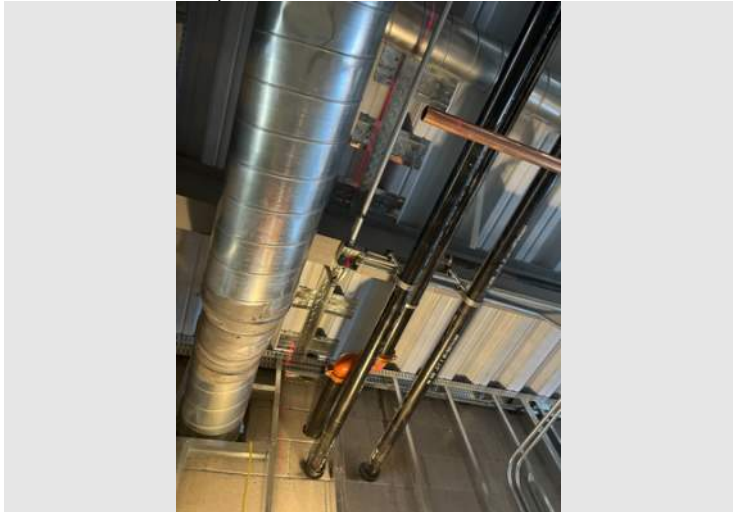

Description

Taken Date

12/01/2023 at 08:26 am

Uploaded By


Carlos Peralta

Upload Date

12/01/2023 at 08:27 am

File Name

[8C722BBA-9DAA-48A5-B2FF-66A...](#)

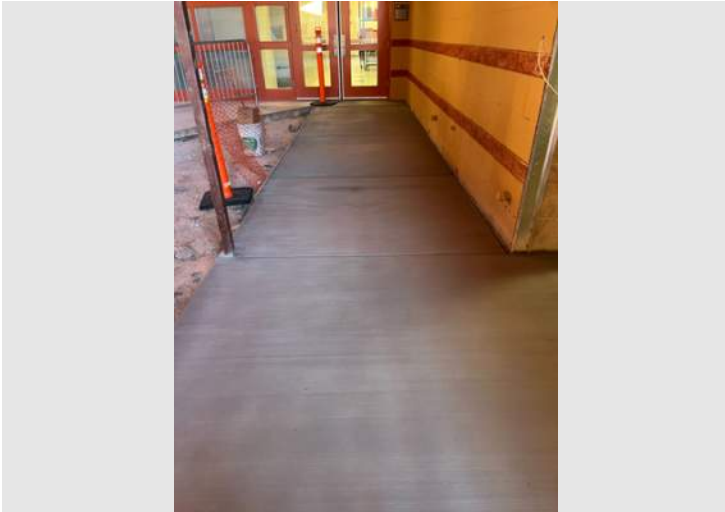

Description

Taken Date

12/01/2023 at 08:15 am

Uploaded By


Frank Bondi

Upload Date

12/01/2023 at 08:15 am

File Name

[9FD4787B-548B-4039-821F-87EB...](#)

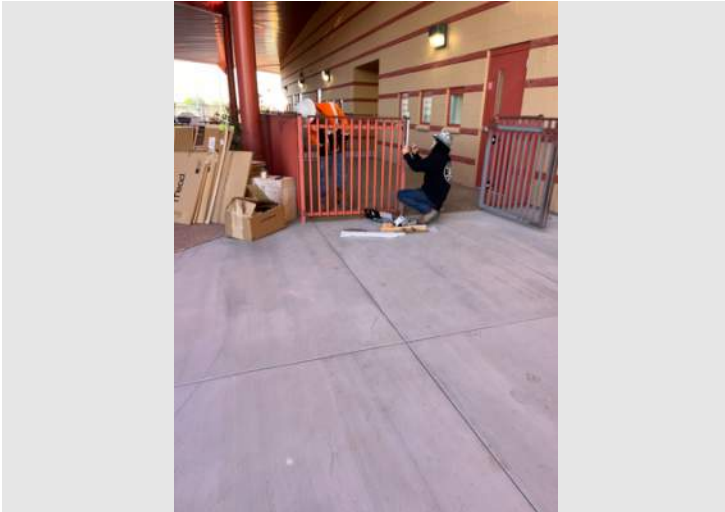

Description

Installing Gate Latches and priming welds on pickets

Taken Date

11/30/2023 at 08:38 am

Uploaded By


Frank Bondi

Upload Date

11/30/2023 at 03:41 pm

File Name

[FA9E5C5B-9E61-40AB-BD29-656...](#)

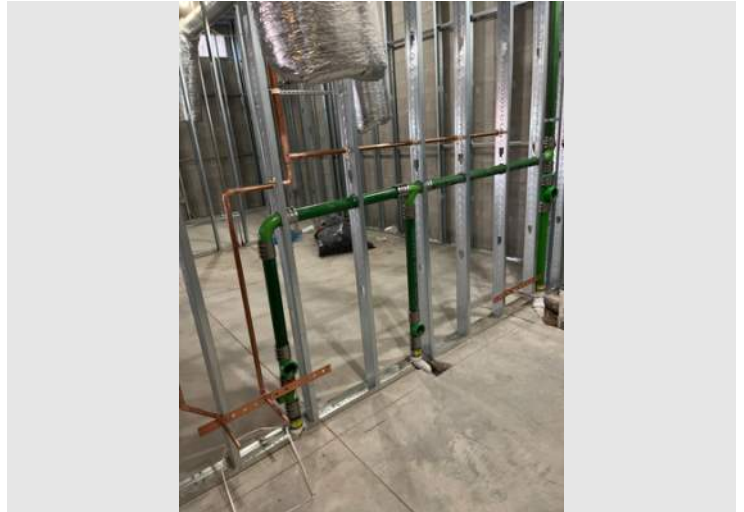

Description

Plumbing getting installed in building B Restroom.

Taken Date

11/30/2023 at 02:27 pm

Uploaded By

Carlos Peralta

Upload Date

11/30/2023 at 02:36 pm

File Name

[70BC97B7-F511-4766-B84E-0D3...](#)



Description

Teachers Lounge ADA landing pour.

Taken Date

11/30/2023 at 05:52 am

Uploaded By

Frank Bondi

Upload Date

11/30/2023 at 05:53 am

File Name

[62F1388B-96C2-437F-B973-8786...](#)



Description

New boiler install in progress.

Taken Date

11/29/2023 at 10:49 am

Uploaded By


Frank Bondi

Upload Date

11/29/2023 at 10:49 am

File Name

[259A00E6-9272-4EBF-BCC0-AD0...](#)

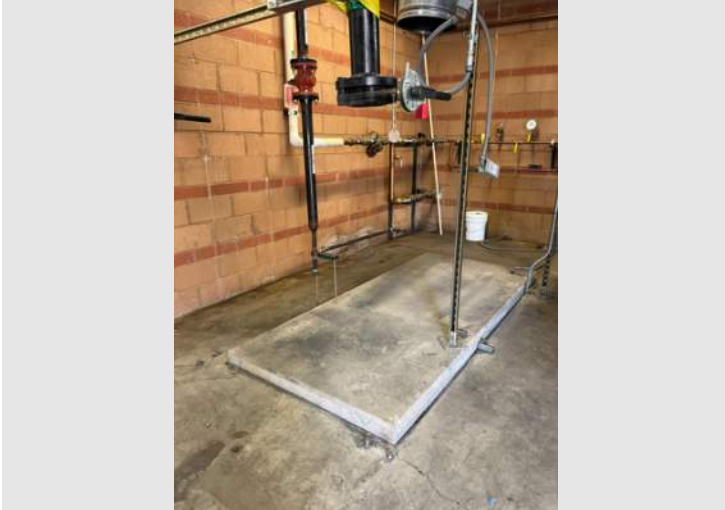

Description

Old boiler removed new one to follow.

Taken Date

11/28/2023 at 11:21 am

Uploaded By

Carlos Peralta

Upload Date

11/28/2023 at 11:33 am

File Name

[88D65A49-94C8-45BA-BC71-618...](#)



Description

Building B 2nd floor Installing Ductwork.

Taken Date

11/29/2023 at 07:04 am

Uploaded By

Frank Bondi

Upload Date

11/29/2023 at 07:04 am

File Name

[0263C875-E6D7-4088-8A03-E2A...](#)



Description

Exterior louvers primer.

Taken Date

11/28/2023 at 11:17 am

Uploaded By


Carlos Peralta

Upload Date

11/28/2023 at 11:21 am

File Name

[38FE4D5C-7181-49F9-BA69-EB06...](#)

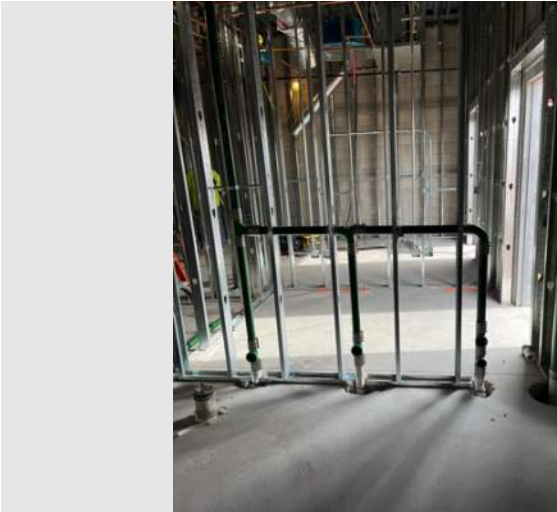

Description

Plumbing wall rough in

Taken Date

11/27/2023 at 11:49 am

Uploaded By


Carlos Peralta

Upload Date

11/27/2023 at 12:15 pm

File Name

[D584BEEF-8C45-42A8-A566-420...](#)

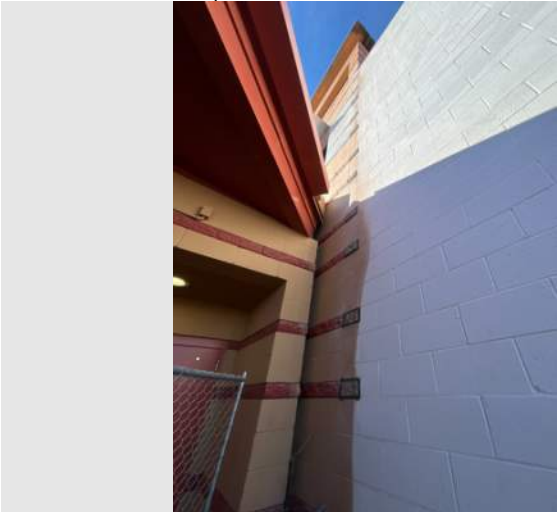

Description

Split face block repairs complete

Taken Date

11/22/2023 at 10:20 am

Uploaded By


Carlos Peralta

Upload Date

11/22/2023 at 01:28 pm

File Name

[7777CAFF-FF6E-4172-A6D7-D74E...](#)

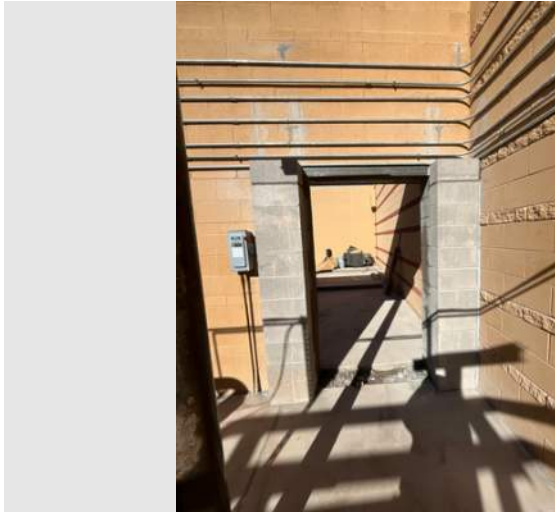

Description

Pilars at exciting mechanical yard complete

Taken Date

11/22/2023 at 01:28 pm

Uploaded By


Carlos Peralta

Upload Date

11/22/2023 at 02:46 pm

File Name

[BE61299B-057A-4F2C-8A46-3E41...](#)

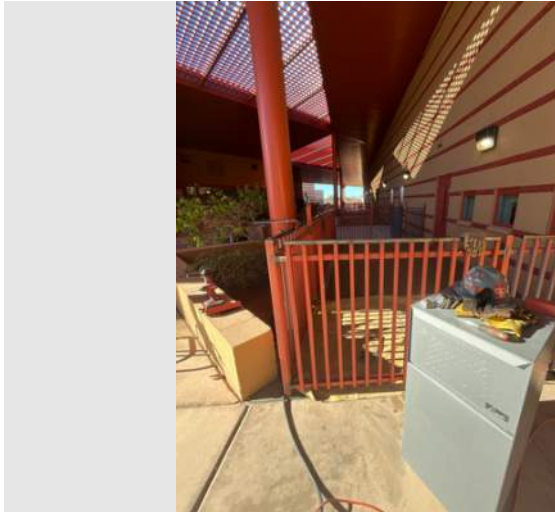

Description

1" Picket install in progress.

Taken Date

11/22/2023 at 09:23 am

Uploaded By


Carlos Peralta

Upload Date

11/22/2023 at 09:52 am

File Name

[432EB4ED-19D0-44BC-B43D-7AE...](#)

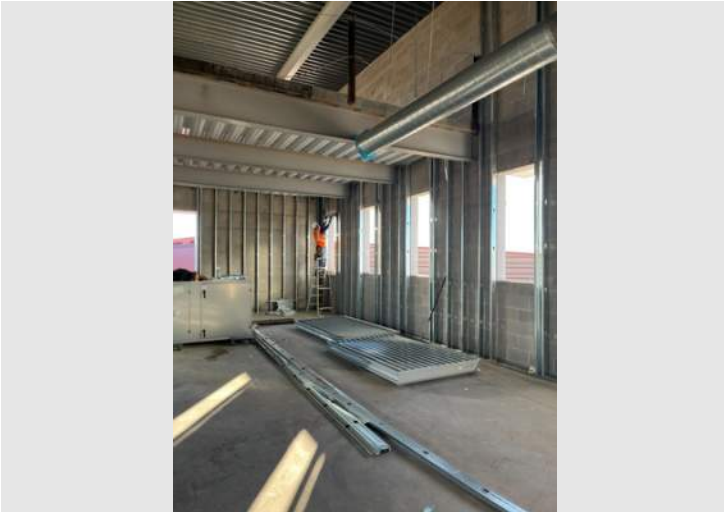

Description

Wall Furr out in progress second floor.

Taken Date

11/22/2023 at 08:12 am

Uploaded By


Carlos Peralta

Upload Date

11/22/2023 at 08:14 am

File Name

[AD5B0617-212D-4641-A9DE-8D1...](#)

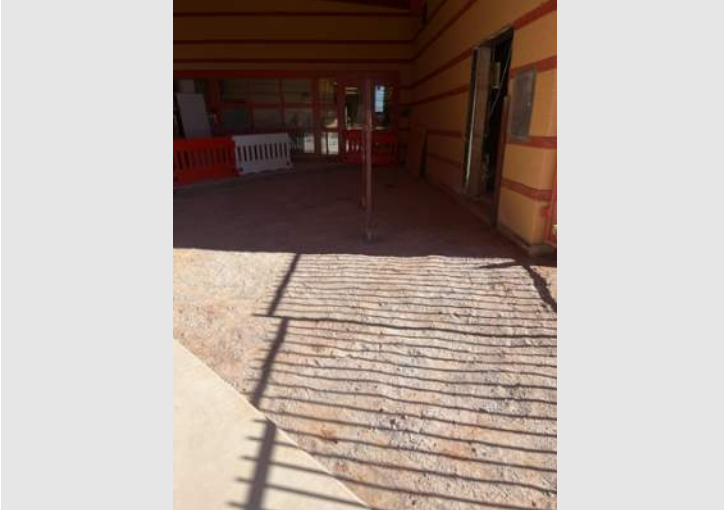

Description

Teachers lounge ready for concrete pour.

Taken Date

11/20/2023 at 01:00 pm

Uploaded By

Carlos Peralta

Upload Date

11/20/2023 at 01:04 pm

File Name

[E74D2616-8B90-4B8E-8630-A19...](#)



Description

Second floor framing in progress.

Taken Date

11/22/2023 at 08:12 am

Uploaded By


Carlos Peralta

Upload Date

11/22/2023 at 08:13 am

File Name

[3652CD3C-F896-41A4-B23F-9877...](#)

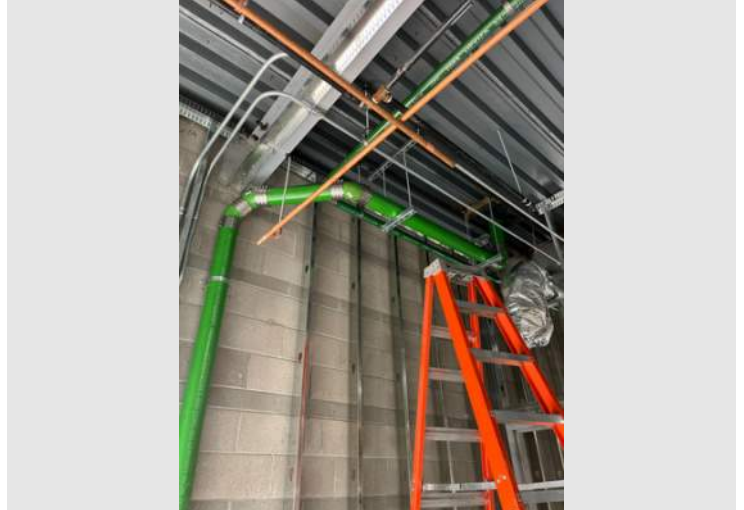

Description

first floor storm drain pipe connection complete.

Taken Date

11/16/2023 at 02:22 pm

Uploaded By


Carlos Peralta

Upload Date

11/17/2023 at 06:27 am

File Name

[31C5DF7B-E299-47DE-AC34-9DC...](#)

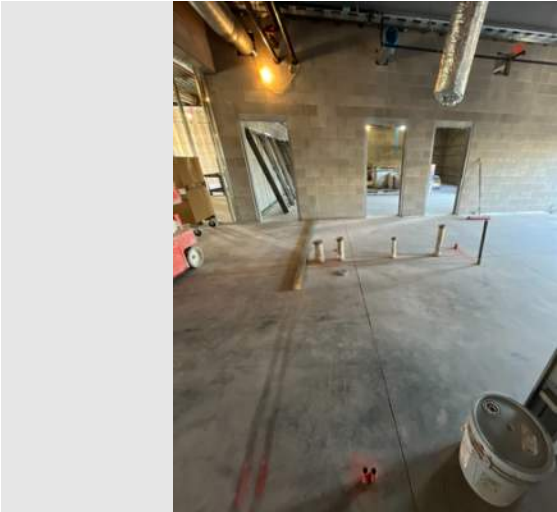

Description

Back to back infant restrooms on first floor

Taken Date

11/13/2023 at 02:23 pm

Uploaded By


Carlos Peralta

Upload Date

11/13/2023 at 02:25 pm

File Name

662C91E8-E1D2-4C39-9A34-BE1...

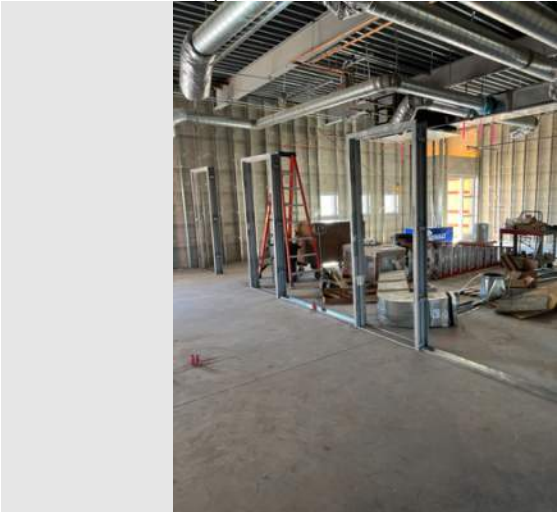

Description

framing continues on first floor.

Taken Date

11/09/2023 at 02:08 pm

Uploaded By

Carlos Peralta

Upload Date

11/09/2023 at 02:08 pm

File Name

FA367C08-3EDA-444F-A77F-0FC3...



Description

First floor framing in progress

Taken Date

11/13/2023 at 02:23 pm

Uploaded By

Carlos Peralta

Upload Date

11/13/2023 at 02:23 pm

File Name

ED07E489-4948-460D-907D-FA0...



Description

Door frames install in progress first floor.

Taken Date

11/09/2023 at 02:08 pm

Uploaded By

Carlos Peralta

Upload Date

11/09/2023 at 02:18 pm

File Name

81526CA7-6DDE-4720-92FE-D3C...



Description

Platinum color sample.

Taken Date

11/09/2023 at 08:34 am

Uploaded By


Carlos Peralta

Upload Date

11/09/2023 at 08:35 am

File Name

[EA0C5F6D-D8B9-47F2-8144-E18...](#)

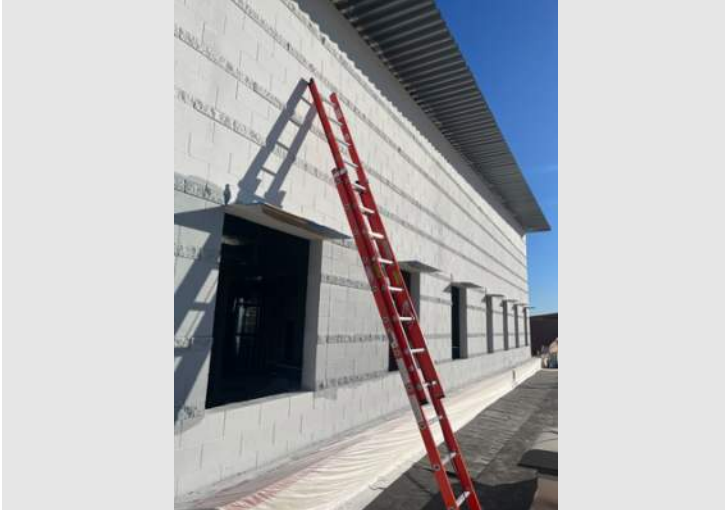

Description

South side view bldg. B

Taken Date

11/09/2023 at 08:34 am

Uploaded By


Carlos Peralta

Upload Date

11/09/2023 at 08:34 am

File Name

[B28E87E3-2262-4024-B94F-B571...](#)

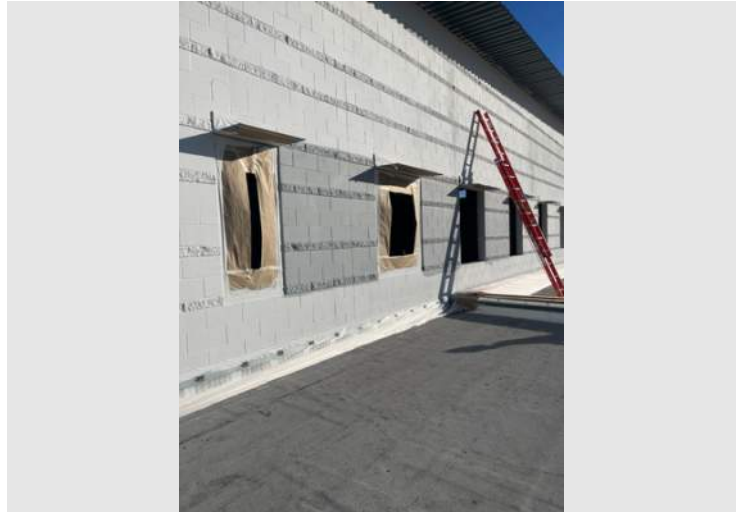

Description

Platinum color ban on the South side bldg.b

Taken Date

11/09/2023 at 08:34 am

Uploaded By

Carlos Peralta

Upload Date

11/09/2023 at 08:34 am

File Name

[CE2EF9F6-36D5-4035-944D-0777...](#)



Description

North side of bldg. B painting complete.

Taken Date

11/06/2023 at 10:31 am

Uploaded By


Carlos Peralta

Upload Date

11/06/2023 at 10:31 am

File Name

[EA049D06-B628-4574-B66D-761...](#)

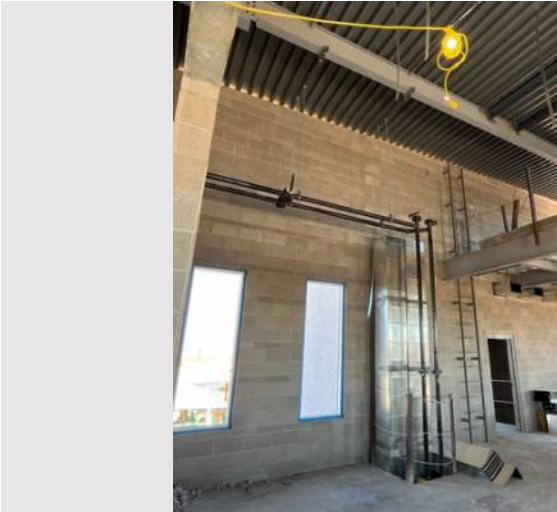

Description

2" Water lines valves install in progress.

Taken Date

11/06/2023 at 10:29 am

Uploaded By


Carlos Peralta

Upload Date

11/06/2023 at 10:31 am

File Name

B9A6169F-17DB-4762-B5AC-D5D...

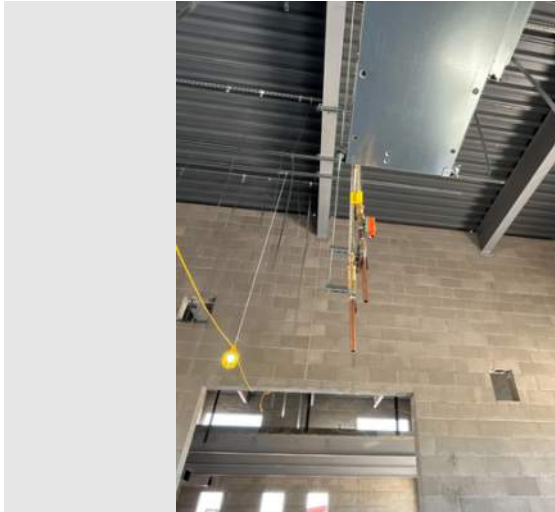

Description

Water hose lines installed

Taken Date

11/06/2023 at 10:29 am

Uploaded By

Carlos Peralta

Upload Date

11/06/2023 at 10:31 am

File Name

3FE7B5E5-4295-4814-97D9-033E...



Description

North side bldg. painting in progress.

Taken Date

11/03/2023 at 01:30 pm

Uploaded By

Carlos Peralta

Upload Date

11/03/2023 at 01:35 pm

File Name

0808357A-4C6B-4A5F-A4CF-8919...



Description

Mezzanine ladder install Complete.

Taken Date

11/03/2023 at 01:28 pm

Uploaded By

Carlos Peralta

Upload Date

11/03/2023 at 01:28 pm

File Name

15A85393-6FEA-43F1-9FC9-51D8...



Description

Taken Date

11/03/2023 at 07:53 am

Uploaded By

Carlos Peralta

Upload Date

11/03/2023 at 08:14 am

File Name

[B10C8045-B8A1-4CFD-A625-0C1...](#)



Description

Duct at East stairwell install complete.

Taken Date

11/02/2023 at 07:12 am

Uploaded By

Carlos Peralta

Upload Date

11/02/2023 at 07:28 am

File Name

[0EB8360C-17E8-4345-9F02-C60A...](#)



Description

ERV unit on site.

Taken Date

11/03/2023 at 07:02 am

Uploaded By

Carlos Peralta

Upload Date

11/03/2023 at 07:06 am

File Name

[F4F39C18-B9D4-4173-B284-1C9E...](#)

SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Attachments:

Item/s
1.
