



# Salt River Pima-Maricopa Indian Community

10005 East Osborn Road • Scottsdale, Arizona 85256

Phone (480) 362-7700 • Fax (480) 362-5597

## MONTHLY PROJECT PROGRESS UPDATE

**Project:** ECEC Classroom and Parking Expansion

**Issued Date:** January 5, 2024 | **January - 2024 UPDATE**

**Distribution:**

	Name	Department/ Company
X	Tami Brungard	ECEC – Edu Leader
X	Lekisha Morris	ECEC - EHS
X	Barbara White	ECEC - HS
X	Melody Herne	EDU - Superintendent
X	Michael Fowler	EDU - Support Svc Director
X	Tate Walker	Public Relations Dir.
X	Heaven Sepulveda	Edu. Board./ Policy Council
X	Pamela Prasher	ECEC – CCDF

	Name	Department/ Company
X	Felicia Toya	Policy Council - HSR
X	Jocy Goseyun	Policy Council - HSR
X	Robyn Masten	Policy Council - HSR
X	Lorna Phillips	Policy Council - EHSR
X	Ruben Reyes	Policy Council - EHSR
X	Martha Ludlow-Martinez	Policy Council - HBR
X	Carmen Briones	Policy Council
X	Mikah Carlos	Community Council

## Work Completed:

### Items


1. Group #3 Classroom renovations completed. Group #4 (A-138, A-121, B-143, C-109) started, heat pumps installed. Anticipated completion 2/2/24. Two groups remaining (6 rooms).
2. Building B Addition canopy column re-installed.
3. Playground #2 new sand pit and shade structure relocation completed.
4. Building B Addition 2<sup>nd</sup> floor metal studs 75% completed.
5. Building B Addition 1st floor electrical wire pulling started.

## Work anticipated in the next month:

1. Mechanical yard cooling tower to arrive and be installed on 1/8/24.
2. Existing building exterior painting on-going.
3. Building B Addition 2<sup>nd</sup> Floor metal roof install to continue.
4. Infant playground work to be completed and open.
5. Building D Staff Lounge renovation to be completed.
6. Building B Addition window glass install to start.
7. Drywall install to start.

# SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

## Project Schedule | Three Week Look Ahead

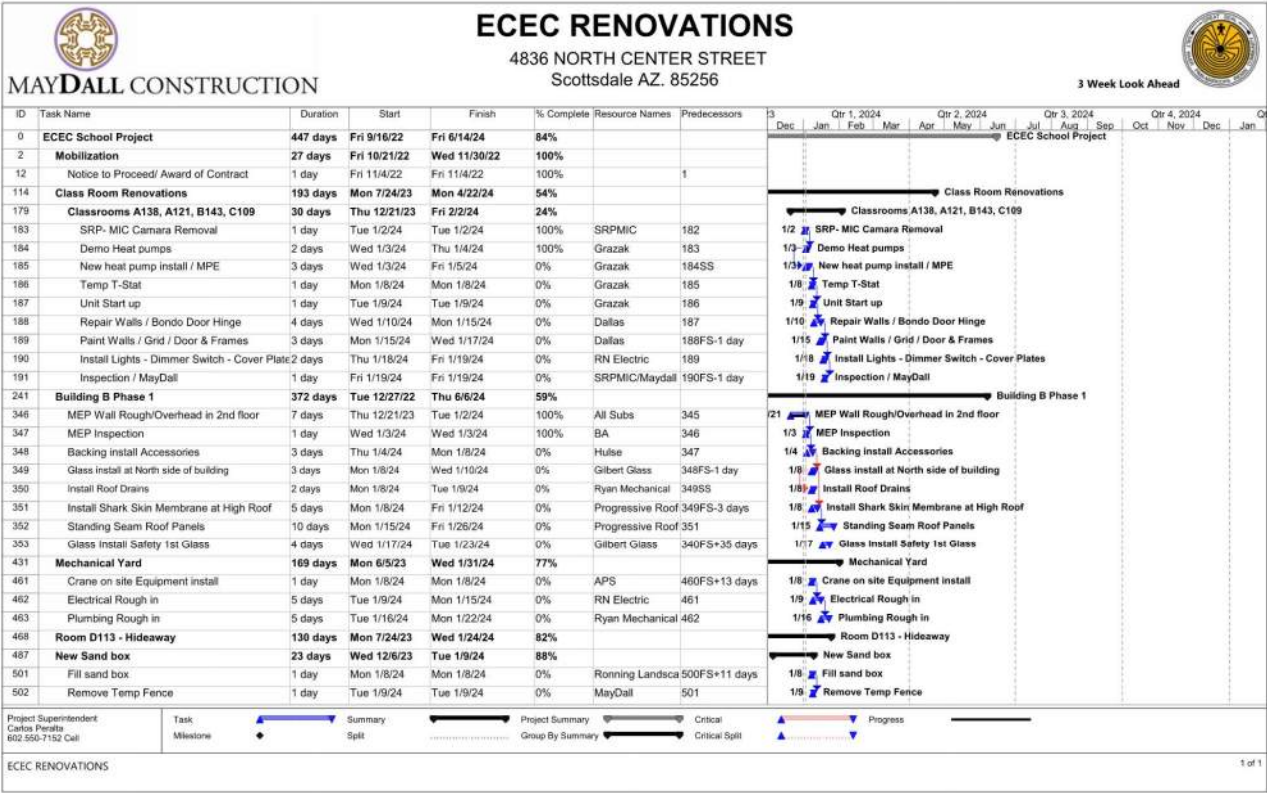

# SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Progress Photos:

---

See attached.



**Description**

Ceiling Damage in A121

**Taken Date**

12/28/2023 at 12:32 pm

**Uploaded By**

Frank Bondi

**Upload Date**

12/28/2023 at 12:32 pm

**File Name**

[ED60C57D-C8A3-4334-B9B1-1E1...](#)



**Description**

Core Drilling for Second Floor Plumbing

**Taken Date**

12/28/2023 at 11:06 am

**Uploaded By**


Frank Bondi

**Upload Date**

12/28/2023 at 11:19 am

**File Name**

[F163E164-9382-44F3-B3C1-1F91...](#)



**Description**

315 Fire - Charles Pumping up the System for Test

**Taken Date**

12/28/2023 at 11:19 am

**Uploaded By**


Frank Bondi

**Upload Date**

12/28/2023 at 11:19 am

**File Name**

[95FAEF1B-5343-4CEB-85BB-F9C5...](#)



**Description**

RN - Manny roughing in Second Floor

**Taken Date**

12/28/2023 at 11:02 am

**Uploaded By**


Frank Bondi

**Upload Date**

12/28/2023 at 11:02 am

**File Name**

[A323BA1C-D6E4-4816-9A47-96F...](#)



**Description**

RN - Chris Bending Conduit on Second Floor Rough-in

**Taken Date**

12/28/2023 at 11:01 am

**Uploaded By**


Frank Bondi

**Upload Date**

12/28/2023 at 11:01 am

**File Name**

[0E7E3D04-C4DB-4D1B-BCA0-BC6...](#)



**Description**

Hooking-up New Heat Pump Unit

**Taken Date**

12/28/2023 at 07:21 am

**Uploaded By**


Frank Bondi

**Upload Date**

12/28/2023 at 07:21 am

**File Name**

[2676A1A0-A53E-468B-99B1-E5D...](#)



**Description**

Ryan Mech. bring Plumbing up to Second Floor

**Taken Date**

12/28/2023 at 11:00 am

**Uploaded By**

Frank Bondi

**Upload Date**

12/28/2023 at 11:00 am

**File Name**

[62E913F3-0C34-463C-A0E0-BED...](#)



**Description**

Painter has 1st coat of paint on.

**Taken Date**

12/27/2023 at 12:26 pm

**Uploaded By**


Frank Bondi

**Upload Date**

12/27/2023 at 12:26 pm

**File Name**

[F9DF9F86-371F-4682-B268-8884...](#)

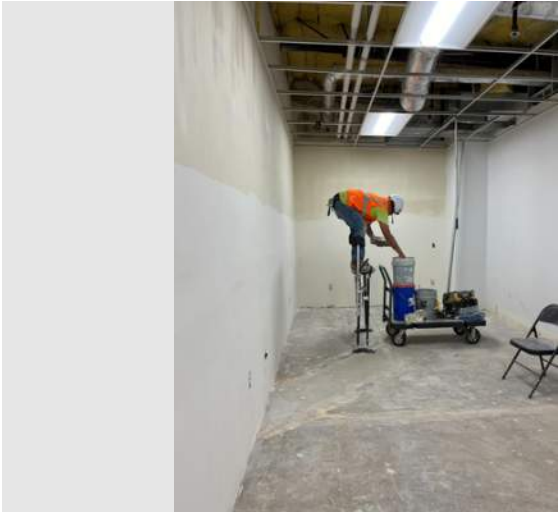

**Description**

Taper putting topcoat on. Teacher's Lounge

**Taken Date**

12/27/2023 at 12:03 pm

**Uploaded By**

Frank Bondi

**Upload Date**

12/27/2023 at 12:03 pm

**File Name**

[81542C96-0433-4DD1-A4D2-2B8...](#)



**Description**

**Taken Date**

12/21/2023 at 12:20 pm

**Uploaded By**

Frank Bondi

**Upload Date**

12/21/2023 at 12:20 pm

**File Name**

[77E10014-9A6F-49E8-946F-8C1A...](#)



**Description**

Second unit in place just need to fine tune it. C109

**Taken Date**

12/27/2023 at 11:56 am

**Uploaded By**

Frank Bondi

**Upload Date**

12/27/2023 at 12:03 pm

**File Name**

[F995A950-7937-4C7B-80E7-D7D...](#)



**Description**

**Taken Date**

12/21/2023 at 12:20 pm

**Uploaded By**

Frank Bondi

**Upload Date**

12/21/2023 at 12:20 pm

**File Name**

[404AEFB3-F562-4BBF-B319-7A8E...](#)



**Description**

**Taken Date**

12/21/2023 at 12:20 pm

**Uploaded By**


Frank Bondi

**Upload Date**

12/21/2023 at 12:20 pm

**File Name**

[22962927-8B10-4532-9A2E-69A6...](#)

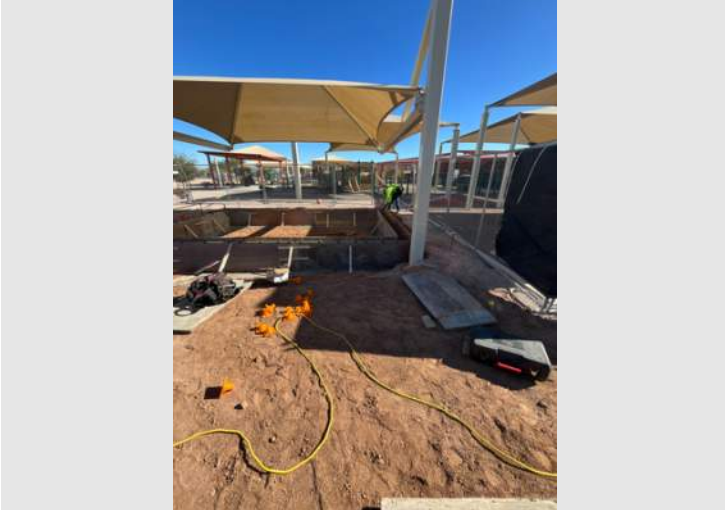

**Description**

**Taken Date**

12/21/2023 at 12:09 pm

**Uploaded By**

Frank Bondi

**Upload Date**

12/21/2023 at 12:09 pm

**File Name**

[1DAE1983-FA2E-48E2-BFC5-7192...](#)



**Description**

**Taken Date**

12/21/2023 at 12:15 pm

**Uploaded By**


Frank Bondi

**Upload Date**

12/21/2023 at 12:15 pm

**File Name**

[E43D6AE4-572D-4662-B0FA-091...](#)



**Description**

CJS mixing Grout for the Column Bases.

**Taken Date**

12/21/2023 at 11:03 am

**Uploaded By**

Frank Bondi

**Upload Date**

12/21/2023 at 11:03 am

**File Name**

[ACF12449-CE8F-4A5E-8146-C264...](#)



**Description**

RN Electric doing rough-in on the Second Floor of Building B.

**Taken Date**

12/21/2023 at 09:32 am

**Uploaded By**


Frank Bondi

**Upload Date**

12/21/2023 at 09:32 am

**File Name**

[6E2F3E43-CD19-4C88-ACB7-CAA...](#)

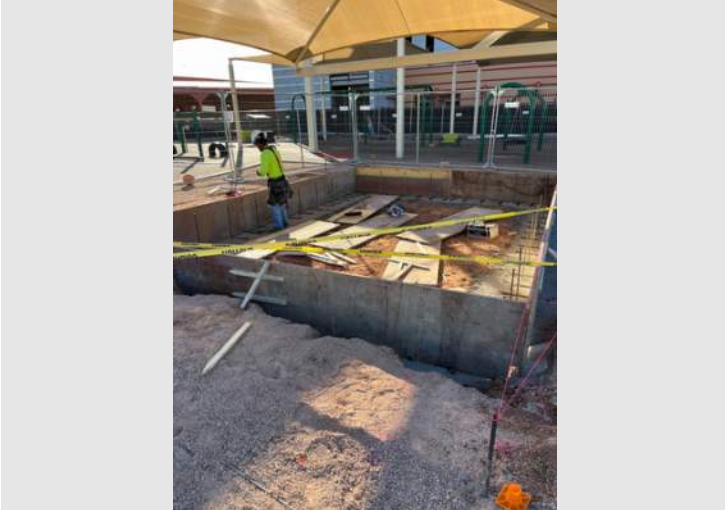

**Description**



**Description**

CJS setting Forms for the New Sandbox Curbing.

**Taken Date**

12/21/2023 at 09:29 am

**Uploaded By**


Frank Bondi

**Upload Date**

12/21/2023 at 09:30 am

**File Name**

[43B6A458-C509-4A32-9C78-136...](#)

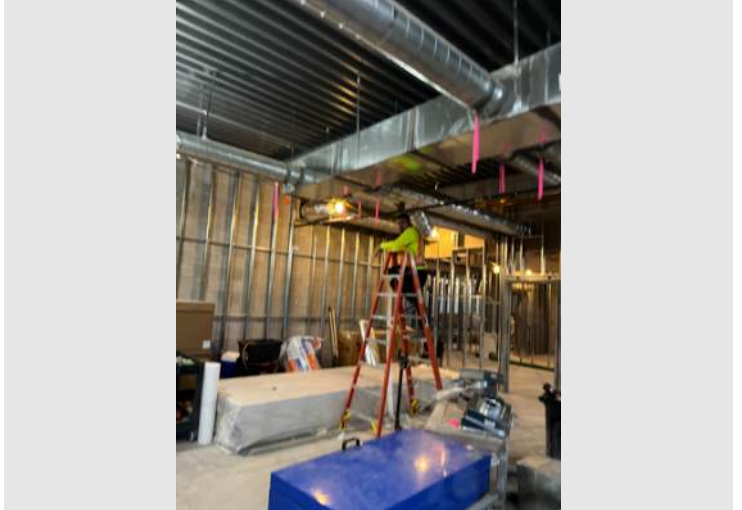

**Description**

**Taken Date**

12/21/2023 at 09:29 am

**Uploaded By**

Frank Bondi

**Upload Date**

12/21/2023 at 09:29 am

**File Name**

[0500D93E-BC0B-4A44-9D7F-DE2...](#)

**Taken Date**

12/20/2023 at 07:52 am

**Uploaded By**


Frank Bondi

**Upload Date**

12/20/2023 at 07:52 am

**File Name**

[814DA256-E58A-45DF-BB1C-4BA...](#)

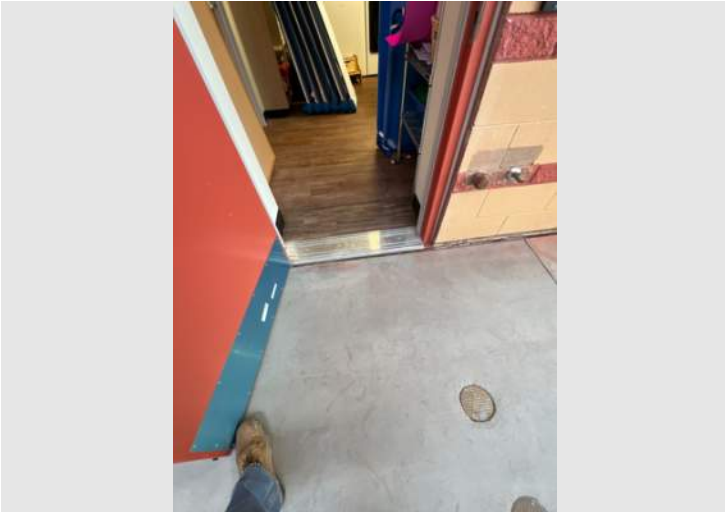

**Description**

**Taken Date**

12/19/2023 at 08:55 am

**Uploaded By**


Carlos Peralta

**Upload Date**

12/19/2023 at 09:15 am

**File Name**

[A175E918-75CA-44A6-B38A-10D...](#)



**Description**

Ductwork moving along on the second floor.

**Taken Date**

12/18/2023 at 02:40 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

12/18/2023 at 03:04 pm

**File Name**

[E5EE64B3-9866-4B24-A360-E142...](#)



**Description**

Footing poured for Sandbox Curbing.

**Taken Date**

12/18/2023 at 02:41 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

12/18/2023 at 03:08 pm

**File Name**

[DE740846-5E4F-4F53-B8B1-0AB8...](#)



**Description**

Footing Rebar for Sandbox curbing.

**Taken Date**

12/14/2023 at 02:17 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

12/14/2023 at 02:27 pm

**File Name**

[E1627F5D-EE7C-4E73-8A0A-84B...](#)



**Description**

Another angel of the Rebar.

**Taken Date**

12/14/2023 at 02:17 pm

**Uploaded By**


Carlos Peralta

**Upload Date**

12/14/2023 at 02:27 pm

**File Name**

[CAC508FA-E75F-4907-8D62-2051...](#)

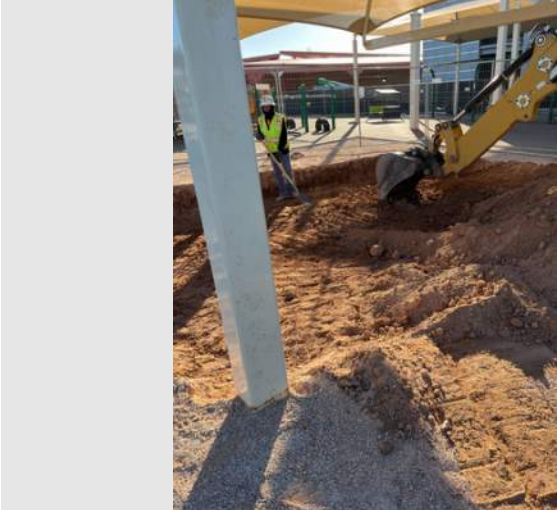

**Description**

Excavation continues.

**Taken Date**

12/13/2023 at 08:58 am

**Uploaded By**

Carlos Peralta

**Upload Date**

12/13/2023 at 10:11 am

**File Name**

[FD7E722F-F91D-499F-B130-6EE2...](#)



**Description**

Digging footings for perimeter curbing.

**Taken Date**

12/13/2023 at 12:15 pm

**Uploaded By**

Frank Bondi

**Upload Date**

12/13/2023 at 12:15 pm

**File Name**

[F81D7ECB-3F2E-4FCD-89B2-BD3...](#)



**Description**

New sand box shade complete.

**Taken Date**

12/13/2023 at 07:06 am

**Uploaded By**

Carlos Peralta

**Upload Date**

12/13/2023 at 07:43 am

**File Name**

[20231213\\_070650.jpg](#)



**Description**

East view elevator roof line.

**Taken Date**

**Uploaded By**


Carlos Peralta

**Upload Date**

12/13/2023 at 06:20 am

**File Name**

CF3B06F2-C472-434D-B9A7-CF1...



**Description**

Steel crew setting columns on the Northside.

**Taken Date**

12/08/2023 at 12:17 pm

**Uploaded By**

Frank Bondi

**Upload Date**

12/08/2023 at 12:17 pm

**File Name**

0D23C673-95D8-42F3-9B32-C8B...



**Description**

Canopy Roof Assembly is set.

**Taken Date**

12/12/2023 at 11:17 am

**Uploaded By**

Frank Bondi

**Upload Date**

12/12/2023 at 12:14 pm

**File Name**

91DFA031-6403-41FA-BDB8-5FD...



**Description**

Door Frame set at Teacher's Lounge.

**Taken Date**

12/07/2023 at 03:59 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

12/08/2023 at 12:32 pm

**File Name**

973AAE14-95A4-482E-83C3-8AA...



**Description**

Boiler manifold and pump motor installed.

**Taken Date**

12/07/2023 at 02:10 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

12/07/2023 at 03:37 pm

**File Name**

[A9E64F7A-FF10-486B-B092-3EBC...](#)



**Description**

Rebar Cage in place before concrete pour.

**Taken Date**

12/07/2023 at 12:45 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

12/07/2023 at 01:28 pm

**File Name**

[A9BAE2B6-1512-4511-B5CA-407...](#)



**Description**

One for each column.

**Taken Date**

12/07/2023 at 12:46 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

12/07/2023 at 01:24 pm

**File Name**

[2183ED84-9322-4F23-BAAD-14B...](#)



**Description**

Workers installing Shark Skin barrier over exterior before siding is installed.

**Taken Date**

12/07/2023 at 09:55 am

**Uploaded By**


Carlos Peralta

**Upload Date**

12/07/2023 at 10:00 am

**File Name**

[AB6AF779-19BF-4D3E-9EAE-225...](#)



**Description**

Another angel of railing at Teacher's Lounge.

**Taken Date**

12/07/2023 at 09:52 am

**Uploaded By**

Carlos Peralta

**Upload Date**

12/07/2023 at 10:00 am

**File Name**

[1B0001DF-E03D-4B13-AEAD-827...](#)



**Description**

Teachers lounge concrete pour in progress.

**Taken Date**

12/05/2023 at 06:13 am

**Uploaded By**


Frank Bondi

**Upload Date**

12/05/2023 at 06:13 am

**File Name**

[95CA248A-35FD-46AF-8F6B-2BA...](#)



**Description**

Teachers lounge broom finish in progress.

**Taken Date**

12/05/2023 at 10:10 am

**Uploaded By**


Carlos Peralta

**Upload Date**

12/05/2023 at 02:35 pm

**File Name**

[2C6F7E6E-FEB4-4BE5-BFC4-1A72...](#)



**Description**

Pumping concrete at teachers lounge.

**Taken Date**

12/05/2023 at 05:43 am

**Uploaded By**

Frank Bondi

**Upload Date**

12/05/2023 at 05:43 am

**File Name**

[8275FF34-6321-4B95-B6B2-5749...](#)



Description

**Taken Date**  
 12/01/2023 at 09:35 am

**Upload Date**  
 12/01/2023 at 09:59 am

**Uploaded By**  
 Carlos Peralta

**File Name**  
[9BA24FD4-A2AF-4D2B-9B01-FFD...](#)



Description

**Taken Date**  
 12/01/2023 at 08:15 am

**Upload Date**  
 12/01/2023 at 08:15 am

**Uploaded By**  
 Frank Bondi

**File Name**  
[9FD4787B-548B-4039-821F-87EB...](#)

# SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

## Attachments:

---

Item/s
1. None
