



Salt River Pima-Maricopa Indian Community

10005 East Osborn Road • Scottsdale, Arizona 85256

Phone (480) 362-7700 • Fax (480) 362-5597

MONTHLY PROJECT PROGRESS UPDATE

Project: ECEC Classroom and Parking Expansion

Issued Date: **October 4, 2023** | **October-2023 UPDATE**

Distribution:

	Name	Department/ Company
X	Tami Brungard	ECEC – Edu Leader
X	Lekisha Morris	ECEC
X	Barbara White	ECEC
X	Melody Herne	Act. Superintendent
X	Tate Walker	Public Relations Dir.
X	Deanna Scabby	Edu. Board./ Council
X	Mikah Carlos	Community Council
X	Pamela Prasher	ECEC

	Name	Department/ Company
X	Kimberly Manuel	ECEC – Policy Council
X	Carmen Briones	ECEC – Policy Council
X	Jennifer Correa	ECEC – Policy Council
X	Brittany Barranca	ECEC – Policy Council
X	Frank Perez	ECEC – Policy Council
X	Rene Uriarte	ECEC – Policy Council
X	Symone Kann	ECEC – Policy Council
X	Felicia Toya	ECEC – Policy Council

Work Completed:


Items

1. Group #2 Classroom renovation started (A-154, A-139, B-135, C-102). Tentative completion 10/20/23.
2. Building B 2nd Floor concrete poured.
3. Existing parking lot new light pole install completed.
4. Mechanical Yard CMU wall completion.
5. Building automation system new cabling installed.

Work anticipated in the next month:

1. Group #3 Classroom renovation tentative start end of the month (A-131, A-120, B-142, C-108).
2. Building B Addition, mechanical mezzanine level and roof steel decking install. Mechanical mezzanine concrete pour.
3. Building B 1st Floor roof membrane install, 2nd Floor Standing seam metal roof start by end of the month.
4. On-Going mechanical, plumbing and electrical rough-in work.
5. Infant playground area fencing and rubber play surface install.
6. Building D Staff Lounge renovation finishes complete by end of month.

Project Schedule | Three Week Look Ahead

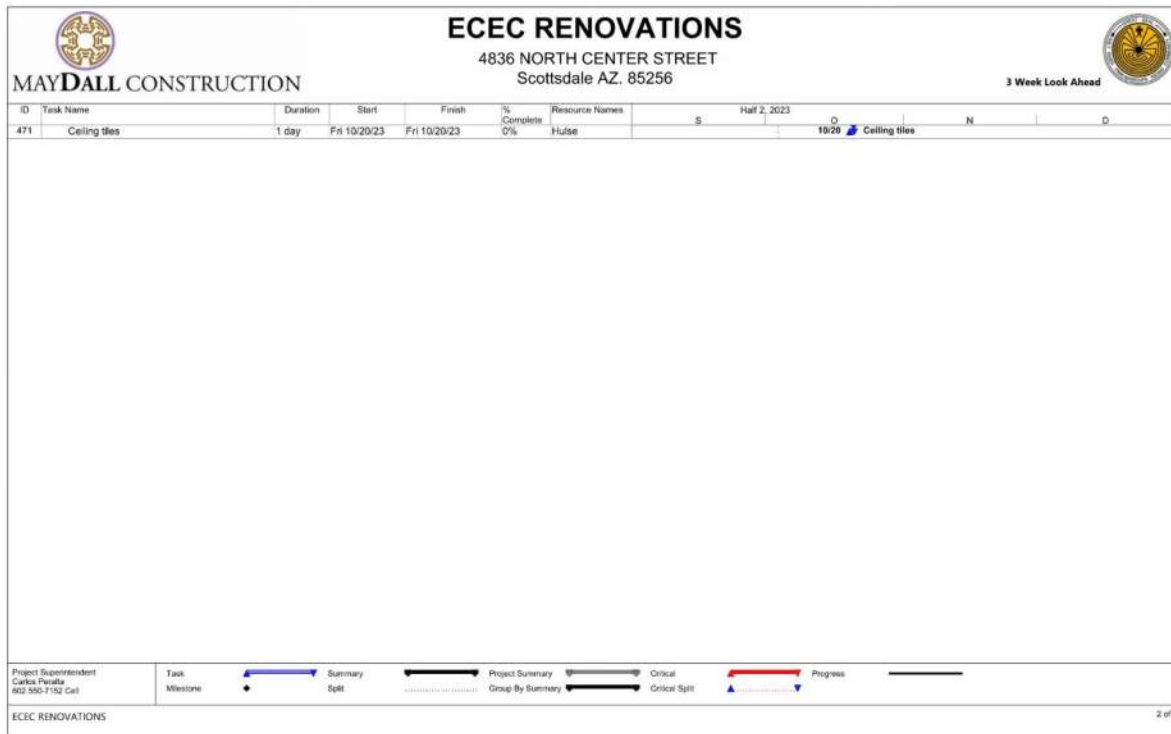

SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Progress Photos:

See attached.



Description

Playground 3 complete.

Taken Date

09/29/2023 at 02:08 pm

Uploaded By

Carlos Peralta

Upload Date

09/29/2023 at 03:20 pm

File Name

[6CB18E44-2BF0-494A-B8EA-8AC...](#)



Description

Barricade in teachers lounge installed.

Taken Date

09/29/2023 at 06:30 am

Uploaded By

Carlos Peralta

Upload Date

09/29/2023 at 03:20 pm

File Name

[D8C8B020-8929-47BD-AD15-970...](#)



Description

Playground 3 under Ramp rubber membrane complete.

Taken Date

09/29/2023 at 02:08 pm

Uploaded By


Carlos Peralta

Upload Date

09/29/2023 at 03:20 pm

File Name

[CC2E13BD-B627-4907-A5CE-433...](#)

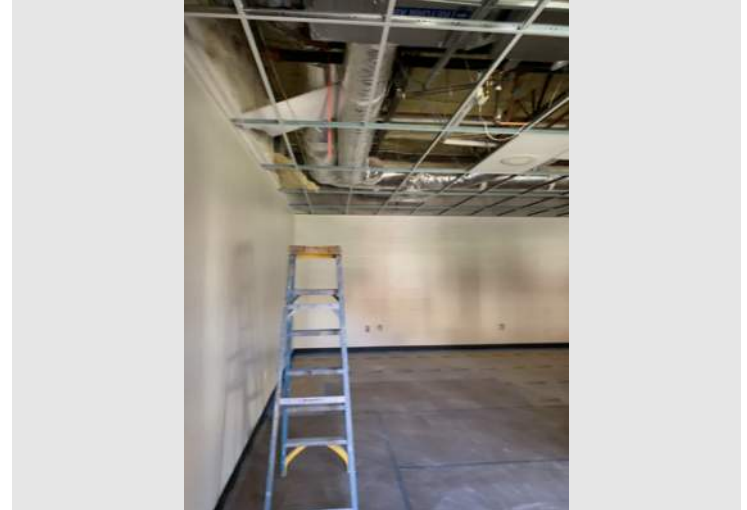

Description

Room A-139 painted

Taken Date

09/28/2023 at 02:00 pm

Uploaded By

Cameron Vildosola

Upload Date

09/29/2023 at 08:49 am

File Name

[A9C518FF-1DCF-49EA-81C0-0AD...](#)



Description

Ceiling grid patch back complete.

Taken Date

09/28/2023 at 02:00 pm

Uploaded By


Cameron Vildosola

Upload Date

09/29/2023 at 08:49 am

File Name

[7EDFD0DD-6150-4693-8407-A5D...](#)

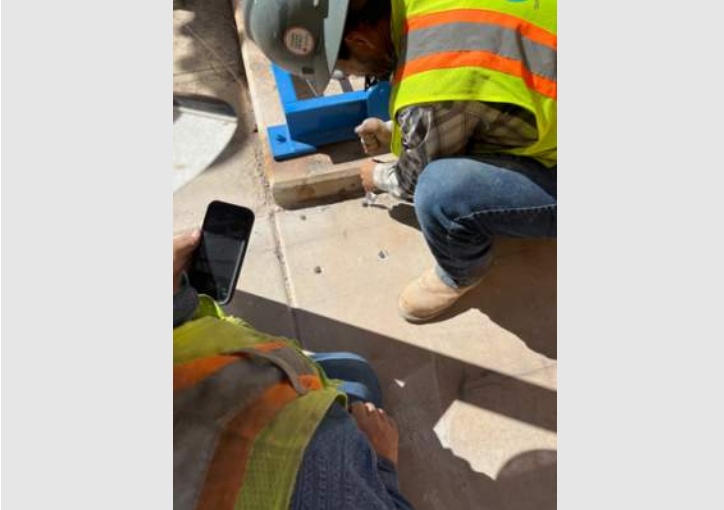

Description

Cleaning holes for pipe stand at mechanical yard for overhead water lines to new chiller.

Taken Date

09/28/2023 at 01:45 pm

Uploaded By

Carlos Peralta

Upload Date

09/28/2023 at 01:45 pm

File Name

[0AF64F47-6DCD-40DF-9EDC-A60...](#)



Description

Painting at classrooms all complete.

Taken Date

09/28/2023 at 02:00 pm

Uploaded By


Cameron Vildosola

Upload Date

09/29/2023 at 08:49 am

File Name

[F65455D4-1C04-4461-BE5A-0C9F...](#)

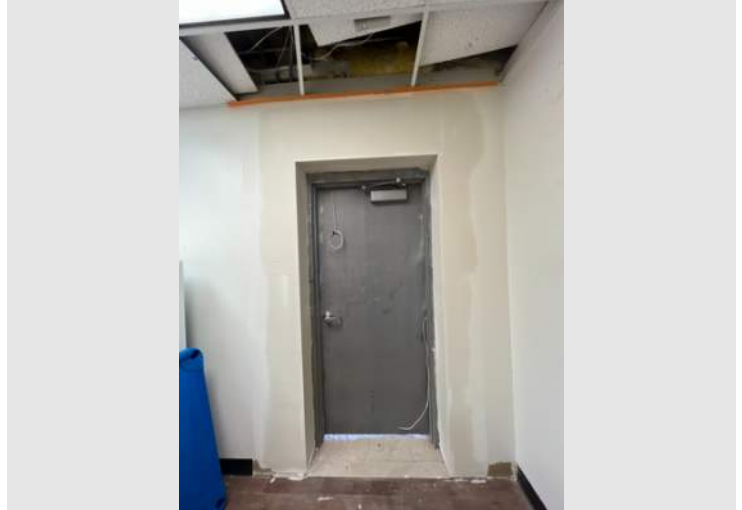

Description

Laundry Room C-110 Drywall repairs in progress.

Taken Date

09/28/2023 at 12:28 pm

Uploaded By


Carlos Peralta

Upload Date

09/28/2023 at 01:45 pm

File Name

[227DA3EF-11E4-4C41-AADE-A1C...](#)

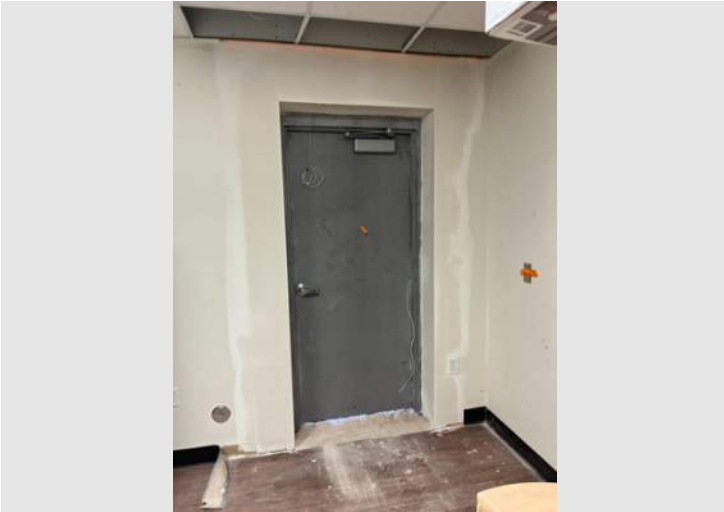

Description

Laundry Room drywall repairs C-103

Taken Date

09/28/2023 at 12:26 pm

Uploaded By

Carlos Peralta

Upload Date

09/28/2023 at 01:45 pm

File Name

78DF1247-1761-4454-88C8-3754...



Description

Steel for east stairwell storefront

Taken Date

09/28/2023 at 12:16 pm

Uploaded By

Carlos Peralta

Upload Date

09/28/2023 at 12:23 pm

File Name

6A03F2C0-7D78-4454-87AF-3AB...



Description

New barricades deliver and installed.

Taken Date

09/28/2023 at 12:24 pm

Uploaded By

Carlos Peralta

Upload Date

09/28/2023 at 01:44 pm

File Name

9B618974-4251-4B26-A0A4-09D...



Description

Light poles assembly complete for ECEC

Taken Date

09/28/2023 at 12:15 pm

Uploaded By


Carlos Peralta

Upload Date

09/28/2023 at 12:23 pm

File Name

0E5834AE-31A6-4139-9060-F599...

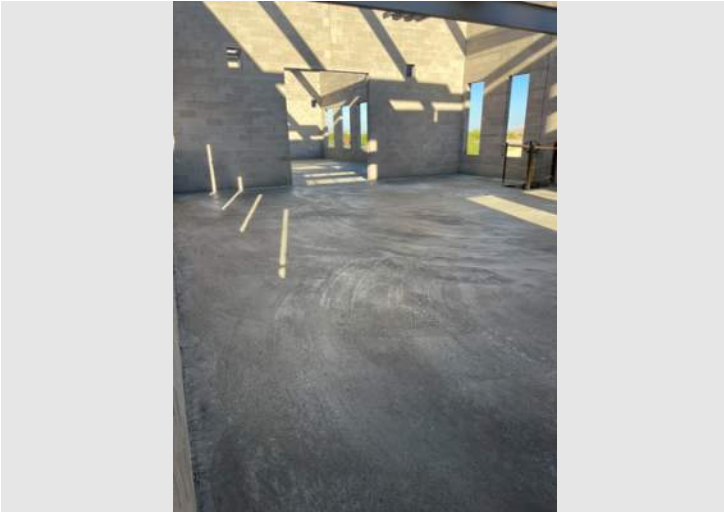

Description

Second floor concrete complete

Taken Date

09/28/2023 at 07:58 am

Uploaded By

Carlos Peralta

Upload Date

09/28/2023 at 07:59 am

File Name

[02226886-AC79-443D-A6E3-90D...](#)



Description

New light poles install and energize in progress.

Taken Date

09/28/2023 at 05:54 am

Uploaded By

Carlos Peralta

Upload Date

09/28/2023 at 07:09 am

File Name

[B48DCEE4-F73E-4770-85BA-B8F8...](#)



Description

Bus drop off lighting complete and energize.

Taken Date

09/28/2023 at 05:54 am

Uploaded By

Carlos Peralta

Upload Date

09/28/2023 at 07:09 am

File Name

[D068ADC9-966A-4C76-9D24-09A...](#)



Description

Heat pumps at bldg. B install in progress.

Taken Date

09/27/2023 at 02:44 pm

Uploaded By

Carlos Peralta

Upload Date

09/27/2023 at 02:55 pm

File Name

[47848358-6F8F-4667-B979-184F...](#)



Description

Texture complete at all classroom renovation.

Taken Date

09/27/2023 at 11:09 am

Uploaded By

Carlos Peralta

Upload Date

09/27/2023 at 11:59 am

File Name

[9A4081B0-DEF8-40C6-A847-8D1...](#)



Description

Split face block repairs complete.

Taken Date

09/27/2023 at 09:29 am

Uploaded By

Carlos Peralta

Upload Date

09/27/2023 at 11:53 am

File Name

[F151FF5D-B638-401B-833F-BE58...](#)



Description

Ceiling grid repairs all complete at all classrooms renovation

Taken Date

09/27/2023 at 11:09 am

Uploaded By


Carlos Peralta

Upload Date

09/27/2023 at 11:58 am

File Name

[D50C356D-58ED-4495-90F9-A74...](#)

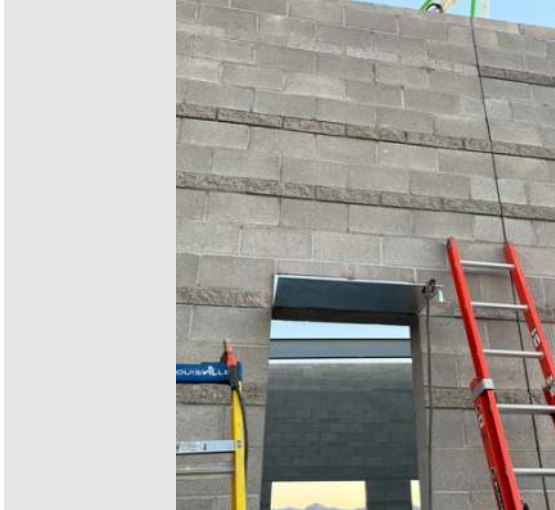

Description

Steel hade install complete South side.

Taken Date

09/27/2023 at 06:22 am

Uploaded By


Carlos Peralta

Upload Date

09/27/2023 at 08:52 am

File Name

[CECA53C1-23E8-4E46-AB79-F25...](#)

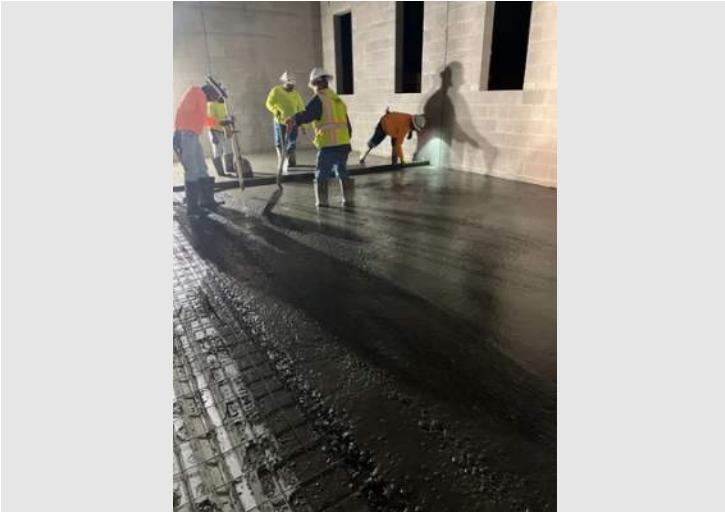

Description

Second floor concrete pour in progress bldg.B

Taken Date

09/27/2023 at 04:39 am

Uploaded By

Carlos Peralta

Upload Date

09/27/2023 at 05:08 am

File Name

[D480DB68-8DDB-4D15-987B-4B...](#)



Description

Bum extended ready for pumping.

Taken Date

09/27/2023 at 04:36 am

Uploaded By

Carlos Peralta

Upload Date

09/27/2023 at 05:04 am

File Name

[443C5CF7-86A6-431C-ACEC-2CB...](#)



Description

Concrete pump ready for concrete pour.

Taken Date

09/27/2023 at 04:36 am

Uploaded By

Carlos Peralta

Upload Date

09/27/2023 at 05:02 am

File Name

[B5762F8E-E8A7-4856-B68E-E485...](#)



Description

Taken Date

09/26/2023 at 12:40 pm

Uploaded By


Carlos Peralta

Upload Date

09/26/2023 at 12:41 pm

File Name

[61427935-7DDC-4BD3-A3BC-C76...](#)

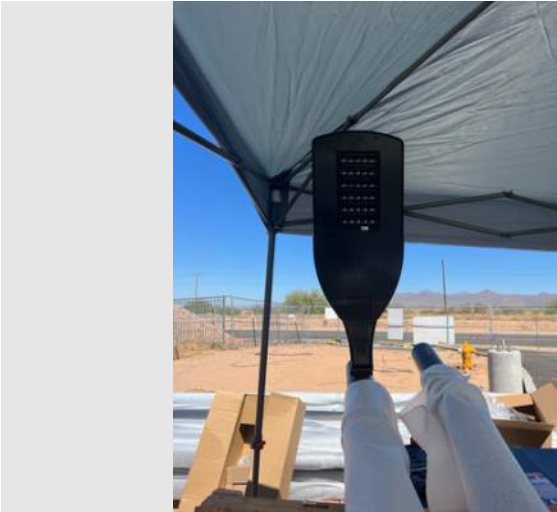

Description

Light poles heads install in progress.

Taken Date

09/25/2023 at 11:23 am

Uploaded By


Carlos Peralta

Upload Date

09/25/2023 at 11:37 am

File Name

[12EDE7BB-DA4B-45DE-8D57-A76...](#)

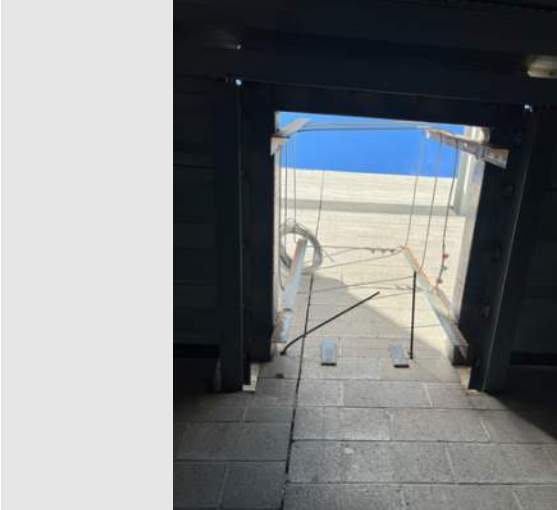

Description

Taken Date

09/22/2023 at 02:16 pm

Uploaded By

Carlos Peralta

Upload Date

09/22/2023 at 02:31 pm

File Name

[E045AFA4-12E7-4CFD-95E1-DF2F...](#)



Description

Light poles delivery

Taken Date

09/25/2023 at 09:03 am

Uploaded By

Carlos Peralta

Upload Date

09/25/2023 at 09:31 am

File Name

[5129F377-119E-4359-9316-7F92...](#)



Description

Taken Date

09/22/2023 at 02:15 pm

Uploaded By

Carlos Peralta

Upload Date

09/22/2023 at 02:31 pm

File Name

[8AF3E875-BF53-4A99-B62E-5826...](#)



Description

Canopy columns on the north side.

Taken Date

09/22/2023 at 12:49 pm

Uploaded By

Carlos Peralta

Upload Date

09/22/2023 at 12:49 pm

File Name

[D14B34CC-5006-49F6-9C9D-0E3...](#)



Description

Duct install complete Classroom A 139

Taken Date

09/22/2023 at 12:44 pm

Uploaded By

Carlos Peralta

Upload Date

09/22/2023 at 12:48 pm

File Name

[DC387CE1-66D1-47FA-9095-2F77...](#)



Description

Bldg. B Overhead MPE in progress.

Taken Date

09/22/2023 at 12:48 pm

Uploaded By

Carlos Peralta

Upload Date

09/22/2023 at 12:49 pm

File Name

[055AEEF4-85BD-41CE-9F00-19A...](#)



Description

Painting protection installs in progress in all classrooms.

Taken Date

09/22/2023 at 12:43 pm

Uploaded By

Carlos Peralta

Upload Date

09/22/2023 at 12:48 pm

File Name

[BE780AF8-7103-4246-9D0B-078...](#)



Description

Canopy columns on the south side.

Taken Date

09/22/2023 at 12:42 pm

Uploaded By


Carlos Peralta

Upload Date

09/22/2023 at 12:48 pm

File Name

[EE1B0AF8-F952-4CD6-A59E-70B...](#)

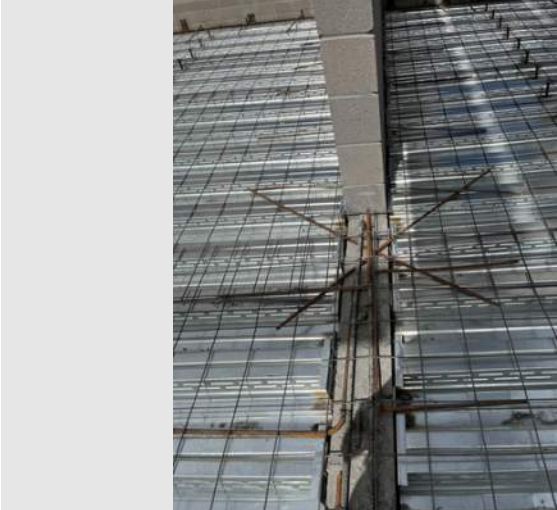

Description

Second walk thru,tours the east

Taken Date

09/22/2023 at 12:39 pm

Uploaded By


Carlos Peralta

Upload Date

09/22/2023 at 12:41 pm

File Name

[9266CD0E-CD3C-4ECC-9E51-2E8...](#)

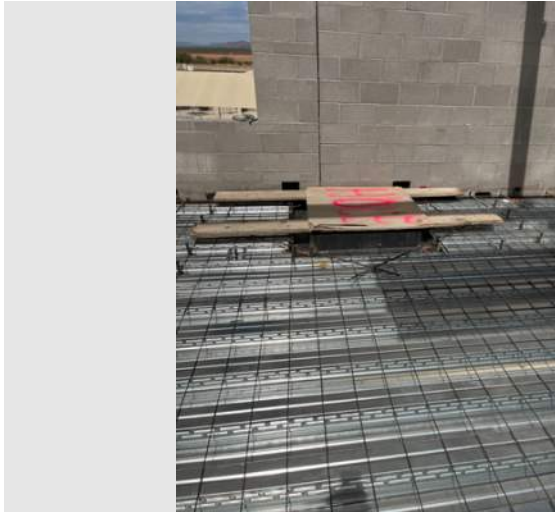

Description

Bent plate install complete at duct shaft on second floor.

Taken Date

09/22/2023 at 12:40 pm

Uploaded By


Carlos Peralta

Upload Date

09/22/2023 at 12:41 pm

File Name

[769A406E-CDD7-4B72-8711-628...](#)

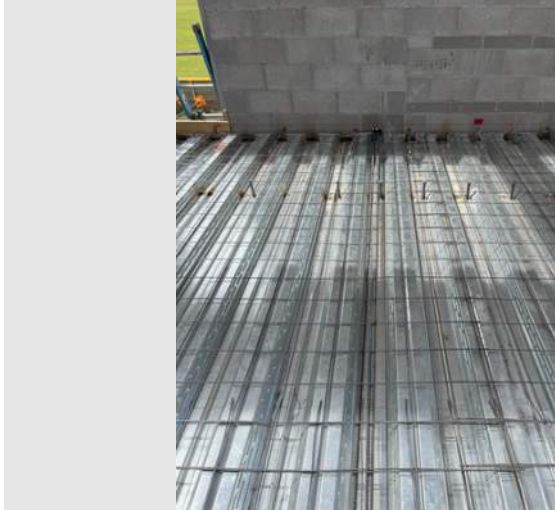

Description

Rebar on the north to tie in floor to stair landing.

Taken Date

09/22/2023 at 12:39 pm

Uploaded By

Carlos Peralta

Upload Date

09/22/2023 at 12:41 pm

File Name

[837A83C2-D2C0-415E-AB40-1BC...](#)



Description

concrete band install 2nd section

Taken Date

09/21/2023 at 04:46 am

Uploaded By


Cameron Vildosola

Upload Date

09/21/2023 at 05:25 am

File Name

[0A32A14B-AA03-411D-8B1F-3C2...](#)

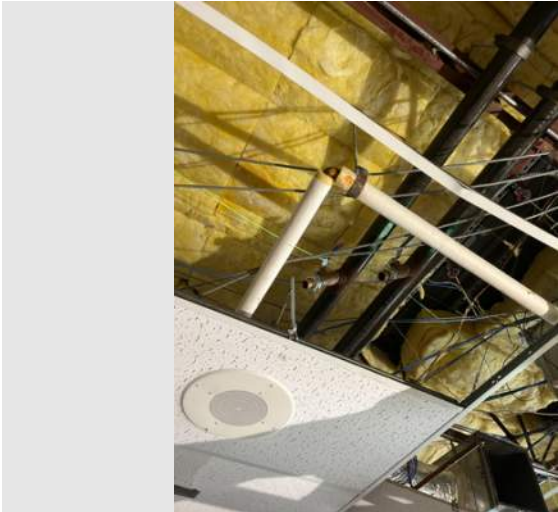

Description

Above ceiling valves copper fittings install ready for heat pump connection.

Taken Date

09/20/2023 at 11:30 am

Uploaded By

Carlos Peralta

Upload Date

09/20/2023 at 11:42 am

File Name

[A87DF189-F550-4656-9DE0-568...](#)



Description

concrete band install 1st section

Taken Date

09/21/2023 at 04:45 am

Uploaded By

Cameron Vildosola

Upload Date

09/21/2023 at 05:25 am

File Name

[8F9219A3-F201-4EB5-AADF-2F44...](#)



Description

column install southeast side

Taken Date

09/20/2023 at 09:00 am

Uploaded By

Cameron Vildosola

Upload Date

09/25/2023 at 08:13 am

File Name

[61A8B5E0-C327-42CE-9BBC-41D...](#)



Description

Canopy columns install in progress.

Taken Date

09/20/2023 at 08:07 am

Uploaded By


Carlos Peralta

Upload Date

09/20/2023 at 08:51 am

File Name

[781CE054-4A8F-41F4-8A09-25ED...](#)

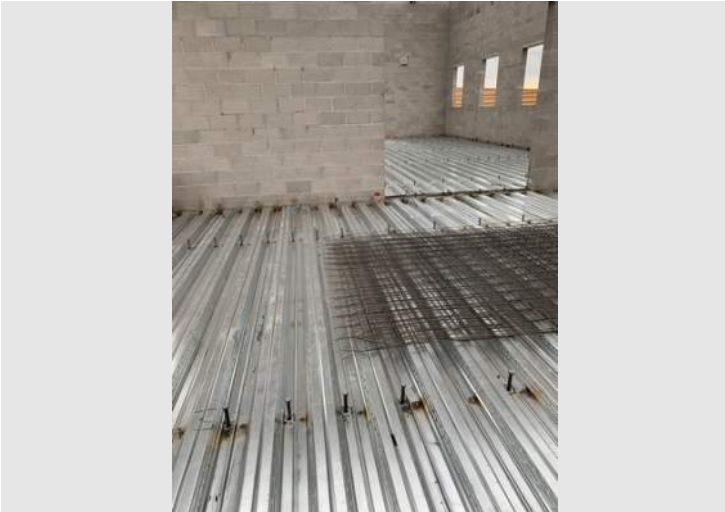

Description

wire mesh install

Taken Date

09/20/2023 at 07:28 am

Uploaded By


Cameron Vildosola

Upload Date

09/21/2023 at 07:25 am

File Name

[635C4A90-8501-4B87-9C37-3B9...](#)

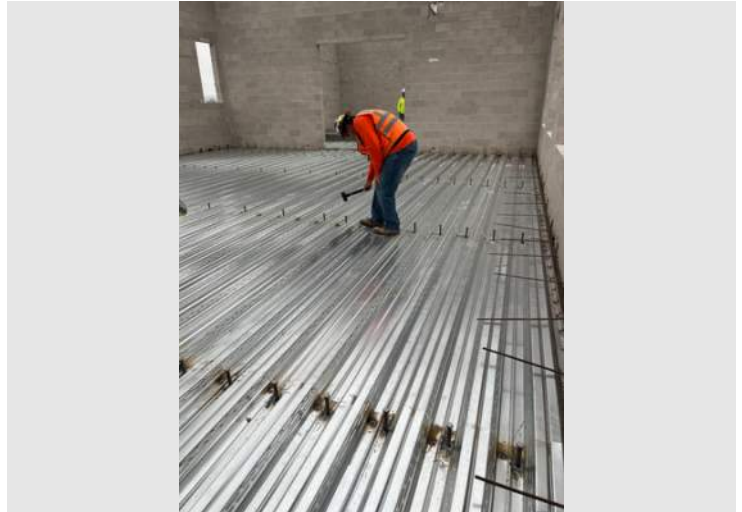

Description

Ninyo and moore

Taken Date

09/20/2023 at 07:30 am

Uploaded By


Carlos Peralta

Upload Date

09/20/2023 at 08:51 am

File Name

[B082A397-0467-4768-9E9B-14E6...](#)

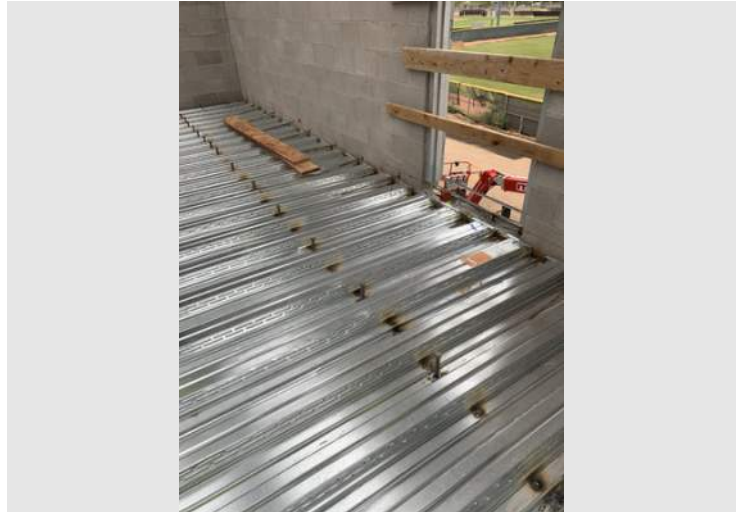

Description

Nelson studs passing inspection

Taken Date

09/20/2023 at 07:28 am

Uploaded By

Cameron Vildosola

Upload Date

09/25/2023 at 08:13 am

File Name

[6B20A67F-8B71-4665-9AA2-67E...](#)



Description

Bent plate delivery.

Taken Date

09/19/2023 at 09:56 am

Uploaded By


Carlos Peralta

Upload Date

09/19/2023 at 10:05 am

File Name

[A61EB86D-20E7-4682-9AAA-910...](#)

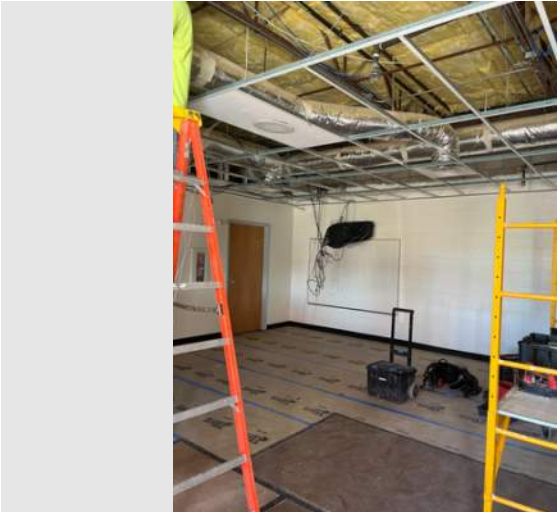

Description

Taken Date

09/19/2023 at 09:22 am

Uploaded By

Carlos Peralta

Upload Date

09/19/2023 at 10:04 am

File Name

[5B805930-645F-4477-82DC-88E1...](#)



Description

Curve Metal Panels on site.

Taken Date

09/19/2023 at 09:56 am

Uploaded By

Carlos Peralta

Upload Date

09/19/2023 at 10:05 am

File Name

[4366B4DA-244B-40F3-A759-63A...](#)



Description

Sampling station Complete.

Taken Date

09/19/2023 at 09:16 am

Uploaded By


Carlos Peralta

Upload Date

09/19/2023 at 09:17 am

File Name

[9701ABA2-9128-44F6-BF96-5BF5...](#)

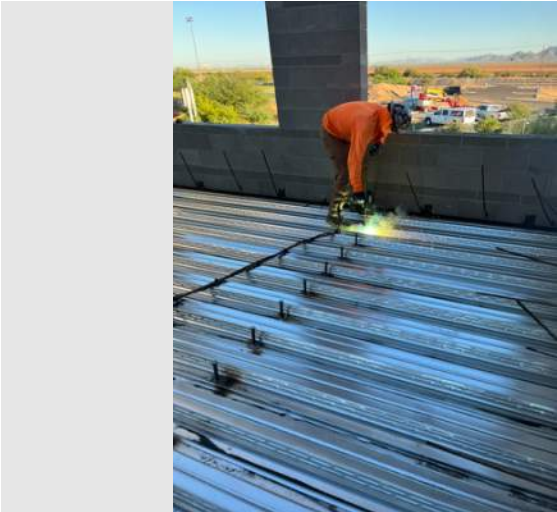

Description

Nelson studs welding in progress.

Taken Date

09/19/2023 at 07:08 am

Uploaded By


Carlos Peralta

Upload Date

09/19/2023 at 09:16 am

File Name

[7CAFA9C9-8B74-49C6-A840-A44...](#)

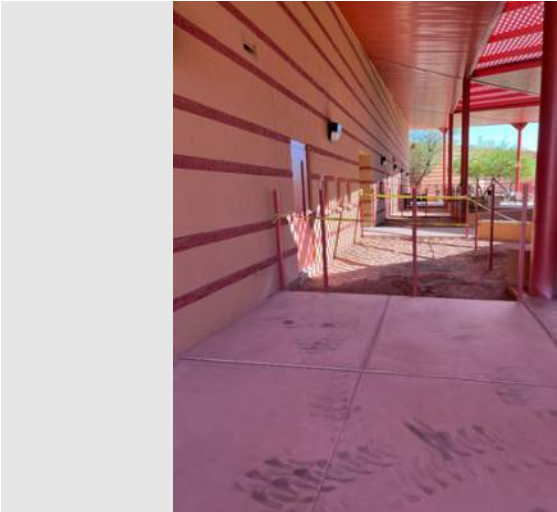

Description

Infant area fence post install complete.

Taken Date

09/15/2023 at 10:12 am

Uploaded By

Carlos Peralta

Upload Date

09/15/2023 at 10:23 am

File Name

[1EB55CBC-335B-418A-A261-49C...](#)



Description

Forming for concrete Ban in progress at infant area.

Taken Date

09/18/2023 at 11:12 am

Uploaded By


Carlos Peralta

Upload Date

09/18/2023 at 11:46 am

File Name

[BFD1CD5C-2679-4D63-922B-3D6...](#)

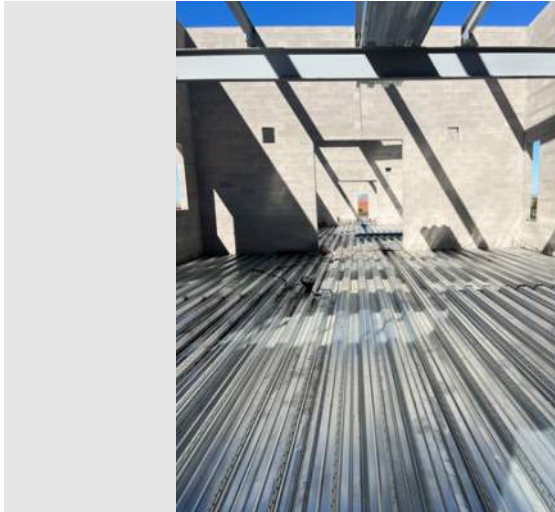

Description

Second floor decking install in progress.

Taken Date

09/15/2023 at 09:37 am

Uploaded By


Carlos Peralta

Upload Date

09/15/2023 at 10:16 am

File Name

[DC9FBC3E-16BA-476B-969B-34C...](#)

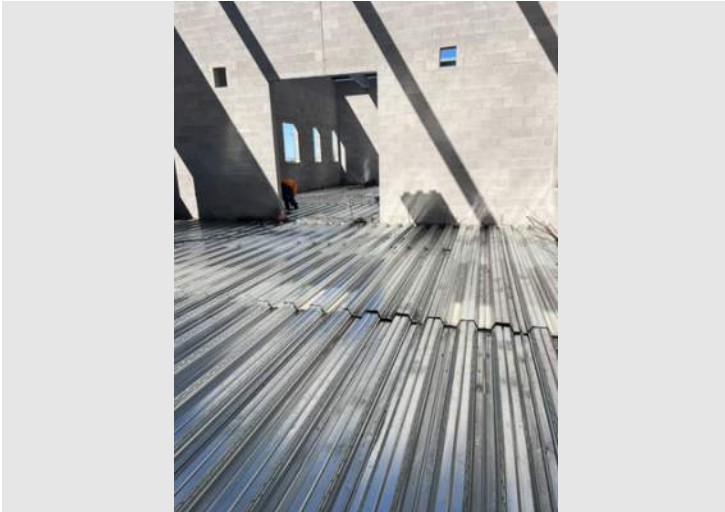

Description

Decking welding in progress.

Taken Date

09/15/2023 at 09:37 am

Uploaded By


Carlos Peralta

Upload Date

09/15/2023 at 10:12 am

File Name

[94F75833-D5F2-475C-8D86-444F...](#)

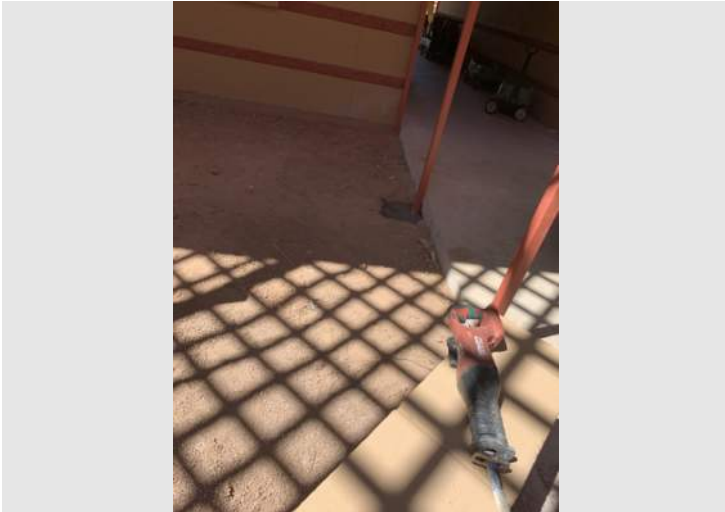

Description

Installed fence post between laundry rooms

Taken Date

09/14/2023 at 01:15 pm

Uploaded By


Cameron Vildosola

Upload Date

09/14/2023 at 02:05 pm

File Name

[B64FA031-AC4D-416A-BCF7-F149...](#)

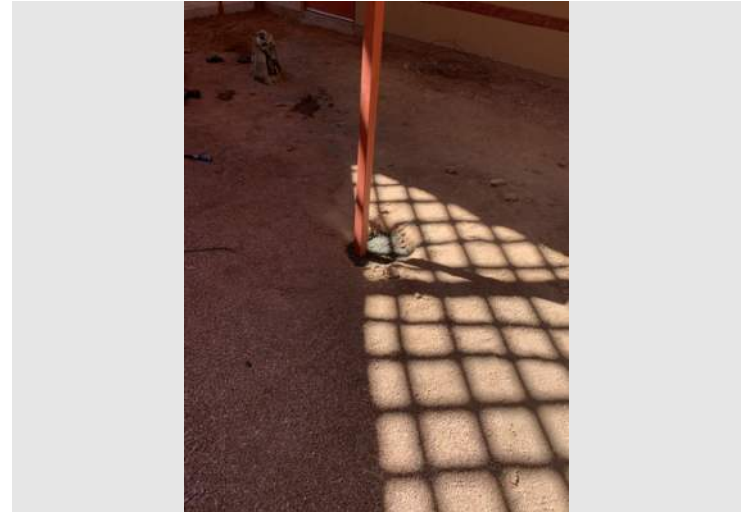

Description

Fence post installed left of laundry ramp

Taken Date

09/14/2023 at 01:15 pm

Uploaded By

Cameron Vildosola

Upload Date

09/14/2023 at 02:05 pm

File Name

[EAD8C4A-D6D9-45EE-BA52-921...](#)



Description

APS heat pump plumbing install in progress

Taken Date

09/14/2023 at 08:31 am

Uploaded By

Carlos Peralta

Upload Date

09/14/2023 at 08:58 am

File Name

[7776070A-3018-41B0-8ADE-2EB...](#)



Description

Decking install in progress

Taken Date

09/14/2023 at 08:30 am

Uploaded By

Carlos Peralta

Upload Date

09/14/2023 at 08:43 am

File Name

[6EB82069-8419-4610-B41B-E029...](#)



Description

Blank plate ceiling tile half-demoded in A-139

Taken Date

09/14/2023 at 07:24 am

Uploaded By


Cameron Vildosola

Upload Date

09/14/2023 at 07:32 am

File Name

[B8D6EAC7-1646-4CE0-BAE8-11E...](#)

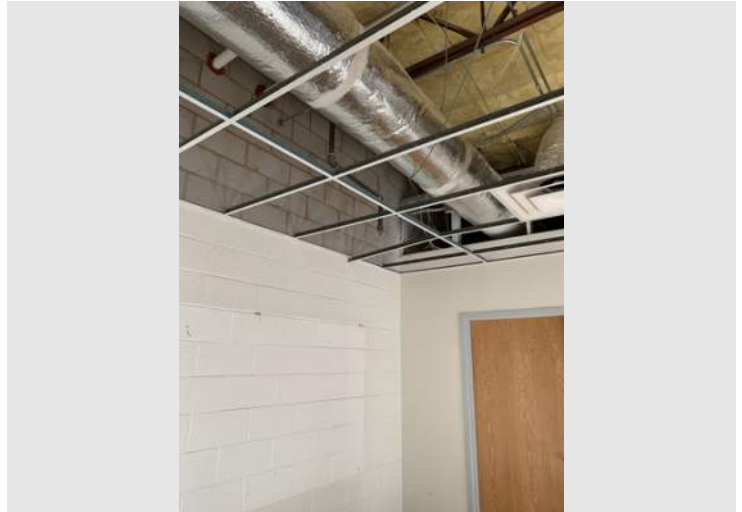

Description

A-139 ceiling tile demo, back right corner

Taken Date

09/14/2023 at 07:24 am

Uploaded By


Cameron Vildosola

Upload Date

09/14/2023 at 07:32 am

File Name

[65438D14-3B50-4B38-8474-EE7...](#)

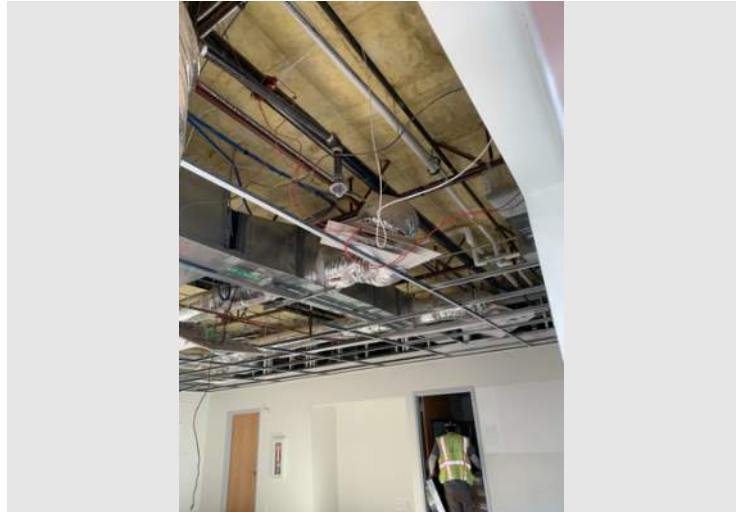

Description

Diffuser set on ceiling grid in A-139

Taken Date

09/14/2023 at 07:24 am

Uploaded By

Cameron Vildosola

Upload Date

09/14/2023 at 07:33 am

File Name

[27F35485-EE1D-4CC3-BFB7-75A...](#)



Description

Floor protection A-139

Taken Date

09/14/2023 at 07:24 am

Uploaded By

Cameron Vildosola

Upload Date

09/14/2023 at 07:32 am

File Name

[89A5B296-13F7-49EF-BF93-FBE6...](#)



Description

Floor protection A-139 with vent filter on the floor

Taken Date

09/14/2023 at 07:24 am

Uploaded By

Cameron Vildosola

Upload Date

09/14/2023 at 07:32 am

File Name

[C6801437-51B2-4CEB-A0A2-E67...](#)



Description

Floor protection A-139

Taken Date

09/14/2023 at 07:24 am

Uploaded By


Cameron Vildosola

Upload Date

09/14/2023 at 07:33 am

File Name

[EFF4BF95-5C4D-41C9-AE62-DBE...](#)

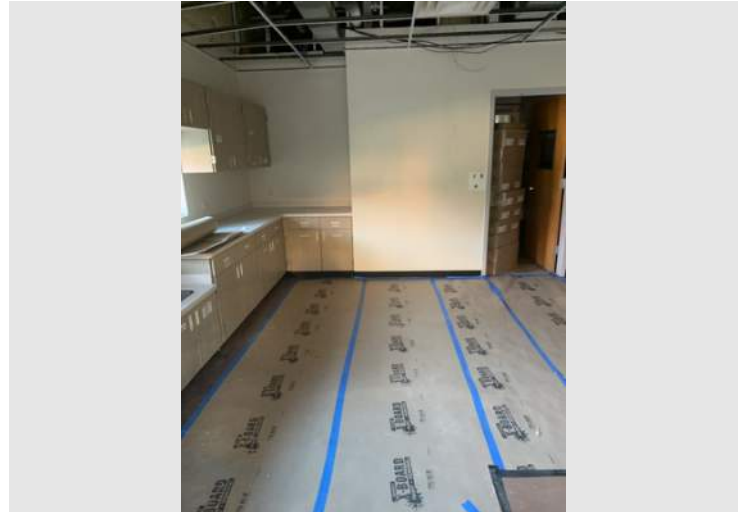

Description

Floor protection and ceiling tile delivery in A-139

Taken Date

09/14/2023 at 07:21 am

Uploaded By


Cameron Vildosola

Upload Date

09/14/2023 at 07:45 am

File Name

[A80A2121-22FE-46F5-AC53-BF79...](#)

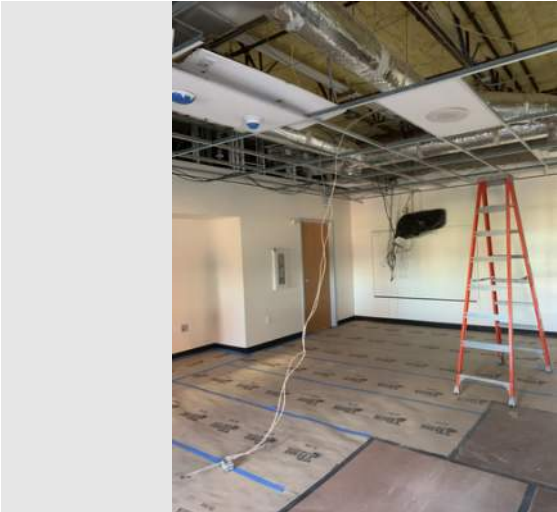

Description

Projector covering in A-154

Taken Date

09/14/2023 at 07:21 am

Uploaded By


Cameron Vildosola

Upload Date

09/14/2023 at 07:49 am

File Name

[198731E4-D032-4FC7-B610-7F8A...](#)

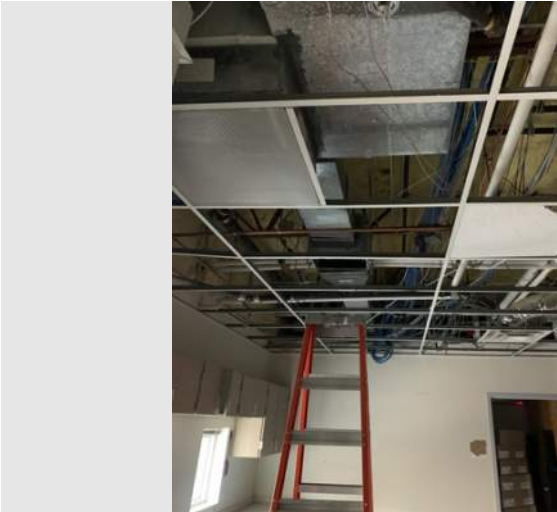

Description

Ceiling tile demo B-135

Taken Date

09/14/2023 at 07:17 am

Uploaded By


Cameron Vildosola

Upload Date

09/14/2023 at 08:27 am

File Name

[2C32F411-0EA0-441E-886C-7069...](#)

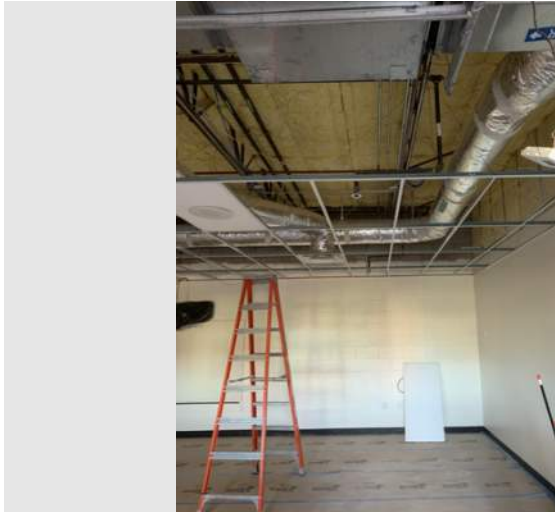

Description

Demo ceiling tile in A-154

Taken Date

09/14/2023 at 07:21 am

Uploaded By


Cameron Vildosola

Upload Date

09/14/2023 at 07:49 am

File Name

[296B7B0D-8ADA-45AA-98C4-757...](#)

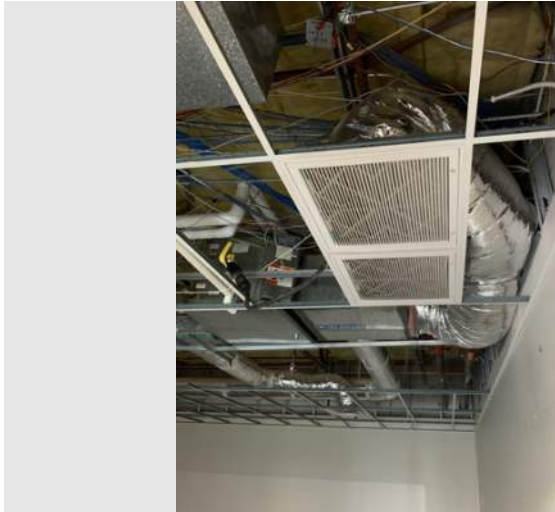

Description

Connected vent filters in B-135

Taken Date

09/14/2023 at 07:17 am

Uploaded By


Cameron Vildosola

Upload Date

09/14/2023 at 08:27 am

File Name

[2A4F342B-4134-4208-A999-9C4F...](#)

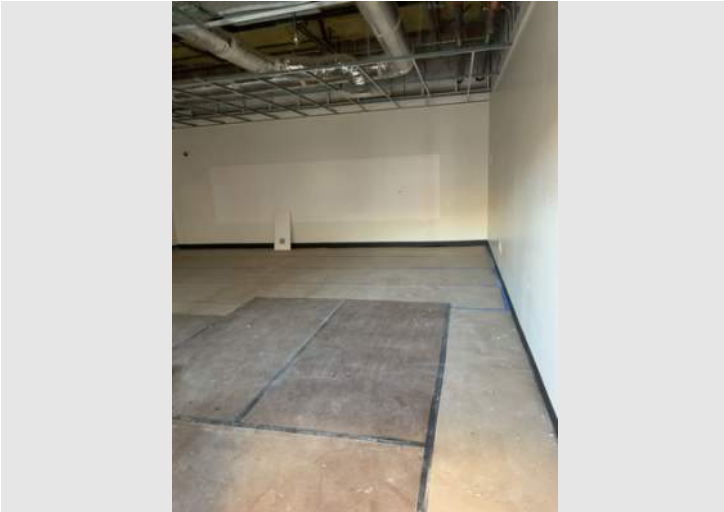

Description

Floor protection in B-135

Taken Date

09/14/2023 at 07:17 am

Uploaded By

Cameron Vildosola

Upload Date

09/14/2023 at 08:27 am

File Name

AC8B7C7E-88F0-4ACE-B81A-44C...



Description

Floor protection and ceiling tile delivery in B-135

Taken Date

09/14/2023 at 07:17 am

Uploaded By


Cameron Vildosola

Upload Date

09/14/2023 at 08:27 am

File Name

C5BD154E-0CAE-495E-A24B-E94...

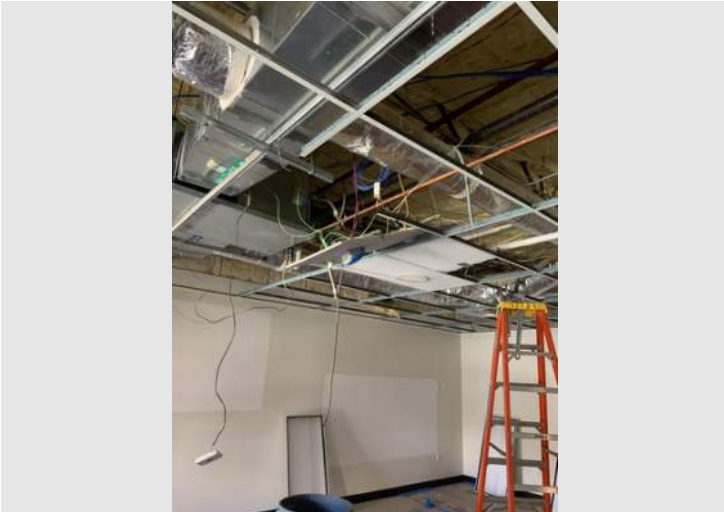

Description



Description

Infant area fence post holes.

Taken Date

09/13/2023 at 12:10 pm

Uploaded By

Cameron Vildosola

Upload Date

09/14/2023 at 08:27 am

File Name

10A57670-A7BA-436C-A1EC-488...

Taken Date

09/12/2023 at 08:01 am

Uploaded By

Cameron Vildosola

Upload Date

09/12/2023 at 08:17 am

File Name

41A78F29-A8C7-4ACF-B43B-865E...



Description

Infant area fence post holes.

Taken Date

09/12/2023 at 08:01 am

Uploaded By

Cameron Vildosola

Upload Date

09/12/2023 at 08:20 am

File Name

[B0DC67FD-1644-4F7A-9FEC-1BA...](#)



Description

Floor protection in place.

Taken Date

09/11/2023 at 01:35 pm

Uploaded By

Carlos Peralta

Upload Date

09/11/2023 at 02:05 pm

File Name

[5030A6FD-CE62-449E-8224-E821...](#)



Description

Floor protection in place.

Taken Date

09/11/2023 at 01:35 pm

Uploaded By


Carlos Peralta

Upload Date

09/11/2023 at 06:53 pm

File Name

[6E07F7E7-9D28-4D12-9E1A-BD4...](#)

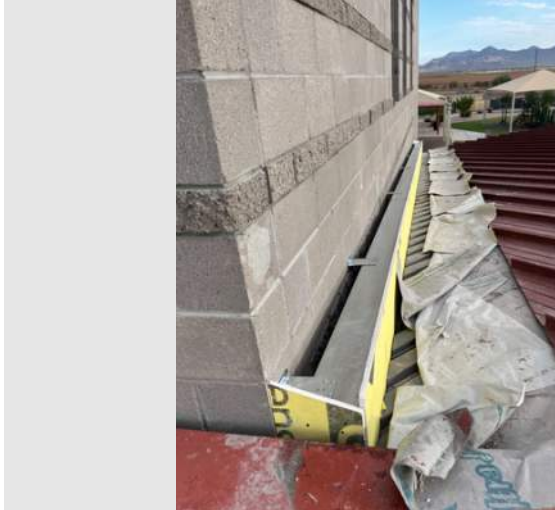

Description

Cricket at existing building framed and rock wood to follow.

Taken Date

09/11/2023 at 07:42 am

Uploaded By

Carlos Peralta

Upload Date

09/11/2023 at 07:45 am

File Name

[5116C6E0-FD4A-4F8E-9112-F2B3...](#)



Description

Taken Date

09/08/2023 at 01:38 pm

Uploaded By


Carlos Peralta

Upload Date

09/08/2023 at 02:12 pm

File Name

[9F18617D-5968-44E1-BFF3-6E13...](#)

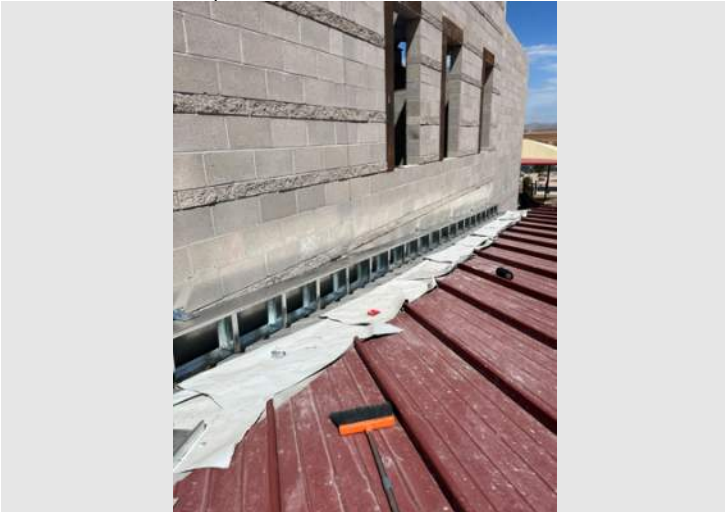

Description

Taken Date

09/08/2023 at 10:47 am

Uploaded By

Carlos Peralta

Upload Date

09/08/2023 at 10:53 am

File Name

[7ECA0E4E-7800-4A02-90C2-8678...](#)



Description

Taken Date

09/08/2023 at 01:38 pm

Uploaded By

Carlos Peralta

Upload Date

09/08/2023 at 02:12 pm

File Name

[AB954E0D-0A06-46D4-A573-B25...](#)



Description

Taken Date

09/08/2023 at 10:47 am

Uploaded By

Carlos Peralta

Upload Date

09/08/2023 at 10:53 am

File Name

[27F3AC7C-970A-48AE-9D09-6C6...](#)



Description

Aerial view Mechanical Yard.

Taken Date

09/07/2023 at 01:41 pm

Uploaded By


Saen Framjee

Upload Date

09/12/2023 at 10:29 am

File Name

[50C2C651-2A38-423E-AAFF-290E...](#)

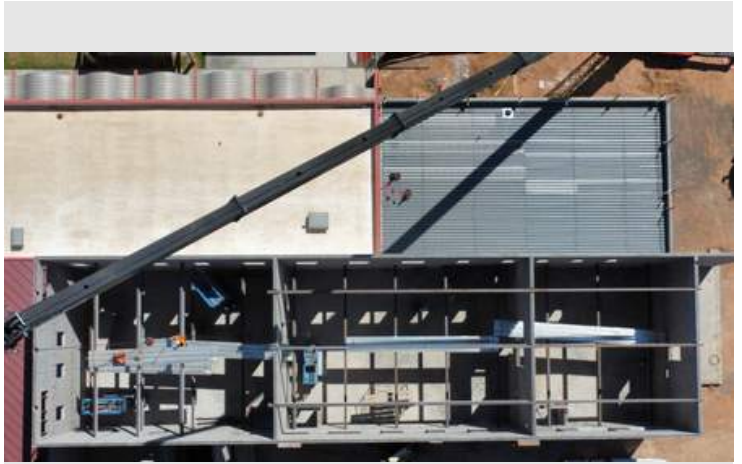

Description

Aerial view bldg.B

Taken Date

09/07/2023 at 01:40 pm

Uploaded By

Saen Framjee

Upload Date

09/12/2023 at 10:29 am

File Name

[C28EEE4E-41AE-484D-8EA4-440...](#)



Description

Aerial view bldg.B

Taken Date

09/07/2023 at 01:40 pm

Uploaded By

Saen Framjee

Upload Date

09/12/2023 at 10:29 am

File Name

[59D8D89A-87F2-44E2-8907-2FD...](#)



Description

Aerial view bldg.B

Taken Date

09/07/2023 at 01:38 pm

Uploaded By

Saen Framjee

Upload Date

09/12/2023 at 10:29 am

File Name

[55955519-7339-466F-B732-AB64...](#)



Description

Aerial view bldg.B

Taken Date

09/07/2023 at 01:37 pm

Uploaded By

Saen Framjee

Upload Date

09/12/2023 at 10:29 am

File Name

[106887F5-C49F-4675-9D27-C1D...](#)



Description

Aerial view bldg.B

Taken Date

09/07/2023 at 01:36 pm

Uploaded By


Saen Framjee

Upload Date

09/12/2023 at 10:29 am

File Name

[7CABD274-E327-4746-B00E-77C...](#)

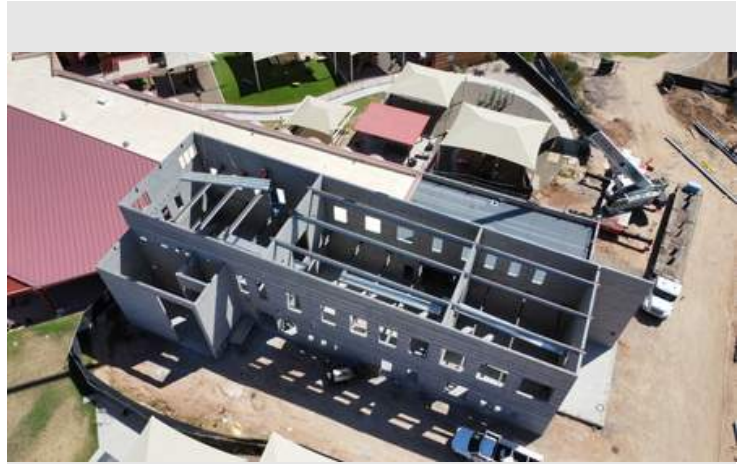

Description

Aerial view bldg.B

Taken Date

09/07/2023 at 01:37 pm

Uploaded By


Saen Framjee

Upload Date

09/12/2023 at 10:29 am

File Name

[7BCD9F2C-E7E1-49B2-830A-1A3...](#)

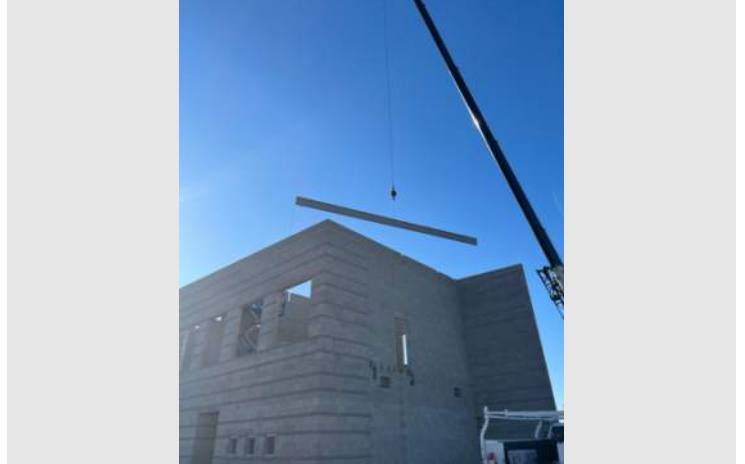

Description

Taken Date

09/07/2023 at 07:53 am

Uploaded By

Carlos Peralta

Upload Date

09/07/2023 at 08:23 am

File Name

[D5FD7219-B1CD-45D6-9264-604...](#)



Description

Taken Date

09/06/2023 at 03:18 pm

Uploaded By

Carlos Peralta

Upload Date

09/06/2023 at 08:30 pm

File Name

[CBEA7219-F59F-4793-A69F-A452...](#)



Description

Taken Date

09/06/2023 at 03:17 pm

Uploaded By


Carlos Peralta

Upload Date

09/06/2023 at 08:30 pm

File Name

[2A289704-DB68-4240-AEA6-E3C...](#)

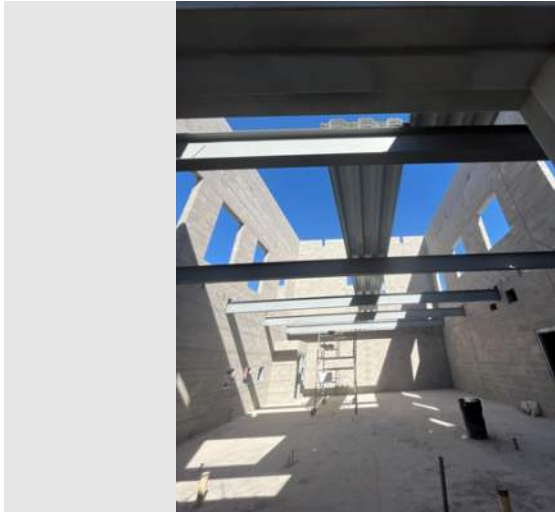

Description

Taken Date

09/06/2023 at 03:17 pm

Uploaded By

Carlos Peralta

Upload Date

09/06/2023 at 08:30 pm

File Name

[F0E8BDDA-63D5-48A9-BA9A-5B6...](#)



Description

W&W Crane on site.

Taken Date

09/06/2023 at 08:29 am

Uploaded By

Carlos Peralta

Upload Date

09/06/2023 at 03:04 pm

File Name

[0B69D79B-0E9D-429C-B812-A13...](#)



Description

Mechanical yard top out ready for grout.

Taken Date

09/06/2023 at 08:29 am

Uploaded By

Carlos Peralta

Upload Date

09/06/2023 at 03:04 pm

File Name

[DAA7B63F-6E8E-43A9-942A-DEE...](#)

SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Attachments:

Item/s
1. None
