



# Salt River Pima-Maricopa Indian Community

10005 East Osborn Road • Scottsdale, Arizona 85256

Phone (480) 362-7700 • Fax (480) 362-5597

## MONTHLY PROJECT PROGRESS UPDATE

**Project:** ECEC Classroom and Parking Expansion

**Issued Date:** June 5, 2023 | **June-2023 UPDATE**

**Distribution:**

	Name	Department/ Company
X	Tami Brungard	ECEC – Edu Leader
X	Lekisha Morris	ECEC
X	Barbara White	ECEC
X	Melody Herne	Act. Superintendent
X	Tate Walker	Public Relations Dir.
X	Deanna Scabby	Edu. Board./ Council
X	Mikah Carlos	Community Council

	Name	Department/ Company
X	Kimberly Manuel	ECEC – Policy Council
X	Carmen Briones	ECEC – Policy Council
X	Jennifer Correa	ECEC – Policy Council
X	Brittany Barranca	ECEC – Policy Council
X	Frank Perez	ECEC – Policy Council
X	Rene Uriarte	ECEC – Policy Council
X	Symone Kann	ECEC – Policy Council
X	Felicia Toya	ECEC – Policy Council

## Work Completed:

### Items



1. Building B Addition concrete footings poured and masonry stem wall installed.
2. CONEX storage container removed, (4) classrooms emptied for start of renovations.
3. Parking lot light bases and conduit installed.
4. Final grading and stone base at parking completed.
5. Building under slab utilities installed and stone base placed.
6. Last (2) exterior restroom renovations completed.

## Work anticipated in the next month:

1. Parking lot asphalt pavement.
2. Building B Addition 1<sup>st</sup> floor concrete slab.
3. Building B Addition CMU vertical walls.
4. Perimeter fencing install start.
5. Central Plant mechanical yard construction start (site, footings CMU walls).
6. Classroom renovations are pending material delivery, tentative start 7/19.

SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Project Schedule | Three Week Look Ahead

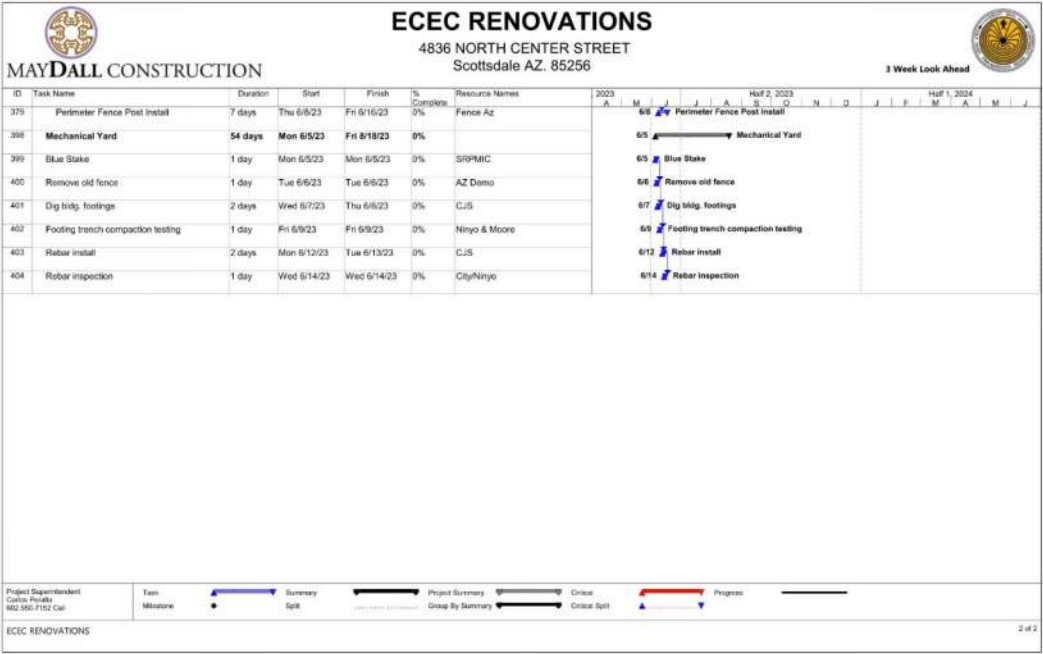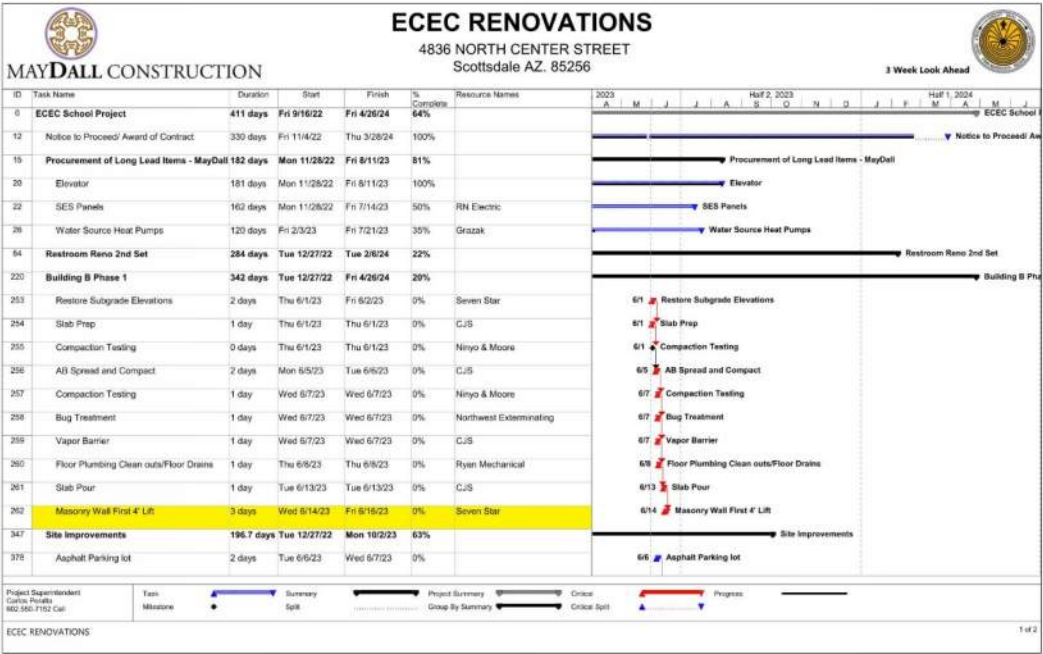

# SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Progress Photos:

---

See attached.



Description

**Taken Date**

06/02/2023 at 12:15 pm

**Uploaded By**

Saen Framjee

**Upload Date**

06/02/2023 at 01:31 pm

**File Name**

[DEBF2E43-AE0A-407E-A7FE-CFE1...](#)



Description

**Taken Date**

06/02/2023 at 12:14 pm

**Uploaded By**

Saen Framjee

**Upload Date**

06/02/2023 at 01:31 pm

**File Name**

[8625FBC7-5D4D-48C4-908B-C9A...](#)



Description

**Taken Date**

06/02/2023 at 12:15 pm

**Uploaded By**

Saen Framjee

**Upload Date**

06/02/2023 at 01:31 pm

**File Name**

[77B8A6C2-48B9-4326-988C-794...](#)



Description

**Taken Date**

06/02/2023 at 12:14 pm

**Uploaded By**

Saen Framjee

**Upload Date**

06/02/2023 at 01:31 pm

**File Name**

[F07E8C6B-F274-41C9-AB69-0CE5...](#)





**Description**

**Taken Date**

06/02/2023 at 06:44 am

**Uploaded By**

Carlos Peralta

**Upload Date**

06/02/2023 at 06:46 am

**File Name**

[3B1B0796-FE5F-4BEB-A382-D62...](#)



**Description**

AB Bldg.. B Compaction to follow.

**Taken Date**

06/01/2023 at 06:37 am

**Uploaded By**


Carlos Peralta

**Upload Date**

06/01/2023 at 06:50 am

**File Name**

[37064989-869F-411C-9A0F-A67C...](#)

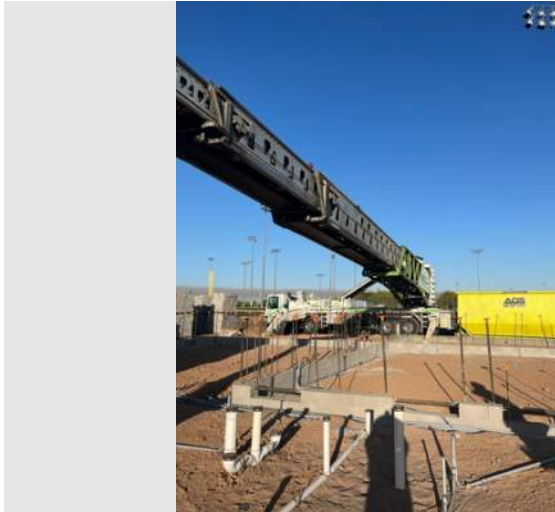

**Description**

Conveyer belt Spreading AB bldg.B

**Taken Date**

06/01/2023 at 06:37 am

**Uploaded By**


Carlos Peralta

**Upload Date**

06/01/2023 at 06:44 am

**File Name**

[18606E2A-2B5F-4798-96E6-C15A...](#)

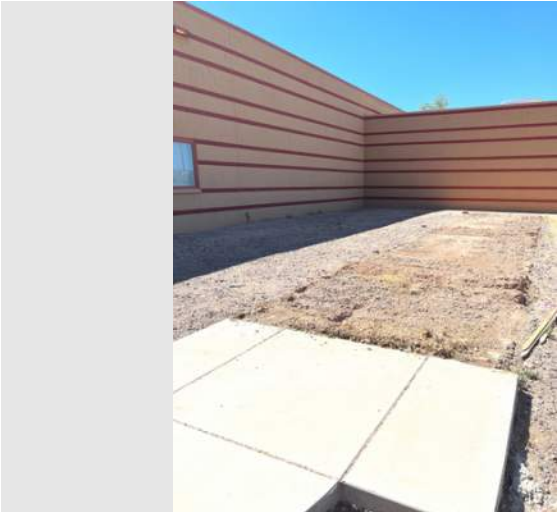

**Description**

New Cooling tower Location.

**Taken Date**

05/31/2023 at 09:38 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/31/2023 at 09:39 am

**File Name**

[8EDEBD5B-3634-42A9-BF49-CA9...](#)



**Description**

Curb elevations per surveyors.

**Taken Date**

05/25/2023 at 02:00 pm

**Uploaded By**


Carlos Peralta

**Upload Date**

05/25/2023 at 02:08 pm

**File Name**

[AEB50365-8A3B-4908-9DF8-9EE...](#)

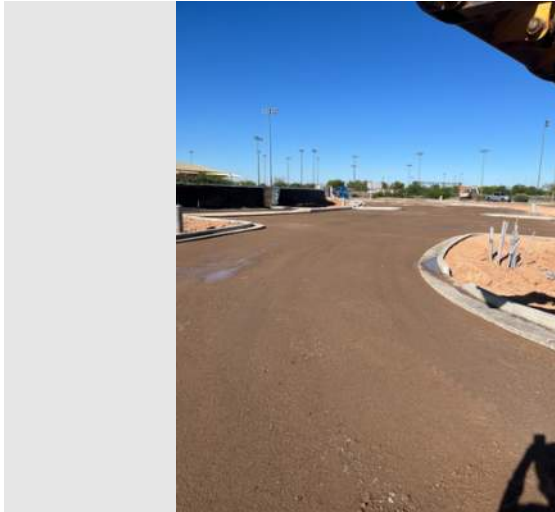

**Description**

Parking lot ready for asphalt.

**Taken Date**

05/30/2023 at 07:59 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/30/2023 at 11:38 am

**File Name**

[7EA5D1B1-F34B-423D-AFC5-A09...](#)



**Description**

West side entry curb and gutter.

**Taken Date**

05/25/2023 at 02:00 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

05/25/2023 at 02:08 pm

**File Name**

[C91C99A5-FBA2-4C66-9446-C7C...](#)



**Description**

Surveyors elevations for curb and gutter. East side.

**Taken Date**

05/25/2023 at 01:59 pm

**Uploaded By**


Carlos Peralta

**Upload Date**

05/25/2023 at 02:08 pm

**File Name**

[CD52CBF2-B16C-4388-B9B6-22B...](#)

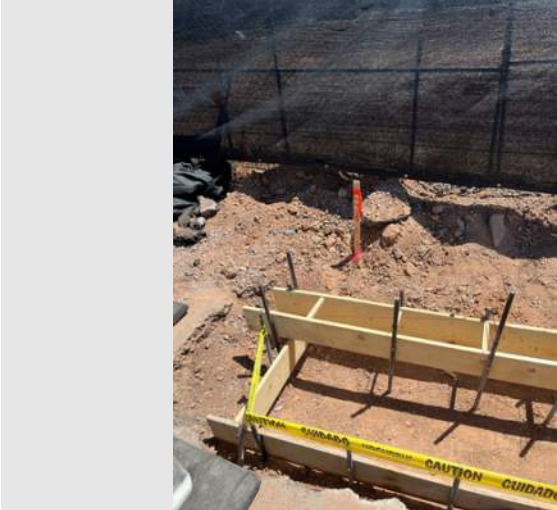

**Description**

Curb and Gutter form and ready for concrete pour.

**Taken Date**

05/25/2023 at 01:59 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

05/25/2023 at 02:08 pm

**File Name**

[E2B47262-E10C-48EA-B0A4-E3D...](#)



**Description**

Curb and Gutter on the east side.

**Taken Date**

05/25/2023 at 01:59 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

05/25/2023 at 02:08 pm

**File Name**

[6124E0D8-6847-4DDB-86BE-B41...](#)



**Description**

Elevations per surveyors. Curb and gutter.

**Taken Date**

05/25/2023 at 01:58 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

05/25/2023 at 02:08 pm

**File Name**

[C327CF7D-9F35-4A4E-84F0-7CD...](#)





**Description**

Canal street entry wings form and ready for concrete pour.

**Taken Date**

05/25/2023 at 01:58 pm

**Uploaded By**


Carlos Peralta

**Upload Date**

05/25/2023 at 02:08 pm

**File Name**

E1F95DAA-F8E9-4FE5-B7EC-E726...

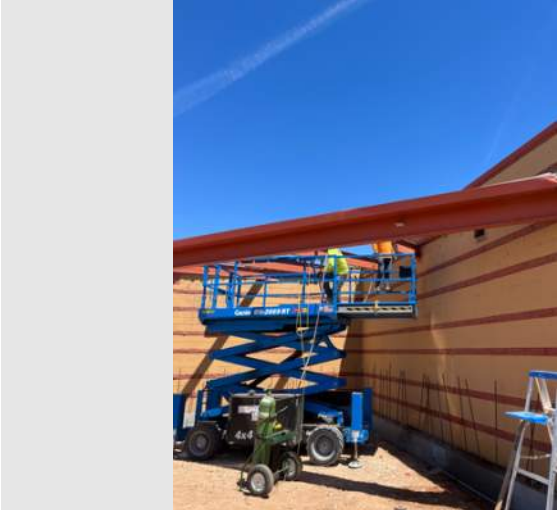

**Description**

Canopy demo in progress .

**Taken Date**

05/25/2023 at 01:50 pm

**Uploaded By**


Carlos Peralta

**Upload Date**

05/25/2023 at 02:08 pm

**File Name**

731CE249-088E-436B-AFC2-8B10...

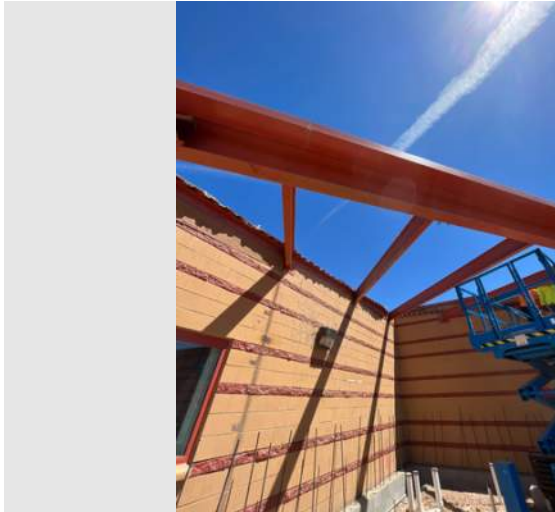

**Description**

Canopy deck removed beams to follow.

**Taken Date**

05/25/2023 at 01:50 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

05/25/2023 at 02:08 pm

**File Name**

9B6A23A8-BA99-4152-835F-4D1...



**Description**

Mountain of dirt removed from main retention

**Taken Date**

05/25/2023 at 08:05 am

**Uploaded By**

Carlos Peralta


**Upload Date**

05/25/2023 at 08:33 am

**File Name**

77889FA6-7F20-49B3-B14D-5A73...



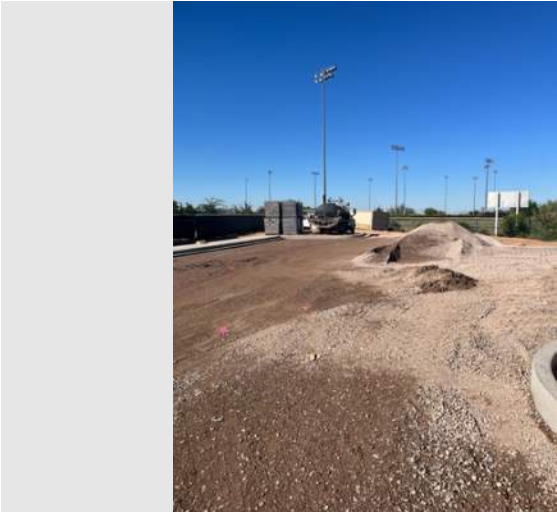

**Description**

AB Deliveries continue Parking lot.

**Taken Date**

05/25/2023 at 08:05 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/25/2023 at 08:31 am

**File Name**

66ACF7E5-4FFF-4455-9885-0864...



**Description**

Gridding continues

**Taken Date**

05/25/2023 at 08:05 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/25/2023 at 08:31 am

**File Name**

D9E8F6E9-5B42-462C-B47A-EBD...



**Description**

Rolling AB and ready for compactio.

**Taken Date**

05/25/2023 at 08:05 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/25/2023 at 08:31 am

**File Name**

ED4E7A97-F585-4878-9B17-9155...



**Description**

Shane grading AB lay down in progress Parking lot.

**Taken Date**

05/22/2023 at 08:08 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/22/2023 at 08:30 am

**File Name**

1CEAE011-30DA-4150-87DB-7A4...



**Description**

Underground electrical at electric Room.

**Taken Date**

05/22/2023 at 07:12 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/22/2023 at 07:48 am

**File Name**

47FFBF89-A3B2-429E-9890-6814...



**Description**

Undergrounds electrical install complete inspection on weds.

**Taken Date**

05/22/2023 at 07:11 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/22/2023 at 07:43 am

**File Name**

E3D26521-A29A-4769-8DA3-D7A...



**Description**

Underground electrical At offices B164 B163

**Taken Date**

05/22/2023 at 07:11 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/22/2023 at 07:48 am

**File Name**

3ACC6C53-DADA-4EAE-BE59-ECF...



**Description**

**Taken Date**

05/18/2023 at 10:23 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/22/2023 at 07:32 am

**File Name**

369C0704-7101-4FBF-B43D-37B2...



**Description**

**Taken Date**

05/18/2023 at 10:23 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/22/2023 at 07:30 am

**File Name**

[224EB7DC-5C4A-4445-8AF2-91E...](#)



**Description**

Traffic Control.

**Taken Date**

05/17/2023 at 07:51 am

**Uploaded By**


Carlos Peralta

**Upload Date**

05/17/2023 at 11:30 am

**File Name**

[EC884155-8F8F-4AF3-9B4D-3D2...](#)

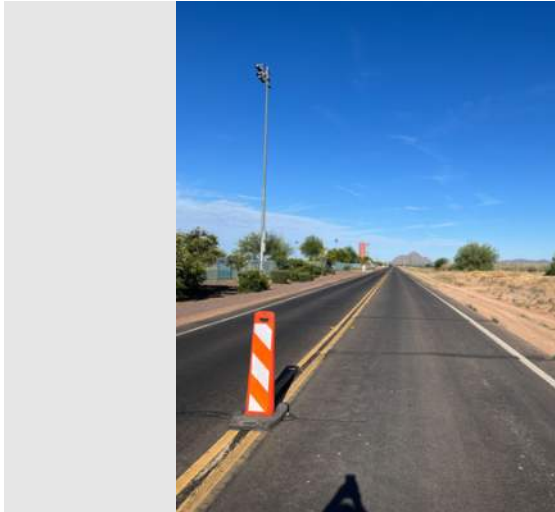

**Description**

Traffic Control.

**Taken Date**

05/17/2023 at 07:51 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/17/2023 at 11:30 am

**File Name**

[19841086-CCF8-4A62-8EB1-C77...](#)



**Description**

Traffic Control.

**Taken Date**

05/17/2023 at 07:49 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/17/2023 at 11:30 am

**File Name**

[E36D98FF-0FEE-4931-B2BC-1FD2...](#)





**Description**

Traffic Control Canal Street

**Taken Date**

05/17/2023 at 07:49 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/17/2023 at 11:30 am

**File Name**

[A8137615-9FA2-4699-9E5A-C4B8...](#)



**Description**

Block stocking in progress.

**Taken Date**

05/15/2023 at 07:43 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/15/2023 at 07:44 am

**File Name**

[491939B9-B272-41FE-AD5A-C18F...](#)



**Description**

Stem wall in progress.

**Taken Date**

05/15/2023 at 11:06 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/15/2023 at 11:06 am

**File Name**

[CB367AEE-5B83-4338-A723-B99...](#)



**Description**

**Taken Date**

05/12/2023 at 12:44 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

05/12/2023 at 01:46 pm

**File Name**

[0C56A47A-9065-4EFF-B530-56D3...](#)





**Description**

Bathroom accessories install complete.

**Taken Date**

05/12/2023 at 12:43 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

05/12/2023 at 12:48 pm

**File Name**

[37CC83AC-611D-4614-BF14-C83...](#)



**Description**

D-112 bathrooms behind Excysting mechanical yard

**Taken Date**

05/11/2023 at 11:32 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/11/2023 at 12:06 pm

**File Name**

[WIN\\_20230511\\_11\\_32\\_22\\_Pro.jpg](#)



**Description**

Elevator shaft walls concrete poured.

**Taken Date**

05/12/2023 at 12:41 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

05/12/2023 at 12:48 pm

**File Name**

[8C2CCF24-F15E-4984-91C2-AFB1...](#)



**Description**

D-115 Women's bathroom

**Taken Date**

05/11/2023 at 11:32 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/11/2023 at 12:06 pm

**File Name**

[WIN\\_20230511\\_11\\_32\\_12\\_Pro.jpg](#)



**Description**

Repair and re- routed 4" water line at the east retention area.

**Taken Date**

05/10/2023 at 11:02 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/10/2023 at 11:24 am

**File Name**

[191341D6-EE02-4813-AABA-A95...](#)



**Description**

Flooring at storage room complete.

**Taken Date**

05/09/2023 at 02:37 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

05/09/2023 at 02:44 pm

**File Name**

[F5BBAD79-F7AE-40C0-804F-1C0...](#)



**Description**

4" line reconnected on the southwest corner

**Taken Date**

05/09/2023 at 02:53 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

05/09/2023 at 02:53 pm

**File Name**

[AC1AB9A4-A435-4523-8F2A-102...](#)



**Description**

Existing pipe reconnection in progress landscapers.

**Taken Date**

05/09/2023 at 01:38 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

05/09/2023 at 02:44 pm

**File Name**

[6DA7080B-ED02-4DD4-ACDD-CA...](#)





**Description**

Storage room floor pre in progress before tile install.

**Taken Date**

05/09/2023 at 01:31 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

05/09/2023 at 01:34 pm

**File Name**

[9F4EAE0B-5574-49C4-8B31-2AE9...](#)



**Description**

4" Wire line repairs continue new leak at shovel area.

**Taken Date**

05/09/2023 at 09:54 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/09/2023 at 09:55 am

**File Name**

[3963936B-C586-42A7-A900-2CB...](#)



**Description**

4" wire line landscapers waiting for water shut off before repairing.

**Taken Date**

05/09/2023 at 09:54 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/09/2023 at 10:01 am

**File Name**

[99EBAC64-DBB8-4CF0-8452-AFF...](#)



**Description**

Cut elbow and cap.

**Taken Date**

05/09/2023 at 08:22 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/09/2023 at 08:56 am

**File Name**

[88D78D00-4B28-4B9F-9B61-2A1...](#)



**Description**

Landscaping pipe near the main entrance found and cap Previous GC left.

**Taken Date**

05/09/2023 at 08:22 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/09/2023 at 08:56 am

**File Name**

[2AB651EF-5D25-4794-9CEE-18A...](#)



**Description**

String for electrical wire pull in place

**Taken Date**

05/08/2023 at 11:35 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/08/2023 at 11:42 am

**File Name**

[90D3594B-0BC4-468F-A46C-913...](#)



**Description**

Bathroom repairs complete near dragon fly classroom.

**Taken Date**

05/08/2023 at 01:06 pm

**Uploaded By**


Carlos Peralta

**Upload Date**

05/08/2023 at 01:38 pm

**File Name**

[739FBEE0-9CB5-4A86-A796-057...](#)

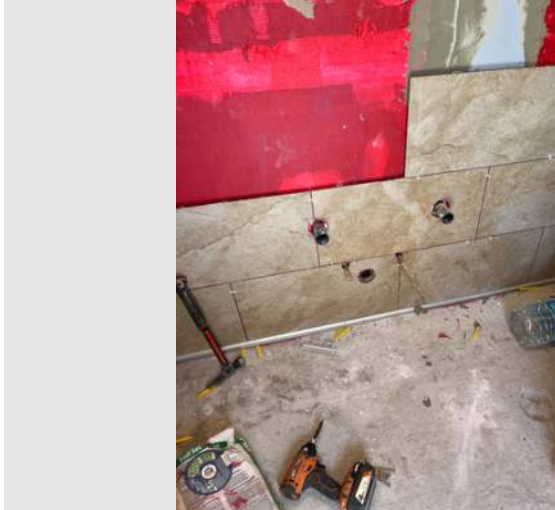

**Description**

Bathroom 134A wall install continues.

**Taken Date**

05/05/2023 at 02:57 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

05/05/2023 at 03:31 pm

**File Name**

[50F865C0-F7B5-4F80-973B-6C0F...](#)





**Description**

Wall tile at bathroom A150 tile crew will continue on Monday.

**Taken Date**

05/05/2023 at 02:57 pm

**Uploaded By**

Carlos Peralta

**Upload Date**

05/05/2023 at 03:31 pm

**File Name**

D3DFC128-AC3B-405E-8034-4A2...



**Description**

Light poles concrete pour complete

**Taken Date**

05/05/2023 at 07:08 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/05/2023 at 07:12 am

**File Name**

40C6C97A-1C88-4C72-AFBF-7FC...



**Description**

Extra dirt needs to be removed from the property Might be able to use in the new play ground.

**Taken Date**

05/05/2023 at 07:08 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/05/2023 at 07:12 am

**File Name**

1C8D72AB-2704-4F15-BE16-486...



**Description**

Delivery of block for bldg.

**Taken Date**

05/05/2023 at 07:07 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/05/2023 at 10:39 am

**File Name**

EE58BFDE-3312-491F-B7F2-E9CD...



**Description**

Light poles electrical complete waiting for city inspection.

**Taken Date**

05/03/2023 at 07:53 am

**Uploaded By**


Carlos Peralta

**Upload Date**

05/03/2023 at 01:26 pm

**File Name**

83601F3B-038E-434C-B967-B976...

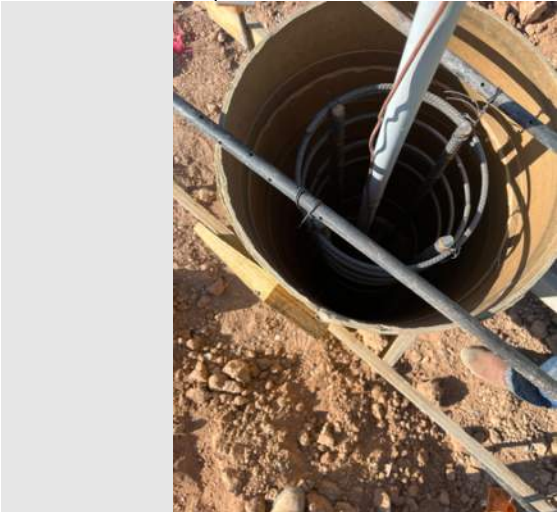

**Description**

Light pole cages ready for concrete pour.

**Taken Date**

05/03/2023 at 07:53 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/03/2023 at 01:26 pm

**File Name**

3D3B4460-C6B8-4BBB-909B-577...



**Description**

Light pole sonic tube in place and we are at 10' deep.

**Taken Date**

05/03/2023 at 07:53 am

**Uploaded By**


Carlos Peralta

**Upload Date**

05/03/2023 at 01:26 pm

**File Name**

998E91AD-550A-4625-8C7D-7E2...

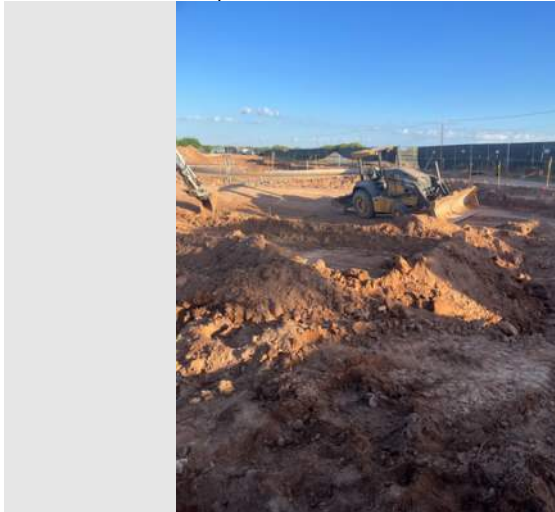

**Description**

Shane grading cutting retention on the East side.

**Taken Date**

05/03/2023 at 06:44 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/03/2023 at 06:53 am

**File Name**

CBB3AA21-569E-4995-AE6F-329...



**Description**

4" Water line Repairs complete at East side by retention.

**Taken Date**

05/03/2023 at 06:44 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/03/2023 at 06:53 am

**File Name**

99197E40-B5AB-49FC-A562-D7F...



**Description**

Swell St south side complete

**Taken Date**

05/01/2023 at 09:40 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/01/2023 at 09:46 am

**File Name**

A1338E65-18E5-42E4-808C-AAE2...



**Description**

Sidewalk on the south side forming in progress

**Taken Date**

05/01/2023 at 09:40 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/01/2023 at 09:46 am

**File Name**

4798353D-3CF9-4439-8C38-ECA...



**Description**

RN Continue on running conduits at light poles.

**Taken Date**

05/01/2023 at 09:39 am

**Uploaded By**

Carlos Peralta

**Upload Date**

05/01/2023 at 09:40 am

**File Name**

19E5AC11-CCE8-4FE3-88D1-7F3...

# SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

**Attachments:**

---

Item/s
1. None
