



Salt River Pima-Maricopa Indian Community

10005 East Osborn Road • Scottsdale, Arizona 85256

Phone (480) 362-7700 • Fax (480) 362-5597

MONTHLY PROJECT PROGRESS UPDATE

Project: ECEC Classroom and Parking Expansion

Issued Date: **March 31, 2023** | **April-2023 UPDATE**

Distribution:

	Name	Department/ Company
X	Tami Brungard	ECEC – Edu Leader
X	Lekisha Morris	ECEC
X	Barbara White	ECEC
X	Melody Herne	Act. Superintendent
X	Tate Walker	Public Relations Dir.
X	Deanna Scabby	Edu. Board./ Council
X	Mikah Carlos	Community Council

	Name	Department/ Company
X	Kimberly Manuel	ECEC – Policy Council
X	Carmen Briones	ECEC – Policy Council
X	Jennifer Correa	ECEC – Policy Council
X	Brittany Barranca	ECEC – Policy Council
X	Frank Perez	ECEC – Policy Council
X	Rene Uriarte	ECEC – Policy Council
X	Symone Kann	ECEC – Policy Council
X	Felicia Toya	ECEC – Policy Council

Work Completed:

Items



1. Site closed for approximately 8 days due to rain and to allow time to dry out.
2. 6" Fire line relocated and pressure tested.
3. 4" Irrigation line relocated.
4. Flooded excavations cleaned out and prepped, rebar reinstalled.

Work anticipated in the next month:

1. Existing floor saw cut and tie-in to existing sanitary line.
2. Concrete footing final preparation pour.
3. Electrical site rough-in for site lighting.
4. Site work including concrete curbs, drive and parking base and asphalt.
5. Masonry stem wall to start.
6. Under slab utility install, (sanitary & electric).
7. 1st Floor concrete slab pour.
8. Classroom renovations are pending material delivery, new heat pumps are currently 16 weeks out for delivery.

SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Project Schedule | Three Week Look Ahead

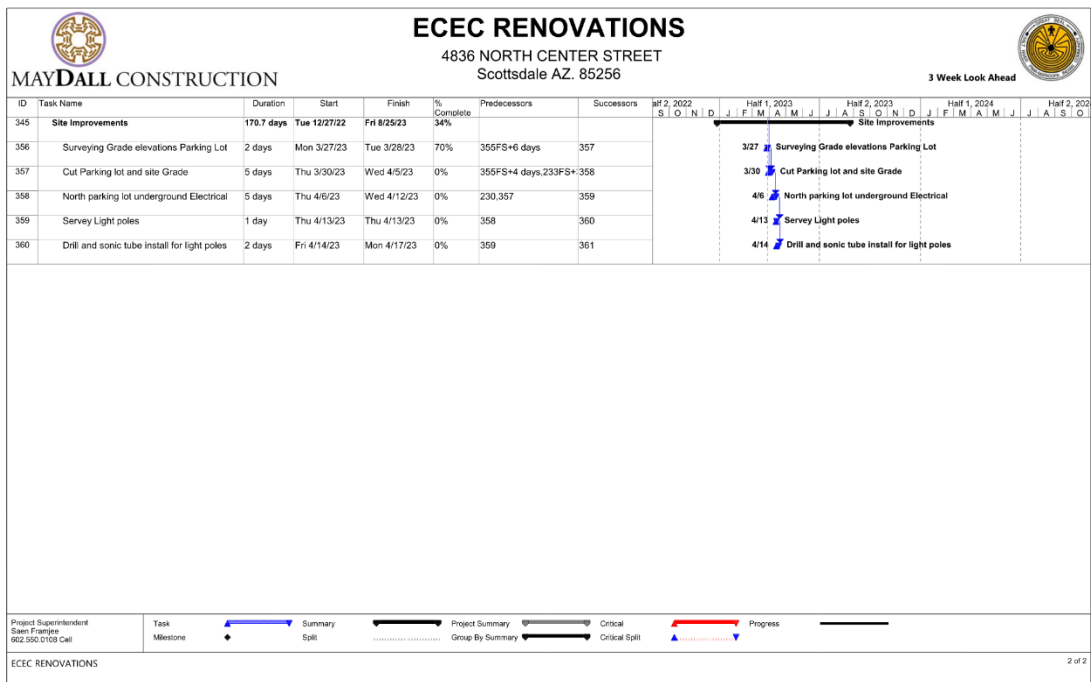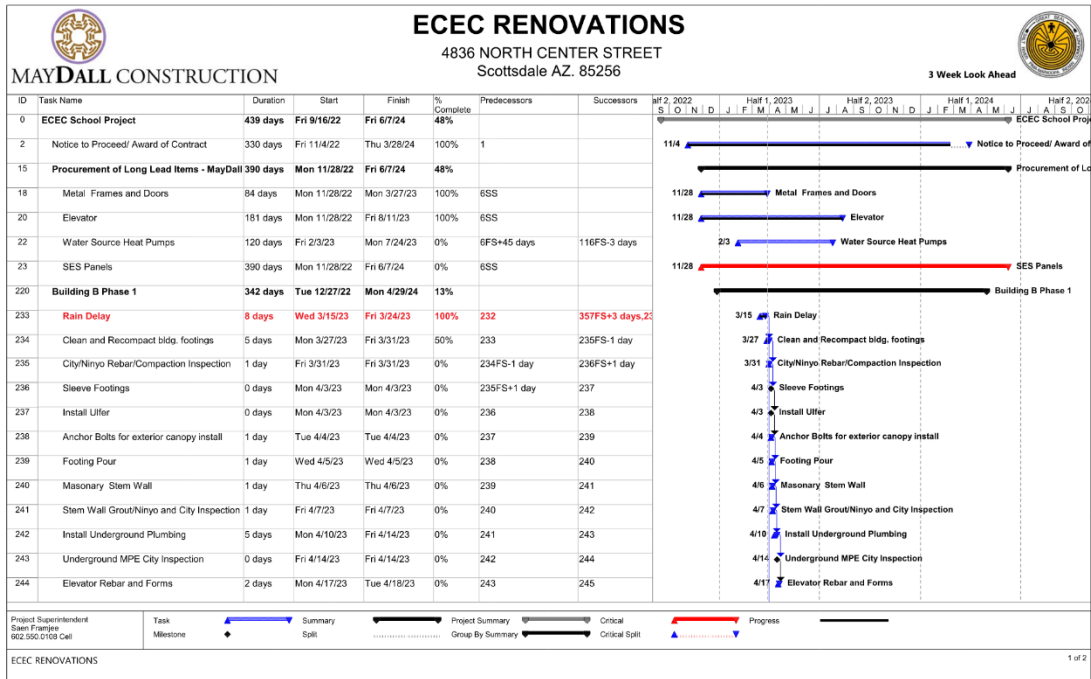


SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Progress Photos:



Aerial – Building B Footings

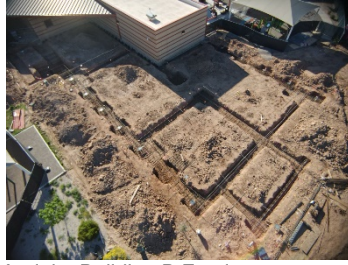


Aerial – Building B Footings



Aerial – Parking & Retention



Flooded Footing




Flooded Footing




Flooded Elevator Pit



6" Fire Line Connection



Fire Line Pressure Test



Relocated Fire Line



Relocated 4" Irrigation Line



Sanitary Line Location



Column Footing Rebar



Elevator Pit Rebar



Footing Rebar



Footing Rebar

SRP-MIC MONTHLY PROJECT PROGRESS UPDATE

Attachments:

Item/s
1. None
